QIDDIYA DEVELOPMENT COMPANY					
DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00007	REVISION NUMBER:	0D	ISSUED BY:	PMO
DOCUMENT TITLE	MIR FORM	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022

Qiddiya

MATERIAL INSPECTION REQUEST (MIR) FORM

Contractor:	HAIF COMPANY
Project:	QPMO-410-CT-00618- ROAD ACCESS TO RESORT CORE
Contract No.:	QI09043311-VO-0004
Material Inspection Request Number:	QRXM114000-HFC-TEC-MIR-ITS-02-RO5-00002

شركة هيف Haif Company — Freyssinet — HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☐	Quality	☐	Project Controls	☐
Civil/Structural	☑	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

MATERIAL DESCRIPTION

Inspection / Test Location:	INTERIM ROAD MAIN LINE-02		
Material Name:	ITS -VMS, DMV	Quantity:	05 Pcs.
P.O Number		Delivery Note Number:	TTSDN-HAIF-181225-008
Approved Material Transmittal Number: (Aconex document Approval)		Approval Date:	
Inspection Date:	22-Jan-2026	Inspection Start Time:	09:00 AM
ITP:		Checklist:	
Spec's / Dwg. Ref.:	TRAFFIC TECH SECURITY W.L.L	Approved Method Statement Number:	
Attachments:	Test Certificate: ◉ Yes ○ No IFC / Shop Drawings: ○ Yes ◉ No		

DESCRITPTION OF MATERIAL

(Traffic Signals) VMS DMV With Accessories (Qty.-05) for Interim Road Main Line-02

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Are Complete Details Mentioned in P.O and Delivery Note?	◉ YES ○ NO	REMARKS	
Complies with Approved ITPs/Checklists?	◉ YES ○ NO	REMARKS	
Signs of Physcial Damage?	○ YES ◉ NO	REMARKS	
Conforms to Approved Material Submittal?	○ YES ○ NO	REMARKS	

Accepted:	◉
Accepted with Comments:	○
Rejected (See Remarks):	○

REMARKS:					
Name:	Moataz Elkhateeb	Signature:		Date:	22-01-2026

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDIN

Contractor Has complied with Material requirements?	○ YES ○ NO			○ YES ○ NO ○ NA	
Accepted:					○
Accepted with Comments:					✓
Rejected (See Remarks):					○
REMARKS:	@MIR have been submitted after the installation of VMS, therefore the actual dimensions of VMS shall be verified during WIR stage.				
Name:	M. YASIR.	Signature:		Date	22/01/2026

B: Approved with Comments
QI09043311-UPR TBN17&TNS05
Saud Nawab
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

② Final approval is subject to the acceptance of successful completion of Testing and commissioning

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Haif Company / Freyssinet — HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - **Interim Road Access to Resort Core**	**Project Code:** QRXM114000
Location: 00	**Date:** 08-November-2025
Document Title: **Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (Dynamic Message System (DMS))**	**Ref No:** QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00001
	Rev No: 01

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☑ ITS ☐ Civil

Type: ☐ Pre-Qualification ☐ Method Statement ☒ Material Submittal ☐ Sample ☐ Other

Document Description: Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (Dynamic Message System (DMS))

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00001	**Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (Dynamic Message System (DMS))**

Enclosure:

Submitted By:	**Received By:**
Name: **Eng. Moataz** Signature: Date: 08-Nov-2025	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments:

B: Approved with Comments — Zuhair Fayez Partnership Consultants, Riyadh , Saudi Arabia

B: Approved with Comments — Zuhair Fayez Partnership Consultants, Riyadh , Saudi Arabia

Contractor to comply with the following comments prior to procurement.

1. The proposed DMS does not comply with the required depth size. The specification and BOQ indicate dimensions of 2.3 × 2.0 × 0.25m, whereas the proposed unit is 2.3 × 2.0 × 0.159m. Provide supporting documents to justify the proposed size.
2. Visibility range is not indicated in the data sheet. Contractor to provide actual range in compliance with project specifications.
3. IP rating is not mentioned in the DMS data sheet. Contractor to submit a type test report verifying compliance with outdoor installation requirements.
4. The final finish color of the DMS and all exposed units shall be as per project specifications and QIC recommendations.
5. The contractor shall ensure full compliance with the project specifications for DMS software and data storage
6. SASO/SABER certificate to be provided for subject items.
7. Warranty certificate shall be provided in accordance with the project specification.
8. Server and workstation are not included in the subject submittal. A dedicated DMS server is required as indicated in IFC riser diagram and a separate submittal shall be provided submitted.

Below portion for Client use only

Comments:

- Final approval subject to adherence all comments stated on document.

B: Approved with Comments — Zuhair Fayez Partnership Consultants, Riyadh , Saudi Arabia

Signed by: Signature: Date:

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Haif Company / Freyssinet — HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
Location: 00	**Date:** 26-March-2026
Document Title: **Inspection & Test Plan for DMS/VMS**	**Ref No:** QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00002
	Rev No: 00

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☐ Authority ☒ ITS

Type: ☐ Pre-Qualification ☐ Method Statement ☐ Material Submittal ☐ Sample ☒ ITP

Document Description: This is Inspection & Test Plan for for DMS/VMS

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00002	**Inspection & Test Plan for for DMS/VMS**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz Signature: Date: 26-march-2026	Name: Signature:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments: All the work shall be carried out in accordance with project specification







Below portion for Client use only

Comments:

Signed by: Signature: Date:

TRAFFIC TECH
www.traffic-tech.com

تقنيات المرور الأمنية ذ.م.م.
TRAFFIC TECH SECURITY W.L.L.

Date: 18-Dec-2025
Our Ref: TTSDN-Haif-181225-008

Delivery Note

To: HAIF COMPANY
---------- الى:

Ref: WS045CR-53 (RA2RC – ACCESS ROAD TO RESORT CORE)

SN	Model No. رقم الموديل	Description الوصـــــف	Unit الوحـدة	Qty الكميـة	Remarks ملاحظـات
MATERIAL SUPPLY (TRAFFIC SIGNALS)					
1		VMS DMV With Accessories	NOS	05	

Delivered By: EHAB Basla ---------- Date: 18 Dec 2025 ----------
Printed Name & Signature

Received By: ----------
Printed Name & Signature

Haif Contracting
Date
Project. Qiddiya
WS-045CR
Received

Date: 18-12-2025

شركة تقنيات المرور الأمنية ذ.م.م. TRAFFIC TECH Security W.L.L. Co. سجل تجاري ١٠١٠٨٨٢٧٢٢

IMRANmuhammad

3 Nos of Boxes outside
Check
Head to Provide all the Test Result

Unit No. 38, Building 3990
Anas Bin Malik St., Al Malga District
P.O. Box 13524
6615, Riyadh, Saudi Arabia
E-mail : ttg@traffic-tech.com
Web: www.traffic-tech.com

DMV d.o.o., Kraljevića Marka bb, 18000 Niš, Srbija
Tel/fax: +38118 4591 556, 4591 552
Matični broj: 07707665, Šifra delatnosti: 2651
PIB: 100337350, info@dmv.rs, www.dmv.rs

PACKING LIST

Consignee:

Date: 02.12.2025.

Traffic Tech (Gulf) W.L.L

6th Floor, Buzwair Building #53,
Rawdat Al Khail Street #330,
Al Mansoura, Zone 25,
P.O. Box 30704, Doha, Qatar

Ship to:

Traffic Tech Security W.L.L
Building 8, Floor 6,
Olaya Street
P.O. Box 13524
Riyadh, Saudi Arabia

Invoice 1202/250EXP Shipment content:

Packet	**DESCRIPTION:**	**Order No.**	**pcs**	**kg**	**Dimensions(mm)**
1.	Full color matrix sign, **HOUSING DIMENSIONS (VxH) 2000 x 2300 mm**: with parts included: **TRS-RTNMFC-P1V4-80x96+RCC1-ETH-LS-ED-LBED** HS code: 8530 80 0000	***POR-18834***	3	644	2390x620x2250
2.	Full color matrix sign, **HOUSING DIMENSIONS (VxH) 2000 x 2300 mm**: with parts included: **TRS-RTNMFC-P1V4-80x96+RCC1-ETH-LS-ED-LBED** HS code: 8530 80 0000		2	461	2390x440x2250
3.	Road weather station for monitoring road weather conditions **MS-RWC3-VSBR-WACLF** HS CODE: 90159000	***POR-18352***	1	46	900x690x900
				1151	

Total coolly: 3
Total weight: 1151kg

FOR DELIVERY NOTE NUMBER-TTSDN-Haif-181225-008

TRS-RTNMFC-P1V4-80x96+RCC1-ETH-LS-ED-LBED

Factory Acceptance Test

1. Introduction

This document identifies the Factory Acceptance Testing process for the DMS signs
The signs are to be Factory Acceptance Tested in DMV premises in Nis, Serbia. All tests performed in accordance with this specification.


All tests will be performed by competent staff under controlled conditions.

A test checklist with pass/fail parameters is generated for each test. This will be signed by the Client or the Client representative and the supplier and contractor representative on successful completion of each test. Results and Photographs will be added following completion of the FAT and prior to sign-off of the completed test document.

Sign Specification

Sign Reference – TRS-RTNMFC-P1V4-80x96+RCC1-ETH-LS-ED-LBED

External Dimensions of Signs

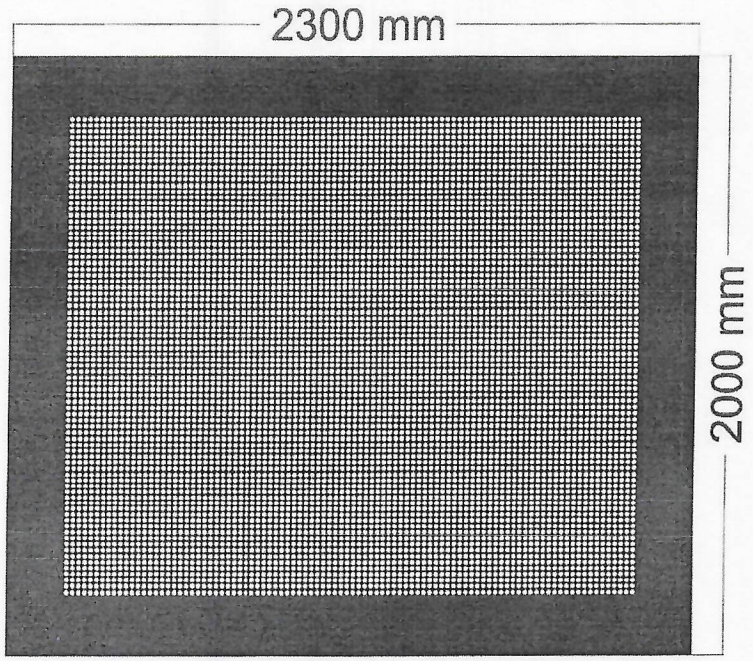

2. Hardware Tests

Overview

Tests will be conducted on one sign.

Test 1 – Dimensional and physical check of the sign

Damage Check

Inspect sign paint and the structure.

Serial Number	Test Criteria	Test Results, pass/fail	Comment
24173001	Are the paint and structure undamaged.	Pass	

Check of seals, doors and openings and integrity of locks and hinges.

Serial Number	Test Criteria	Test Results, pass/fail	Comment
24173001 24173002 24173003 24173004 24173005	• Are seals intact. • Do the doors open and close correctly. • Do the doors seal and lock correctly. • Door fixator check	Pass	

Physical Dimensions

The physical dimensions of the sign will be checked using a standard measuring tape or laser.

Serial Number	Test Criteria	Test Results, pass/fail	Comment
24173001 24173002 24173003 24173004 24173005	Do the measurements meet 2000 mm High x 2300 mm Wide (+/- 10 mm in height and wide)	Pass	

Test 2 Optical characteristics

Overview

The test of optical characteristics must be carried out in two parts.

Because of the equipment required and the conditions imposed by the test, this part of the FAT must be carried out in a controlled environment — namely in the specially outfitted room with specific equipment provided at DMV's test facility in Nis.

This test will measure the Luminous intensity.

The test equipment used is a Konica Minolta Chroma metre CS100A.

Luminosity

Serial Number	Test Criteria	Range	Test Results, pass/fail	Comment
24173001 24173002 24173003 24173004 24173005	Measured luminosity should meet L3 class ie. should be between min max values	White Lmin 12 400 Lmax 37 200	Pass	
24173001 24173002 24173003 -11-		Yellow Lmin 7 440 Lmax 22 320	Pass	
2 -11-		Orange Lmin 4 800 Lmax 14 400	Pass	
-11-		Green Lmin 3 720 Lmax 11 160	Pass	
-11-		Red Lmin 3 100 Lmax 9 300	Pass	
-11-		Blue Lmin 1 240 Lmax 3 720	Pass	

Beam width

Serial Number	Test Criteria	Requirements	Test Results, pass/fail	Comment
24173001 24173002 24173003 24173004 24173005	Measured beam width should meet B6 class, In side angles at -15 and 15 degrees, intensity shouldn't be less than 50% from intensity in 0 axes	Horizontal -15 +15 0	Pass	

Test 3 – Earthing measurements

The test identifies that the necessary earthing protection has been provided.

The test is performed using a gpi-745a electrical safety tester (CE meter) which measures the signs earthing results.

Serial Number	Test Criteria	Result Achieved	Test Results, pass/fail	Comment
24173001	- less than 5 ohms [Ω]	161 mΩ	Pass	

Test 4 – Power Consumption

For the power consumption confirmation test we use the Unimer model PeakTech 2005 and the Current clamp, Model DT266. Unimer measures voltage and the current clamp measures current. Wattage is calculated as the product of both.

The test criteria for power consumption with LEDs at maximum brightness of 100% are:

Maximum consumption (when all LEDs are turn on in white color at maximal brightness): 1200W
Average consumption (when the sign displays realistic scenario- some text or pictogram): between 170- 400W

Serial Number	Test Criteria	Result Achieved	Test Results, pass/fail	Comment
241730001 241730002 241730003 241730004 241730005	Measure maximal power consumption of DMS showing full white and brightness set to 100%	1085W max 250W average	Pass	
-11-	Measure power consumption of DMS showing one pictogram and brightness set to 100%		Pass	
-11-	Measure power consumption of DMS showing text only		Pass	

Test 5 Labelling

Test 5 confirms that the sign is CE marked in compliance with EN 12966:1-2009, and that all warning labels are shown.

Items 1 to 5 below are details of the internal labelling.

1		Protective ground
2		Danger high voltage
3	SN:	Serial number
4	SW:	Software number
5	EA:	Ethernet address

The graphic below is an example of the external sign label.

DMV	DMV industrijski kontrolni sistemi, Kraljevića Marka bb, 18000 Niš, Serbia 25 1304-CPR-0066 M3	CE 1304
Classification acc. EU standard:	EN12966-1:2005 + A1:2009	
Variable message sign installed permanently for the instruction and guidance of road users on public and private land including tunnels		
Product name:	TRS-RTNMFC-P1V4-80x96+RCC1-ETH-LS-ED-LBED	
Product number:	24173001	
Year of production:	2025	
Supply voltage:	230V~, 50Hz, 1200W Max.	
VMS size:	2000 x 2300 x 167mm	
Visual performance:	C2, L3(*), R3, B6	
Uniformity and visible flicker	CCM	
Durability:	T1/T2/T3/T4, IP66, D4	
Impact resistance:	CCM	
Horizontal load:	WL9, DSL4, TDB2, TDT0	

Serial Number	Test Criteria	Result Achieved	Test Results, pass/fail	Comment
24173001 24173002 24173003 24173004 24173005	Check Sign Labels are present and correct.		Pass	

Test 6 DMS functionality

Test 6 confirms that all the DMS functions are working properly.

Serial Number	Test Criteria	Test Results, pass/fail	Comment
2417 3001 2417 3002 2417 3003 2417 3004 2417 3005	Using a lamp, shine a light over the Light Sensor and see if the display reacts accordingly (the display should start increasing the brightness level).	Pass	
-11-	Set the DMS display to full white and check if all the LED-s are working properly.	Pass	
-11-	Remove one LED from the LED board and wait 10 minutes for the detection scan. Check if the DMS is reporting a LED error. (For this test a LED board with an already removed LED should be used).	Pass	
-11-	Remove one LED board from the DMS and wait 10 minutes for the detection scan. Check if the DMS is reporting a LED board error in PC app	Pass	
-11-	Set the fan temperature threshold to be lower than the ambient temperature, wait 10 minutes for the temperature scan. Check whether the fans have been activated.	Pass	

Test 7 Control Center

Test 7 confirms that the DMS functions over the Control Center

Serial Number	Test Criteria	Test Results, pass/fail	Comment
2417 3001 2417 3002 2417 3003 2417 3004 2417 3005	Check whether the device is registered and whether it regularly reports to the server.	Pass	
-11-	Verification of virtual parameters and device type.	Pass	
-11-	RTC technique check	Pass	
-11-	Media Browser technique check	Pass	
-11-	Display technique check	Pass	
-11-	Scenarios technique check	Pass	
-11-	Measurements technique check	Pass	
-11-	LED board error check	Pass	

PARTICIPANTS:

	COMPANY:	SIGNATURE:	DATE:
The Manufacturer:	DMV		09.12.2025.
Supplier:	Traffic Tech		
3rd Party Witness	IMP		9.12.2025.

HAIF-FSA JV Inspection & Test Plan					I &TP	APPROVED DATE	DISCIPLINE
Inteligent Transportation System Works for DMS INSTALLATION AND OPERATION					**HFC-ITP-0080**		ITS
PROJECT TITLE:WBS Access Road To Resort Core (RA2RC)					CONTRACTOR/SUBCONTRACTOR		
WIR No.					CONSTRUCTION-Intelligent Transportation System Works for INSTALLATION AND OPERATION of DMS	HAIF	

ITEM NO.	PROJECT PHASE	TASK / ACTIVITY	Quality Requirements /references/ specifications	Quality Record	INSPECTION RESPONSIBILITY ASSIGNMENTS		REMARKS
					Contractor	Consultant	
1.0 DOCUMENT REVIEW							
1		Material Approval & Shop Drawing	QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00001 QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00001-00086	QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00001 QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00001-00086	R	H	
2.0 MATERIAL RECEIVING INSPECTION							
2		Material receiving inspection, protection & storage	QD0002-ADM-TEM-QMS00007[0A] MaterialReceiving Inspection in site HFC-CKL-4001	QD0002-ADM-TEM-QMS00007[0A] MaterialReceivingInspection in siteHFC-CKL-4001	H	H	MIR to be submitted
3.0 WORK INSTALLATION							
3.1		PRE - INSTALLATION	HFC-CKL-4001	HFC-CKL-4001	H	H	
3.2		INSTALLATION	HFC-CKL-4002	HFC-CKL-4002	H	H	
3.3		TESTING	HFC-CKL-4003	HFC-CKL-4003	H	H	

	GENERAL NOTES
1	Surveillance: QA/QC organization to monitor work in progress without notice from Construction Organization
2	Witness: QA/QC organization shall be notified of the timing of Inspection or test in advance. However, the inspection or test shall be performed as scheduled if the QA/QC organization representative is not present.
3	Hold: QA/QC organization shall be notified of the timing of inspection or test in advance. Inspection or test shall not be carried out without the QA/QC organization representative in attendance.
4	If the Main Contractor delegates the assigned responsibility to the Subcontractor, then the Main Contractor will have the same degree of responsibility as assigned to Consultant.

LEGEND			
H	Hold Point for QC Inspection/ Test	R	Review of Documents
W	Witness Inspection/T	RH	Review & approval of Documents
S	Surveillance		

Checklist : HFC-CKL-4001	Checklist	APPROVED DATE	DISCIPLINE
Material receiving inspection, protection & storage	HFC-CKL-4001		ITS
PROJECT TITLE: Road Access To Resort Core (RA2RC)			CONTRACTOR/SUBCONTRACTOR
WIR No.	CONSTRUCTION- ITS System Works for INSTALLATION AND OPERATION of DMS		HAIF

ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
1.0	**Material receiving inspection,protection &**					
1.1	Deliver ITS Device in packaging, protected, complying with applicable Standard.	project specification SECTION 137730 -DYNAMIC MESSAGE SGN (DMS) SYSTEM				
1.2	Store equipment in a dry location. Protect from weather,fumes, water, debris,direct exposure to the sunlight, ultraviolet,etc	project specification SECTION 137730 -DYNAMIC MESSAGE SGN (DMS) SYSTEM				
1.3	Provide necessary protection if required as per manufacturer's recommendations.	project specification SECTION 137730 -DYNAMIC MESSAGE SGN (DMS) SYSTEM				
1.4	Handle equipment and devices with care, to avoid abrasion, puncturing and tearing housing, paint.	project specification SECTION 137730 -DYNAMIC MESSAGE SGN (DMS) SYSTEM				

Remarks

PM/Contractor			QDC		
Contractor Construction			Third Party (if applicable)		
The work is ready for inspection			Document Reviewed	Work Inspected	Test Records Verified
Name	Signature	Date	Name	Signature	
Faruq					
Contractor QC Inspector			QDC Supervision Consultant		
