QIDDIYA DEVELOPMENT COMPANY					
DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00007	REVISION NUMBER:	0D	ISSUED BY:	PMO
DOCUMENT TITLE	MIR FORM	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022

Qiddiya

MATERIAL INSPECTION REQUEST (MIR) FORM

Contractor:	HAIF COMPANY
Project:	QPMO-410-CT-00618- ROAD ACCESS TO RESORT CORE
Contract No.:	QI09043311-VO-0004
Material Inspection Request Number:	QRXM114000-HFC-TEC-MIR-ITS-02-RO5-00013

Haif Company — Freyssinet — HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☐	Quality	☐	Project Controls	☐
Civil/Structural	☑	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

MATERIAL DESCRIPTION

Inspection / Test Location:	INTERIM ROAD MAIN LINE-02		
Material Name:	Traffic Signal Controller WITH ACCESSORIES	**Quantity:**	2 Nos.
P.O Number		**Delivery Note Number:**	TTSDN-HAIF-280426-21-RO
Approved Material Transmittal Number: (Aconex document Approval)	QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00016	**Approval Date:**	
Inspection Date:	08-Jun-2026	**Inspection Start Time:**	11:00 AM
ITP:		**Checklist:**	
Spec's / Dwg. Ref.:	TRAFFIC TECH SECURITY W.L.L	**Approved Method Statement Number:**	
Attachments:	**Test Certificate:** ◉ Yes ○ No **IFC / Shop Drawings:** ○ Yes ◉ No		

DESCRITPTION OF MATERIAL

Enconolite- Traffic Signal Controllers With Complete Accessories for J2 & J3 (02 Nos.) Interim Road Main Line-02

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Are Complete Details Mentioned in P.O and Delivery Note?	◉ YES ○ NO	REMARKS	
Complies with Approved ITPs/Checklists?	◉ YES ○ NO	REMARKS	
Signs of Physcial Damage?	○ YES ◉ NO	REMARKS	
Conforms to Approved Material Submittal?	○ YES ○ NO	REMARKS	

Accepted:	◉
Accepted with Comments:	○
Rejected (See Remarks):	○

REMARKS:					
Name:	Moataz Elkhateeb	**Signature:**		**Date:**	08-06-2026

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FI

Contractor Has complied with Material requirements?	○ YES ○ NO	?	☑ YES ○ NO ○ NA

B: Approved with Comments
QI09043311-UPR TBN17&TN505
Saud Nawab
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

Accepted:	○
Accepted with Comments:	☑
Rejected (See Remarks):	○

REMARKS:	① Final approval is subject to the successful completion and acceptance of Testing and commissioning. ② Comply with the comments mentioned on attached Supporting documents. ③ Attach approved ITP.				
Name:	M. YASIR.	**Signature:**		**Date**	09/06/2026.

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Haif Company / Freyssinet / HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - **Interim Road Access to Resort Core**	**Project Code:** QRXM114000
Location: 00	**Date:**06-January-2026
Document Title:**Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (**Traffic Signal Controller**)**	**Ref No:** QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00016
	Rev No: 01

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☑ ITS ☐ Civil

Type: ☐ Pre-Qualification ☐ Method Statement ☒ Material Submittal ☐ Sample ☐ Other

Document Description:Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (Traffic Signal Controller)

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00016	**Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L** (Traffic Signal Controller)

Enclosure:

Submitted By:	**Received By:**
Name: **Eng. Moataz**	Name:
Signature:	Signature:
Date:06-January-2026	Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments:

B: Approved with Comments
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

B: Approved with Comments
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

Below portion for Client use only

Comments:

Signed by: Signature: Date:

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Hail Company / Freyssinet / HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
Location: 00	**Date:** 4 -June-2026
Document Title: **Inspection & Test Plan for Inteligent Transportation System Works for TRAFFIC SIGNAL SYSTEM**	**Ref No:** QRXM114000-HFC-TEC-ITP-ITS-00006
	Rev No: 00

Department: ☐ Architectural ☐ Structural ☒ Electrical ☐ Mechanical ☐ Authority ☐ Civil

Type: ☐ Pre-Qualification ☐ Method Statement ☐ Material Submittal ☐ Sample ☒ ITP

Document Description: This is Inspection&Test Plan for Inspection&Test Plan for Inteligent Transportation system Works for TRAFFIC SIGNAL SYSTEM

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-ITP-ITS-00005	**Inspection&Test Plan for Inteligent Transportation system Works for TRAFFIC SIGNAL SYSTEM**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz Signature: Date: 4 -June-2026	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments: All the work shall be carried out inaccordance with project specification, relevant standards & codes and manufacturer recommendations.

A: Approved
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

A: Approved
Saud Nawab
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

A: Approved
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

Below portion for Client use only

Comments:

Signed by: Signature: Date:

HAIF-FSA JV Inspection & Test Plan					I &TP		APPROVED DATE	DISCIPLINE
Inteligent Transportation System Works for TRAFFIC SIGNAL SYSTEM					**HFC-ITP-090**			**ITS**
PROJECT TITLEWBS Access Road To Resort Core (RA2R0)					CONTRACTOR/SUBCONTRACTOR			
WIR No.					CONSTRUCTION- Intelligent Transportation System Works for TRAFFIC SIGNAL SYSTEM		HAIF	

ITEM NO.	PROJECT PHASE	TASK / ACTIVITY	Quality Requirements /references/ specifications	Quality Record	INSPECTION RESPONSIBILITY ASSIGNMENTS			REMARKS
					Contractor	Third Party	Consultant	
1.0 DOCUMENT REVIEW								
1.1		Material Approval & Shop Drawing - Emergency Vehicle Detection System	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0B Section 137780 Emergency Vehicle Detection System IFC Drawings QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000001 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000003	QRXM114000-HFC-TEC-MAT-ITS-02-R05-00009 Material Approval Request for EMERGENCY VEHICLE PREEMPTION SYSTEM Approved SHOP DRAWINGS QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000001 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000003	R		H	
1.2		Material Approval & Shop Drawing - Traffic Signal Controller	SHC 306 Section 12.2.3.1 Traffic Signal Controllers IFC Drawings QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000001 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000003	QRXM114000-HFC-TEC-MAT-ITS-02-R05-00007 Material Approval Request for TRAFFIC SIGNAL CONTROLLER Approved SHOP DRAWINGS: QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000001 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000003	R		H	
1.3		Material Approval & Shop Drawing - Transit Signal Priority System	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0B Section 137750 TRANSIT SIGNAL PRIORITY SYSTEM IFC Drawings QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000001 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000003	QRXM114000-HFC-TEC-MAT-ITS-02-R05-00011 Material Approval Request for TRANSIT SIGNAL PRIORITY SYSTEM Approved SHOP DRAWINGS: QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000001 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000003	R		H	

HAIF-FSA JV Inspection & Test Plan					I &TP		APPROVED DATE	DISCIPLINE ITS
Inteligent Transportation System Works for TRAFFIC SIGNAL SYSTEM					**HFC-ITP-090**			
PROJECT TITLEWBS Access Road To Resort Core (RA2R0)					CONTRACTOR/SUBCONTRACTOR			
WIR No.					CONSTRUCTION- Intelligent Transportation System Works for TRAFFIC SIGNAL SYSTEM		HAIF	

ITEM NO.	PROJECT PHASE	TASK / ACTIVITY	Quality Requirements /references/ specifications	Quality Record	INSPECTION RESPONSIBILITY ASSIGNMENTS			REMARKS
					Contractor	Third Party	Consultant	
1.0 DOCUMENT REVIEW								
1.4		Material Approval & Shop Drawing - Pedestrian Push Button	SHC 306 Section 12.2.3.3 R Pedestrian Push Button IFC Drawings QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000001 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000003	QRXM114000-HFC-TEC-MAT-ITS-02-R05-00013 Material Approval Request for PEDESTRIAN PUSH BUTTON Approved SHOP DRAWINGS: QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000001 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000003	R		H	
1.5		Material Approval & Shop Drawing - Traffic Signal Head	SHC 306 Section 12.2.1.1 Signalization Equipment IFC Drawings QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000001 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000003	QRXM114000-HFC-TEC-MAT-ITS-02-R05-00014 Material Approval Request for TRAFFIC SIGNAL HEAD Approved SHOP DRAWINGS: QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000001 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002 QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000003	R		H	
1.6		Material Approval & Shop Drawing - Traffic Signal Poles and Gantries	SHC 306 Section 12.2.2 Supporting Structure Specifications IFC Drawing QRXP117115-DAH-VORA2R-DWG-GEN-R3-Z00000-5000006	QRXM114000-HFC-TEC-MAT-ITS-02-R05-00015 Material Approval Request for TRAFFIC SIGNAL POLES AND GANTRIES Approved SHOP DRAWINGS: QRXM114000-HFC-DRW-SDW-ITS-02-R05-00019-R02 QRXM114000-HFC-DRW-SDW-ITS-02-R05-00031-R01 QRXM114000-HFC-DRW-SDW-ITS-02-R05-00044-R01	R		H	

HAIF-FSA JV Inspection & Test Plan					I &TP		APPROVED DATE	DISCIPLINE ITS
Inteligent Transportation System Works for TRAFFIC SIGNAL SYSTEM					**HFC-ITP-090**			
PROJECT TITLE:WBS Access Road To Resort Core (RA2RC)					CONTRACTOR/SUBCONTRACTOR			
WIR No.					CONSTRUCTION- Intelligent Transportation System Works for TRAFFIC SIGNAL SYSTEM		HAIF	

ITEM NO.	PROJECT PHASE	TASK / ACTIVITY	Quality Requirements /references/ specifications	Quality Record	INSPECTION RESPONSIBILITY ASSIGNMENTS			REMARKS
					Contractor	Third Party	Consultant	
1.0 DOCUMENT REVIEW								
1.7		Material Approval & Shop Drawing - Vehicle Video Detection System	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0B Section 137714 VEHICLE DETECTION SYSTEM IFC Drawing QRXP117115-DAH-VORA2R-DWG-GEN-R3-Z00000-5000006	QRXM114000-HFC-TEC-MAT-ITS-02-R05-00010 Material Approval Request for VEHICLE VIDEO DETECTION SYSTEM Approved SHOP DRAWINGS: QRXM114000-HFC-DRW-SDW-ITS-02-R05-00019-R02 QRXM114000-HFC-DRW-SDW-ITS-02-R05-00031-R01 QRXM114000-HFC-DRW-SDW-ITS-02-R05-00044-R01	R		H	
2.0 MATERIAL RECEIVING INSPECTION								
2		Material receiving inspection, protection & storage	QD0002-ADM-TEM-QMS00007[0A] MaterialReceiving Inspection in site HFC-CKL-9001	QD0002-ADM-TEM-QMS00007[0A] MaterialReceivingInspection in site HFC-CKL-9001	H		H	MIR to be submitted
3.0 WORK INSTALLATION								
3.1		PRE- INSTALLATION	HFC-CKL-9002	HFC-CKL-9002	H		H	
3.2		INSTALLATION	HFC-CKL-9003	HFC-CKL-9003	H		H	
3.3		TESTING	HFC-CKL-9004	HFC-CKL-9004	H		H	

GENERAL NOTES

1	Surreillance: QA/QC organization to monitor work in progress without notice from Construction Organization
2	Witness: QA/QC organization shall be notified of the timing of Inspection or test in advance. However, the inspection or test shall be performed as scheduled if the QA/QC organization representative is not present
3	Hold: QA/QC organization shall be notified of the timing of inspection or test in advance. Inspection or test shall not be carried out without the QA/QC organization representative in attendance.
4	If the Main Contractor delegates the assigned responsibility to the Subcontractor, then the Main Contractor will have the same degree of responsibility as assigned to Consultant.

LEGEND

H	Hold Point for QC Inspection/ Test	R	Review of Documents
W	Witness Inspection/T	RH	Review & approval of Documents
S	Surveillance		

Checklist : HFC-CKL-9001	Checklist	APPROVED DATE	DISCIPLINE
Material receiving inspection, protection & storage	HFC-CKL-9001		ITS
PROJECT TITLE: Road Access To Resort Core (RA2RC)			CONTRACTOR/SUBCONTRACTOR
WIR No.	CONSTRUCTION- Intelligent Transportation System Works for INSTALLATION AND OPERATION of TRAFFIC SIGNAL SYSTEM		HAIF

ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
1.0	**Material receiving inspection,protection & storage of TRAFFIC SIGNAL SYSTEM**					
A	Deliver, store, and handle products, using means and methods that will prevent damage, deterioration, and loss, including theft and vandalism. Comply with manufacturer's written instructions.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
B	Delivery and Handling:					
1.0	Schedule delivery to minimize long-term storage at Project site and to prevent overcrowding of construction spaces.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
2.0	Coordinate delivery with installation time to ensure minimum holding time for items that are flammable, hazardous, easily damaged, or sensitive to deterioration, theft, and other losses.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
3.0	Deliver products to Project site in an undamaged condition in manufacturer's original sealed container or other packaging system, complete with labels and instructions for handling, storing, unpacking, protecting, and installing.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
4.0	Inspect products on delivery to determine compliance with the Contract Documents and that products are undamaged and properly protected.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
C	Storage:					
1.0	Provide a secure location and enclosure at Project site for storage of materials and equipment.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
2.0	Store products to allow for inspection and measurement of quantity or counting of units.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
3.0	Store materials in a manner that will not endanger Project structure.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
4.0	Store products that are subject to damage by the elements under cover in a weathertight enclosure above ground, with ventilation adequate to prevent condensation and with adequate protection from wind.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
5.0	Protect foam plastic from exposure to sunlight, except to extent necessary for period of installation and concealment.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
6.0	Comply with product manufacturer's written instructions for temperature, humidity, ventilation, and weather-protection requirements for storage.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
7.0	Protect stored products from damage and liquids from freezing.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
8.0	Provide a secure location and enclosure at Project site for storage of materials and equipment by Employer's construction forces. Coordinate location with Employer.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				

Remarks

PM/Contractor			QDC		
Contractor Construction			Third Party (if applicable)		
The work is ready for inspection			Document Reviewed	Work Inspected	Test Records Verified
Name	Signature	Date	Name	Signature	
Michael Stanard Sutton.		08/06/026			
Contractor QC Inspector			QDC Supervision Consultant		

Form Ref. No. Q00002-ADN-TEM-QTY-00003- Rev.0A

(16)

TRAFFIC TECH
www.traffic-tech.com

تقنيات المرور الأمنية ذ.م.م.
TRAFFIC TECH SECURITY W.L.L.

Date: **28-April-2026**
Our Ref: **TTSDN-Haif-280426-21-R0**

Delivery Note

To: **HAIF COMPANY** الى:

Ref: **WS045CR-53 (RA2RC – ACCESS ROAD TO RESORT CORE)**

SN	Part No.	Description الوصف	Unit الوحدة	Qty الكمية	Remarks ملاحظات
MATERIAL SUPPLY (TRAFFIC SIGNALS)					
1	153-0492	Econolite – Traffic Signal Controllers with complete Accessories for J2 & J3	Nos	2	

Delivered By: Mohammad Embabi **Date:** **28 April 2026**

Printed Name & Signature

Received By: **Date:**

Printed Name & Signature

Haif Contracting
Date
Project. Qiddiya
WS-045CR
Received

Building 8, Floor 6
Olaya Street
P.O. Box 13524
Riyadh, Saudi Arabia

E-mail : ttsa@traffic-tech.com
Web: www.traffic-tech.com

Econolite Control Products, Inc.
1250 N. Tustin Avenue
Anaheim, CA 92807
United States
Telephone # (714) 630-3700

ECONOLITE DELIVERY NOTE

Packing slip	ARPK048149
Version	ARPK048149.1
Ship date	4/21/2026
Sales order	S-25720-34A2
Cust P.O.	27345
Job Ref.	
Mode of delivery	Will call pick-up
Terms of delivery	Will Call
Freighted by	Carrier
Customer account	A20260

Ship to:
Traffic Tech Security WLL
Bldg 8, Floor 6, Olaya Street, PO Box 13524
13524 Riyadh
SAU

Bill to:
PTV MENA REGION DMCC
PO BOX 309012
Dubai
Dubai
Dubai
ARE

Mark packages: CONTACT AIREEN CANEDA
PTV TO SCHEDULE PICKUP

Item number	Description	Ordered	Unit	Delivered	Remaining quantity
CAB18996	P44, NAT-OUT/IN, TS2-1 PNG, 16H, BM, 220VAC CAB Quantity :2Serial number :	2.00	EA	2.00	0.00
Line notes: 151-3662	CONTACT PTV TO SCHEDULE PICK UP NEMA MALFUNCTION MANAGEMENT UNIT PAIRS W/151-3663 TO COMPLETE UNIT Quantity :2Serial number:	2.00	EA	2.00	0.00
151-3663	NEMA LOAD SENSOR UNIT(LSU) PAIRS W/151-3662 TO COMPLETE UNIT Quantity :2Serial number:	2.00	EA	2.00	0.00
1084-028	PWR SUP,12VDC,5 AMPS,220VAC, EDI MODEL PS250-E-225 Quantity :2Serial number:	2.00	EA	2.00	0.00
40691P220	FLASH TRANSFER RELAY, 220VAC Quantity :12Serial number:	12.00	EA	12.00	0.00
37006P220	LOAD SWITCH, 220VAC INPUT LED IND, EDI 510-25 Quantity :32Serial number:	32.00	EA	32.00	0.00
44623P5	FLASHER, 2 CKT 15A SOLID STATE W/INDICATORS, EDI 810 Quantity :2Serial number:	2.00	EA	2.00	0.00
Line notes: COBG42100000000000	This item replaces a discontinued 44623P220 flasher.. COBALT G-SERIES 220 VAC TS1/TS2-2 SM EOS 8MB DATAKEY NO COMM Quantity :1Serial number: 281371/H43627 Quantity :1Serial number: 281371/H43628	2.00	EA	2.00	0.00
153-0492	MONITOR, SWITCH, TS-2, TWO CHANNEL Quantity :8Serial number:	8.00	EA	8.00	0.00

Shipping Terms

FREIGHT CHARGES IF APPLICABLE ARE DETERMINED ON THE DAY OF SHIPPING IMPORTANT: F.O.B. point of shipment. Shipper's responsibility ceases F.O.B. point of shipment. Check packing list at once, notify carrier immediately if shortage or damage is discovered and note on carrier's delivery slip. Claims must be reported to carrier within 48 hours. Returned goods will not be accepted by shipper except by prior written agreement. Any claims

ECONOLITE

SALES ORDER: S-25720-34A2-08 **SERIAL NUMBER:** H 43627

CONTROLLER COBG42100000000000 **Top Assy Cobalt Controller**

TESTED BY: **Alicia Quezada** Location: Anaheim VOLTAGE: 110V

TEST DATE: **03-11-2026** TR #: 220V ●

OPERATING SOFTWARE **03.02.32**

Mac Address 0 **00:04:81:0A:1C:6E**

Mac Address 1 **00:04:81:0A:1C:6F**

Data Base **L3000**

PART NUMBER	Revision	DESCRIPTION	SERIAL NUMBER
140-0000-503	B	ASSY,COBALT,TS2-TYPE 2	H 43627 260301523
140-1012-004	C	FRONT PANEL,TS2-TYPE 1,COBALT	H 43627 260301524
119-1032-501	U	ASSY, PCB, ENGINE BOARD	H 43627 260301525
140-1000-501	W	ASSY,PCB,NEMA ATC,HOST BOARD	H 43627 260301526
140-1001-501	F	ASSY, PCB, MINI MOTHER BOARD	H 43627 260301527
140-1002-501	R	ASSY, PCB, NEMA ATC, POWER	H 43627 260301528
140-1004-502	NC	ASSY, PCB, ATC AGC,COBALT	H 43627 260301529
32913P4	NC	KEY, 8MB MEMORY, BLUE	H 43627 260301530

INSPECTED BY BG ECPI 12 QC INSP Ilyas Khalak / Bertha Garcia / Arnel Isaac DATE 03-11-2026

Printed copies are for reference only.
Only the electronic file of this document is stored and controlled and the Econolite Intranet is the master.

DATE: 03-11-2026 PAGE: 1


MODEL : ATC ENGINE BOARD/1C/COBALT TEST COUNT: 0

SERIAL NUMBER: H43627 >>>>> BENCH SINGLE FINAL <<<<<

IP: COM4 TEMP: 25.0 C <> 115.0 VAC <> LOOP COUNT: 1

TEST FOR	STATUS	DETAILS	TIME STAMP
SP8/Port2	PASSED	N/A	06:25:04
SP3S/Port1	PASSED	N/A	06:25:07
DATAKEY	PASSED	N/A	06:25:35
FLASH	PASSED	N/A	06:26:46
SRAM	PASSED	N/A	06:26:54
DRAM	PASSED	N/A	06:27:51
EEPROM	PASSED	N/A	06:27:55
ReadMAC 0	PASSED	00:04:81:0A:1C:6E	06:28:06
ReadMAC 1	PASSED	00:04:81:0A:1C:6F	06:28:18
USB 1	PASSED	N/A	06:28:21
USB 2	PASSED	N/A	06:28:24
SDCARD	PASSED	N/A	06:28:27
DISPLAY	VISUAL	N/A	06:30:29
ETH1 - 1	PASSED	N/A	06:30:57
ETH1 - 2	PASSED	N/A	06:31:26
ETH2 - 1	PASSED	N/A	06:32:05
ETH2 - 2	PASSED	N/A	06:32:33
NEMA IO	PASSED	N/A	06:32:45
SPEAKER	AUDIO	N/A	06:32:56
LED	VISUAL	N/A	06:33:02

*** TEST PASSED ***

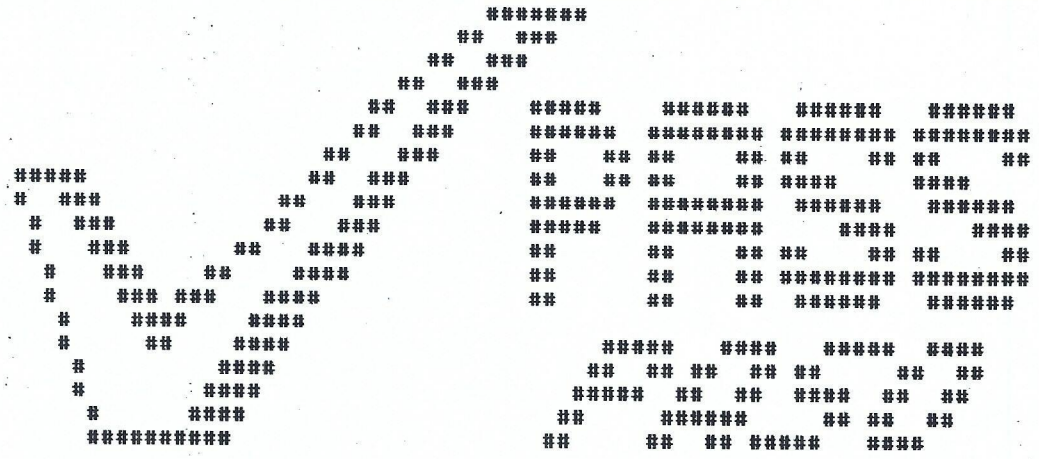

Tested By: Alicia Quezada

Form 0001-20150706 Rev. A

DATE: 03-11-2026 TIME: 07:09:08 PAGE: 1


MODEL : ATC ENGINE BOARD/1C/COBALT

CONTROLLER TYPE: COBALT SHELF MOUNT 2100 DETECTED: COBALT SHELF MOUNT 2100

MAC ID(S): 00:04:81:0A:1C:6E <> 00:04:81:0A:1C:6F

CONTROLLER FIRMWARE		RELEASED FIRMWARE		STATUS
EB U-BOOT	05.06.00	EB U-BOOT	05.06.00	OK
EB OS	06.18.00	EB OS	06.18.00	OK
EB MICRO	07.08.00	EB MICRO	07.08.00	OK
EB USB MICRO	27.01.00	EB USB MICRO	27.01.00	OK
HB PIO MICRO	10.04.00	HB PIO MICRO	10.04.00	OK
HB BGC MICRO	09.08.00	HB BGC MICRO	09.08.00	OK
HB BGR MICRO	18.04.00	HB BGR MICRO	18.04.00	OK
NPS MICRO	11.04.00	NPS MICRO	11.04.00	OK
AGC U-BOOT	12.01.00	AGC U-BOOT	12.01.00	OK
AGC OS	13.15.00	AGC OS	13.15.00	OK
TRAFFIC APP	03.02.32	TRAFFIC APP	03.02.32	OK
AGC APP	03.02.32	AGC APP	03.02.32	OK
DATABASE	L3000/NONE	DATABASE	L3000/NONE	OK

VERSION VERIFICATION: P A S S E D

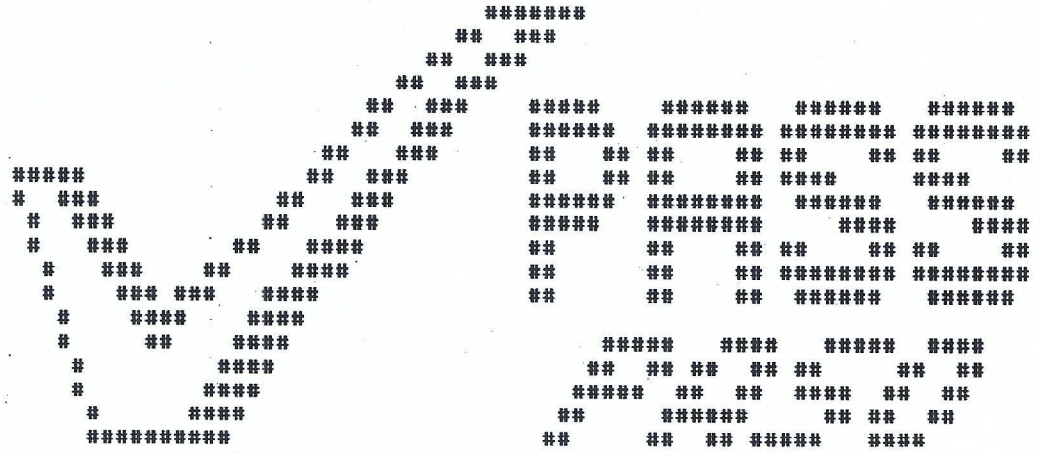

Tested By: Alicia Quezada

Form 0001-20150706 Rev D

ECONOLITE

SALES ORDER: S-25720-34A2-08 **SERIAL NUMBER:** H 43628

CONTROLLER COBG42100000000000 **Top Assy Cobalt Controller**

TESTED BY: **Alicia Quezada** Location: Anaheim 110V

VOLTAGE:

TEST DATE: **03-11-2026** TR #: 220V ●

OPERATING SOFTWARE **03.02.32**

Mac Address 0 **00:04:81:0A:1C:70**

Mac Address 1 **00:04:81:0A:1C:71**

Data Base **L3000**

PART NUMBER	Revision	DESCRIPTION	SERIAL NUMBER
140-0000-503	B	ASSY,COBALT,TS2-TYPE 2	H 43628 260301531
140-1012-004	C	FRONT PANEL,TS2-TYPE 1,COBALT	H 43628 260301532
119-1032-501	U	ASSY, PCB, ENGINE BOARD	H 43628 260301533
140-1000-501	W	ASSY,PCB,NEMA ATC,HOST BOARD	H 43628 260301534
140-1001-501	F	ASSY, PCB, MINI MOTHER BOARD	H 43628 260301535
140-1002-501	R	ASSY, PCB, NEMA ATC, POWER	H 43628 260301536
140-1004-502	NC	ASSY, PCB, ATC AGC,COBALT	H 43628 260301537
32913P4	NC	KEY, 8MB MEMORY, BLUE	H 43628 260301538

INSPECTED BY BG ECPI 12 QC INSP Ilyas Khalak / Bertha Garcia / Arnel Isaac DATE 03-11-2026

Printed copies are for reference only.

Only the electronic file of this document is stored and controlled and the Econolite Intranet is the master.

DATE: 03-11-2026 PAGE: 1


MODEL : ATC ENGINE BOARD/1C/COBALT TEST COUNT: 0

SERIAL NUMBER: H43628 >>>>> BENCH SINGLE FINAL <<<<<

IP: COM5 TEMP: 25.0 C <> 115.0 VAC <> LOOP COUNT: 1

TEST FOR	STATUS	DETAILS	TIME STAMP
SP8/Port2	PASSED	N/A	06:25:04
SP3S/Port1	PASSED	N/A	06:25:07
DATAKEY	PASSED	N/A	06:25:35
FLASH	PASSED	N/A	06:26:44
SRAM	PASSED	N/A	06:26:55
DRAM	PASSED	N/A	06:27:52
EEPROM	PASSED	N/A	06:27:55
ReadMAC 0	PASSED	00:04:81:0A:1C:70	06:28:07
ReadMAC 1	PASSED	00:04:81:0A:1C:71	06:28:18
USB 1	PASSED	N/A	06:28:21
USB 2	PASSED	N/A	06:28:24
SDCARD	PASSED	N/A	06:28:27
DISPLAY	VISUAL	N/A	06:30:29
ETH1 - 1	PASSED	N/A	06:30:57
ETH1 - 2	PASSED	N/A	06:31:27
ETH2 - 1	PASSED	N/A	06:32:05
ETH2 - 2	PASSED	N/A	06:32:34
NEMA IO	PASSED	N/A	06:32:45
SPEAKER	AUDIO	N/A	06:32:56
LED	VISUAL	N/A	06:33:02

*** TEST PASSED ***

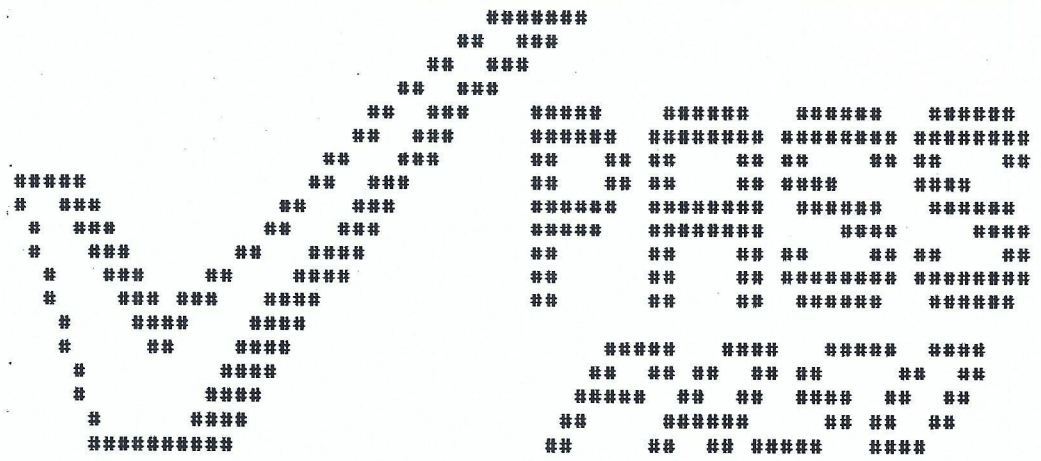

Tested By: Alicia Quezada Form 0001-20150706 Rev. A

DATE: 03-11-2026 TIME: 07:10:14 PAGE: 1


MODEL : ATC ENGINE BOARD/1C/COBALT

CONTROLLER TYPE: COBALT SHELF MOUNT 2100 DETECTED: COBALT SHELF MOUNT 2100

MAC ID(S): 00:04:81:0A:1C:70 <> 00:04:81:0A:1C:71

CONTROLLER FIRMWARE		RELEASED FIRMWARE		STATUS
EB U-BOOT	05.06.00	EB U-BOOT	05.06.00	OK
EB OS	06.18.00	EB OS	06.18.00	OK
EB MICRO	07.08.00	EB MICRO	07.08.00	OK
EB USB MICRO	27.01.00	EB USB MICRO	27.01.00	OK
HB PIO MICRO	10.04.00	HB PIO MICRO	10.04.00	OK
HB BGC MICRO	09.08.00	HB BGC MICRO	09.08.00	OK
HB BGR MICRO	18.04.00	HB BGR MICRO	18.04.00	OK
NPS MICRO	11.04.00	NPS MICRO	11.04.00	OK
AGC U-BOOT	12.01.00	AGC U-BOOT	12.01.00	OK
AGC OS	13.15.00	AGC OS	13.15.00	OK
TRAFFIC APP	03.02.32	TRAFFIC APP	03.02.32	OK
AGC APP	03.02.32	AGC APP	03.02.32	OK
DATABASE	L3000/NONE	DATABASE	L3000/NONE	OK

VERSION VERIFICATION: P A S S E D

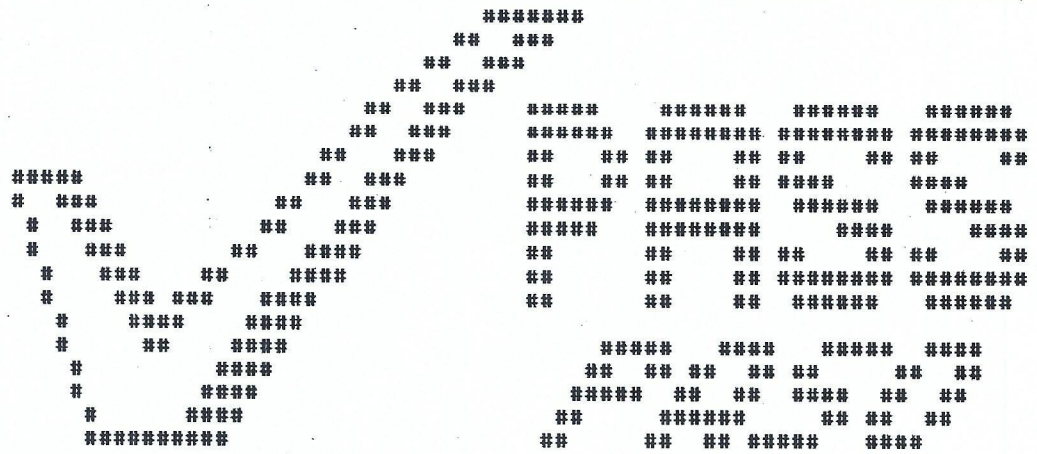

Tested By: Alicia Quezada

Form 0001-20150706 Rev D
