QIDDIYA DEVELOPMENT COMPANY					
DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00007	REVISION NUMBER:	0D	ISSUED BY:	PMO
DOCUMENT TITLE	MIR FORM	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022

Qiddiya

MATERIAL INSPECTION REQUEST (MIR) FORM

Contractor:	HAIF COMPANY
Project:	QPMO-410-CT-00618- ROAD ACCESS TO RESORT CORE
Contract No.:	QI09043311-VO-0004
Material Inspection Request Number:	QRXM114000-HFC-TEC-MIR-ITS-02-RO5-00014

شركة هيف Haif Company — Freyssinet — HAIF-FREYSSINET JV

Discipline									
Architecture	☐	Mechanical	☐	Information Technology	☐	Quality	☐	Project Controls	☐
Civil/Structural	☑	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

MATERIAL DESCRIPTION

Inspection / Test Location:	INTERIM ROAD MAIN LINE-02		
Material Name:	ITS CABINETS WITH ACCESSORIES	**Quantity:**	09 Nos.
P.O Number		**Delivery Note Number:**	TTSDN-HAIF-280426-024
Approved Material Transmittal Number: (Aconex document Approval)	QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00012	**Approval Date:**	
Inspection Date:	30-Jun-2026	**Inspection Start Time:**	11:00 AM
ITP:	QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00007	**Checklist:**	HFC-CKL-1001
Spec's / Dwg. Ref.:	TRAFFIC TECH SECURITY W.L.L	**Approved Method Statement Number:**	
Attachments:	**Test Certificate:** ◉ Yes ○ No **IFC / Shop Drawings:** ○ Yes ◉ No		

DESCRITPTION OF MATERIAL

Control Enclosure 559MMHX438WX470 MMD IP 65,GIG90 Sheet - Powder Coating Finish, DOUBLE Isolated Layer ,1 Fan 220V, Filter ,CNC fOAM gASKET (07 Nos.) Control Enclosure H1800XW800XD600 MM IP 65,GIG90 Sheet - Powder Coating Finish, DOUBLE Isolated Layer ,2 Fan 220V, Filter ,CNC fOAM gASKET (02 Nos.) Interim Road Main Line-02

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Are Complete Details Mentioned in P.O and Delivery Note?	◉ YES ○ NO	**REMARKS**	
Complies with Approved ITPs/Checklists?	◉ YES ○ NO	**REMARKS**	
Signs of Physcial Damage?	○ YES ◉ NO	**REMARKS**	
Conforms to Approved Material Submittal?	○ YES ○ NO	**REMARKS**	

Accepted:	◉
Accepted with Comments:	○
Rejected (See Remarks):	○

REMARKS:					
Name:	Moataz Elkhateeb	**Signature:**		**Date:**	30-06-2026

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Material requirements?	○ YES ○ NO	**Materials Are Stored correctly?**	✓ YES ○ NO ○ NA

Accepted:	✓
Accepted with Comments:	○
Rejected (See Remarks):	○

REMARKS:	Comply with the comments mentioned on attached supporting documents.				
Name:	M. YASIR.	**Signature:**		**Date**	30/06/2026.

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Haif Company / Freyssinet — HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - **Interim Road Access to Resort Core**	**Project Code:** QRXM114000
Location: 00	**Date:** 24-December-2025
Document Title: **Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (**ITS Cabinets**)**	**Ref No:** QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00012
	Rev No: 01

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☑ ITS ☐ Civil

Type: ☐ Pre-Qualification ☐ Method Statement ☒ Material Submittal ☐ Sample ☐ Other

Document Description: Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (ITS Cabinets)

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00012	**Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (ITS Cabinets)**

Enclosure:

Submitted By:	**Received By:**
Name: **Eng. Moataz** Signature: Date:24-December-2025	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments: For comments refer to the CRS

B: Approved with Comments
Saud Nawab
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

B: Approved with Comments
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

Below portion for Client use only

Comments:

Signed by: Signature: Date:

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Haif Company / Freyssinet — HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
Location: 00	**Date:** 14 -June-2026
Document Title: **Inspection & Test Plan for Intelligent Transportation System Works for ITS CABINET SYSTEM INSTALLATION AND OPERATION**	**Ref No:** QRXM114000-HFC-TEC-ITP-ITS-00007
	Rev No: 00

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☐ Authority ☐ Civil ☒ Others

Type: ☐ Pre-Qualification ☐ Method Statement ☐ Material Submittal ☐ Sample ☒ ITP

Document Description: This is Inspection&Test Plan for Intelligent Transportation System Works for ITS CABINET SYSTEM INSTALLATION AND OPERATION

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-ITP-ITS-00007	**Inspection&Test Plan for Intelligent Transportation System Works for ITS CABINET SYSTEM INSTALLATION AND OPERATION**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz Signature: Date: 14-June-2026	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments: All the work shall be carried out in accordance with approved shop drawings, project specifications and relevant standards & codes

A: Approved — Zuhair Fayez Partnership Consultants, Riyadh, Saudi Arabia

A: Approved — Zuhair Fayez Partnership Consultants, Riyadh, Saudi Arabia

A: Approved — Saud Nawab — Zuhair Fayez Partnership Consultants, Riyadh, Saudi Arabia

Below portion for Client use only

Comments:

Signed by: Signature: Date:

HAIF-FSA JV Inspection & Test Plan	I &TP	APPROVED DATE	DISCIPLINE
Inteligent Transportation System Works forITS CABINET SYSTEM INSTALLATION AND OPERATION	**HFC-ITP-0010**		**ITS**
PROJECT TITLE:WBS Access Road To Resort Core (RA4RC)	CONTRACTOR/SUBCONTRACTOR		
WIR No.	CONSTRUCTION- Intelligent Transportation System Works for INSTALLATION AND OPERATION of ITS CABINET	HAIF	

ITEM NO.	PROJECT PHASE	TASK / ACTIVITY	Quality Requirements /references/ specifications	Quality Record	INSPECTION RESPONSIBILITY ASSIGNMENTS			REMARKS
					Contractor	Third Party	Consultant	
1.0 DOCUMENT REVIEW								
1		Material Approval & Shop Drawing	QRXM114000-HFC-TEC-MAT-ITS-04-RO5-000014 QRXM114000-HFC-DRW-SDW-ITS-04-RO5-00001-00086	QRXM114000-HFC-TEC-MAT-ITS-04-RO5-000014 QRXM114000-HFC-DRW-SDW-ITS-04-RO5-00001-00086	R		H	
4.0 MATERIAL RECEIVING INSPECTION								
4		Material receiving inspection, protection & storage	QD0004-ADM-TEM-QMS00007[0A] MaterialReceiving Inspection in site HFC-CKL-1001	QD0004-ADM-TEM-QMS00007[0A] MaterialReceivingInspection in site HFC-CKL-1001	H		H	MIR to be submitted
3.0 WORK INSTALLATION								
3.1		PRE - INSTALLATION	HFC-CKL-1002	HFC-CKL-1002	H		H	
3.4		INSTALLATION	HFC-CKL-1003	HFC-CKL-1003	H		H	
3.3		TESTING	HFC-CKL-1004	HFC-CKL-1004	H		H	

GENERAL NOTES

1	Surveillance: QA/QC organization to monitor work in progress without notice from Construction Organization
4	Witness: QA/QC organization shall be notified of the timing of Inspection or test in advance. However, the inspection or test shall be performed as scheduled if the QA/QC organization representative is not present
3	Hold: QA/QC organization shall be notified of the timing of inspection or test in advance. Inspection or test shall not be carried out without the QA/QC organization representative in attendance.
4	If the Main Contractor delegates the assigned responsibility to the Subcontractor, then the Main Contractor will have the same degree of responsibility as assigned to Consultant.

LEGEND

H	Hold Point for QC Inspection/ Test	R	Review of Documents
W	Witness Inspection/T	RH	Review & approval of Documents
S	Surveillance		

Checklist : HFC-CKL-1001	Checklist	APPROVED DATE	DISCIPLINE
Material receiving inspection, protection & storage	HFC-CKL-1001		ITS
PROJECT TITLE: Road Access To Resort Core (RA4RC)	CONTRACTOR/SUBCONTRACTOR		
WIR No.	CONSTRUCTION- Intelligent Transportation System Works for INSTALLATION AND OPERATION of ITS CABINET — HAIF		

ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
1.0	**Material receiving inspection,protection & storage of CONSTRUCTION- for ITS Devices ITS CABINET SYSTEM**					
A	Deliver, store, and handle products, using means and methods that will prevent damage, deterioration, and loss, including theft and vandalism. Comply with manufacturer's written instructions.	project specification QRXP117115-DAH-VORA4R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING	✓			
B	Delivery and Handling:		✓			
1.0	Schedule delivery to minimize long-term storage at Project site and to prevent overcrowding of construction spaces.	project specification QRXP117115-DAH-VORA4R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING	✓			
4.0	Coordinate delivery with installation time to ensure minimum holding time for items that are flammable, hazardous, easily damaged, or sensitive to deterioration, theft, and other losses.	project specification QRXP117115-DAH-VORA4R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING	✓			
3.0	Deliver products to Project site in an undamaged condition in manufacturer's original sealed container or other packaging system, complete with labels and instructions for handling, storing, unpacking, protecting, and installing.	project specification QRXP117115-DAH-VORA4R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING	✓			
4.0	Inspect products on delivery to determine compliance with the Contract Documents and that products are undamaged and properly protected.	project specification QRXP117115-DAH-VORA4R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING	✓			
C	Storage:		✓			
1.0	Provide a secure location and enclosure at Project site for storage of materials and equipment.	project specification QRXP117115-DAH-VORA4R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING	✓			
4.0	Store products to allow for inspection and measurement of quantity or counting of units.	project specification QRXP117115-DAH-VORA4R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING	✓			
3.0	Store materials in a manner that will not endanger Project structure.	project specification QRXP117115-DAH-VORA4R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING	✓			
4.0	Store products that are subject to damage by the elements under cover in a weathertight enclosure above ground, with ventilation adequate to prevent condensation and with adequate protection from wind.	project specification QRXP117115-DAH-VORA4R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING	✓			
5.0	Protect foam plastic from exposure to sunlight, except to extent necessary for period of installation and concealment.	project specification QRXP117115-DAH-VORA4R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING	✓			
6.0	Comply with product manufacturer's written instructions for temperature, humidity, ventilation, and weather-protection requirements for storage.	project specification QRXP117115-DAH-VORA4R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING	✓			
7.0	Protect stored products from damage and liquids from freezing.	project specification QRXP117115-DAH-VORA4R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING	✓			
8.0	Provide a secure location and enclosure at Project site for storage of materials and equipment by Employer's construction forces. Coordinate location with Employer.	project specification QRXP117115-DAH-VORA4R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING	✓			

Remarks

PM/Contractor			QDC		
Contractor Construction			Third Party (if applicable)		
The work is ready for inspection			Document Reviewed	Work Inspected	Test Records Verified
Name	Signature	Date	Name	Signature	
Muharis Shams		30/6/26			
Contractor QC Inspector			QDC Supervision Consultant		30/06/2026

Form Ref. No. QDD004-ADM-TEM-QTY-00003– Rev.0A

TRAFFIC TECH
www.traffic-tech.com

تقنيات المرور الأمنية ذ.م.م.
TRAFFIC TECH SECURITY W.L.L.

Date: **28-JUNE-2026**
Our Ref: **TTSDN-Haif-280626-024**

Delivery Note

To: **HAIF COMPANY**
---------- الى:

Ref: **WS045CR-53 (RA2RC – ACCESS ROAD TO RESORT CORE)**

SN	Model No. رقم الموديل	Description الوصـــــــف	Unit الوحـدة	Qty الكميـــة	Remarks ملاحظـات
MATERIAL SUPPLY (TRAFFIC SIGNALS)					
1		Control Enclosure 559MMHX438WX470MMD, IP 65, GI G90 SHEET – POWDER COATING FINISH, DOUBLE ISOLATED LAYER, 1 FAN 220V, FILTER, CNC FOAM GASKET	NOS	7	
2		Control Enclosure H1800XW800XD600 MM, IP 65, GI G90 SHEET – POWDER COATING FINISH, DOUBLE ISOLATED LAYER, 2 FAN 220V, 2 FILTER, CNC FOAM GASKET	NOS	2	
3		BASE PLATE (350* 350)	NOS	6	
4		HDG ANCHOR BOLT (M18*500 FOR 3.7 M POLE FOUNDATION	NOS	24	

شركة حائل Hail Contracting
Date
Project. Qiddiya
WS-045CR
Received

Delivered By: EHAB BASLA ---------- **Date:** **28-06-2026** ----------
Printed Name & Signature

Received By: ----------
Printed Name & Signature **Date:** ----------

Unit No. 38, Building 3990
Anas Bin Malik St., Al Malga District
P.O. Box 13524
6615, Riyadh, Saudi Arabia
E-mail : ttg@traffic-tech.com
Web: www.traffic-tech.com

SMART VISION FACTORY
https://svc-ksa.com/
7385 : AL Kharj Branch Rd - Al Noor Dist.
Riyadh 14321-2362

PDI REPORT

Description: - OUTDOOR ENCLOSURE 559 x 438 x 470	Client Name: - Traffic Tech Security W.L. L
Total QTY: - 02PCS	SO, NO: - 2
Date: - 12-6-2026	PO NO: - -
Drawing Number: - SO-870-01	SR NO: - SO-2-01

Sr.No.	Description	Observation					Remarks
		1	2	3	4	5	
FABRICATED CABINET							
1	Punching Of Critical Holes	√	√	√	√	√	
2	Fan Filter Cut Layout	√	√	√	√	√	
3	Wire Outlet	√	√	√	√	√	
4	Mounting plate fixation	√	√	√	√	√	
5	Door Hinge holes	√	√	√	√	√	
6	Din rail Mounting Holes	√	√	√	√	√	
7	Welding	√	√	√	√	√	
8	Draw And Embossing	√	√	√	√	√	
9	Bending	√	√	√	√	√	
10	Fitment	√	√	√	√	√	
11	Front Bazzel	NA	NA	NA	NA	NA	
12	Seismic kit	NA	NA	NA	NA	NA	
13	Assembly Holes	√	√	√	√	√	
14	Bur & Spatter	√	√	√	√	√	
15	Traceability Code	√	√	√	√	√	
POWDER COATED CABINET							
A	Visual Inspection of Coating	√	√	√	√	√	
B	Printing (logos & stickers)	NA	NA	NA	NA	NA	
C	Mean Average Value in microns	90	95	105	89	99	PASS
DIMENSION							
A	With fabrication	√	√	√	√	√	
Conclusion: Accept / Conditional Accept /Reject		Accept					

Prepared By: - Alhareth	Verified By: - Sunil Kashinath

SMART VISION FACTORY
https://svc-ksa.com/
7385 : AL Kharj Branch Rd - Al Noor Dist.
Riyadh 14321-2362

IK10 IMPACT TEST REPORT (IEC 62262)

Report No.	47321-01	**Date**	6-15-2026	**Page**	1 of 1
Customer	Traffic Tech Security W.L.L	**Project**	-	**Location**	RIYADH
Product Name	OUTDOOR ENCLOSURE 559 x 438 x 470	**Model / Type**	ODU	**IP Rating**	IP65
Standard	IEC 62262	**IK Rating**	IK10	**Impact Energy**	20 Joules

TEST DETAILS

Test Equipment	Vertical drop Hammer	**Hammer Mass**	5 kg	**Drop Height**	400 mm
Number of Impacts	3	**Impact Locations**	Front/Rear/Sides	**Ambient Temp**	25
Test Orientation	Vertical downward	**Surface Condition**	Powder Coated		

TEST RESULTS

S.No	Impact Location	Energy (J)	Observation	Damage (Yes/No)	Remarks
1	Door	20	-	no	pass
2	Body	20	-	no	pass
3	Canopy	20	-	no	pass
4					
5					

CONCLUSION

☒ PASS ☐ FAIL

Tested By	Alhareth	**Checked By**	Sunil
Signature & Date		**Signature & Date**	

SMART VISION FACTORY
https://svc-ksa.com/
7385 : AL Kharj Branch Rd - Al Noor Dist.
Riyadh 14321-2362

DC NO-SVC-4321-01
ISSUE DATE 1/2/2023
ISSUE: -1
REV: - 1
QUALITY CONTROL

PDI REPORT

Description: - OUTDOOR ENCLOSURE 1800 x 800 x 600	Client Name: - Traffic Tech Security W.L. L
Total QTY: - 07PCS	SO, NO: - 2
Date: - 15-6-2026	PO NO: - -
Drawing Number: - SO-870-02	SR NO: - SO-2-02

Sr.No.	Description	Observation					Remarks
		1	2	3	4	5	
FABRICATED CABINET							
1	Punching Of Critical Holes	√	√	√	√	√	
2	Fan Filter Cut Layout	√	√	√	√	√	
3	Wire Outlet	√	√	√	√	√	
4	Mounting plate fixation	√	√	√	√	√	
5	Door Hinge holes	√	√	√	√	√	
6	Din rail Mounting Holes	√	√	√	√	√	
7	Welding	√	√	√	√	√	
8	Draw And Embossing	√	√	√	√	√	
9	Bending	√	√	√	√	√	
10	Fitment	√	√	√	√	√	
11	Front Bazzel	NA	NA	NA	NA	NA	
12	Seismic kit	NA	NA	NA	NA	NA	
13	Assembly Holes	√	√	√	√	√	
14	Bur & Spatter	√	√	√	√	√	
15	Traceability Code	√	√	√	√	√	
POWDER COATED CABINET							
A	Visual Inspection of Coating	√	√	√	√	√	
B	Printing (logos & stickers)	NA	NA	NA	NA	NA	
C	Mean Average Value in microns	92	98	102	103	105	PASS
DIMENSION							
A	With fabrication	√	√	√	√	√	
Conclusion: Accept / Conditional Accept /Reject		Accept					

Prepared By: - Alhareth	Verified By: - Sunil Kashinath

SMART VISION FACTORY
https://svc-ksa.com/
7385 : AL Kharj Branch Rd - Al Noor Dist.
Riyadh 14321-2362

IK10 IMPACT TEST REPORT (IEC 62262)

Report No.	47321-01	**Date**	15-6-2026	**Page**	1 of 1
Customer	Traffic Tech Security W.L.L	**Project**	-	**Location**	RIYADH
Product Name	OUTDOOR ENCLOSURE 1800 x 800 x 600	**Model / Type**	ODU	**IP Rating**	IP65
Standard	IEC 62262	**IK Rating**	IK10	**Impact Energy**	20 Joules

TEST DETAILS

Test Equipment	Vertical drop Hammer	**Hammer Mass**	5 kg	**Drop Height**	400 mm
Number of Impacts	4	**Impact Locations**	Front/Rear/Sides	**Ambient Temp**	25
Test Orientation	Vertical downward	**Surface Condition**	Powder Coated		

TEST RESULTS

S.No	Impact Location	Energy (J)	Observation	Damage (Yes/No)	Remarks
1	Door	20	-	no	pass
2	Body	20	-	no	pass
3	Canopy	20	-	no	pass
4	Fan Guard	20		no	pass
5					

CONCLUSION

☒ PASS ☐ FAIL

Tested By	Alhareth	**Checked By**	Sunil
Signature & Date		**Signature & Date**	

TEST REPORT

SR- 436254 **Report Date:** **MAY**, 14 2026

Customer* **Address*** **Customer Request Info**	Smart Vision Factory Al Dera, Al Manakh District, Riyadh, 14614, SAU, GCA-SQ25007685
Manufacturer **Address**	Smart Vision Factory Al Dera, Al Manakh District, Riyadh, 14614, SAU,
Product **Brand** **Model** **Technical specifications** **Country of Mfr.**	GME OUTDOOR CABINET SVC GME CABINET IP-65-GME-SVC-014 Enclosure H-1800 x W-800 x D-600 mm KSA
Received Date **Test Start Date** **Test End Date** **Test Location** **Test Method** **Environmental Conditions**	07-05-2026 08-05-2026 14-05-2026 201st St. 2nd Industrial City, Riyadh, Saudi Arabia SASO GSO IEC 60529:2015 (IP65) 25 °C

Test Results:

Result: **CONFORM**
Remarks:

Authorized Signatory:

Albert Delloro
Technical Manager

GCC Lab Conformity Assessment Company
شركة المختبر الخليجي للتحقق والمطابقة
مختبر فحص المنتجات الكهربائية-الرياض
Electrical Products Testing Lab-Riyadh
CR No.: 2050115437

- Information with "*" denotes Customer provided information.
- Results are found on the succeeding pages.
- Test(s) with "**" denotes non-accredited test(s). Test(s) with "***" denotes subcontracted test(s).
- Results relates to sample as received and only to the item(s) tested on specified Standard Test Method(s) and specific clause(s).
- Tests are performed on standard rated voltages and frequency in Saudi Arabia.
- Test Report shall not be reproduced, except in full, without written approval of EPTLR, GCA.
- The laboratory utilizes decision rule on MSP/7.8/01.01 procedure for tests wherein statement of conformity are stated.
- Unless requested for return, Test Item(s) are destroyed and discarded 90 days after Test Report Date.
- Test conducted may form into unusable and dangerous item(s). GCA, EPTLR do not assume liability resulting from the use of the returned item(s).
- Test report meets the requirement of ILAC-G8:09/2019 Decision Rules. Binary Statement for Simple Acceptance Rule (w = 0)

201st St. 2nd Industrial City, Riyadh, Saudi Arabia
Tel: +966 920029293 Ext. 1108 Fax: +966 920029296
Email: sales@gcclcsc.com , Website: https://www.gcclcsc.com

Result Details: _____

Clause	Test Description	Analysis	Result
13.4	**Dust test for first characteristic numerals 5 and 5**		**PASS**
	The test is made using a dust chamber incorporating the basic principles shown in figure 2 whereby the powder circulation pump may be placed by other means suitable to maintain the talcum powder in suspension in a closed test chamber. The talcum powder used shall be able to pass through a square meshed sieve, the nominal wire diameter of which is 50 µm and the minimal width of a gap between wires 75 µm. The amount of the talcum powder to be used is 2 kg per cubic meter of the test chamber volume. It shall not have been used for more than 20 tests.	Complied	p
	ENCLOSURE ARE OF NECESSITY IN ONE OF TWO CATEGORIES:		
	Category 1: Enclosures where the nominal working cycle of the equipment causes reductions in air pressure within the enclosure below that of the surrounding air, for example, due to thermal cycling effects.	Category 1as per clause 13.6.1 (special conditions for first characteristic numeral 6)	p
	Category 2: Enclosures where no pressure difference relative to the surrounding air is present.	Category 1	NA
	CATEGORY 1ENCLOSURES:		
	The enclosure under test is supported inside the test chamber and the pressure inside the enclosure is maintained below the surrounding atmospheric pressure by a vacuum pump. The suction connection shall be made to a hole specially provided for this test. If not otherwise specified in the relevant product standard, this hole shall be in the vicinity of the vulnerable parts.	The suction connection pass thru the cable inlet hole.	p
	If it is impracticable to make a special hole, the suction connection shall be made for the cable inlet hole. If there are holes (for example, more able inlet holes or drain-holes) these shall be treated as intended for normal use on site.	Complied Cable inlet hole	p
	The object of the test is to draw into the enclosure, be means of depression, a volume of air 80 times the volume of the sample enclosure tested without exceeding the extraction rate of 60 volumes per hour. In no event shall the volume of extraction exceed 2 kPa (20 mbar) on the manometer shown in figure 2.	Complied	p
	If an extraction rate of 40 to 60 volumes per hour is obtained the duration of the test is 2 h.	Not obtained	NA
	If, with a maximum depression of 2 kPa (20 mbar), the	8 Hours	p

201st St. 2nd Industrial City, Riyadh, Saudi Arabia
Tel: +966 920029293 Ext. 1108 Fax: +966 920029296
Email: sales@gcclcsc.com , Website: https://www.gcclcsc.com

	extraction rate is less than 40 volumes per hour, the test is continued until 80 volumes have been drawn through, or a period of 8 h has elapse.		
	Category 2 enclosures:		
	The enclosure under test is supported under its normal operating position inside the test chamber, but is not connected to a vacuum pump. Any drain-hole normally open shall be left open for the duration of the test. The test shall be continued for a period of 8 hours.	Category 1	NA
	Category 1 an category 2 enclosures:		
	If it is impracticable to test the complete enclosure in the test chamber, one of the following procedures shall be applied:	Test conducted at complete enclosure	NA
	- Testing of individually enclosed sections of the enclosure;	-	NA
	- Testing of representative parts of the enclosure, comprising components such as doors, ventilation openings, joints, shafts seals, etc., in position during test;	-	NA
	- Testing of a smaller enclosure having the full-scale design details.	-	NA
	In the last two cases, the volume of air to be drawn through the enclosure under test shall be the same as for the whole enclosure in full scale.	-	NA
13.6	Special conditions for first characteristic numeral 6		-
13.6.1	The enclosure shall be deemed category 1, whether reductions in pressure below the atmospheric pressure are present or not.	Category 2	NA
13.6.2	Acceptance conditions for first characteristic numeral 6	Complied	p
	The protection is satisfactory if no deposit of dust is observable inside the enclosure at the end of the	Complied	p
14.2.5	IP second numerical degree (5: Protected against water jet)		PASS
	Test for second characteristic numeral 5 with 6.3mm nozzle.	Complied	p
	The conditions to be observe are as follows:	Complied	p
	- Internal diameter of nozzle: 6.3 mm;	Complied	p
	- Delivery rate: 12.5l/min ± 5%;	Complied	p
	- Water pressure: to be adjusted to achieve the specified delivery rate	Complied	p
	- Core of the substantial stream: circle of approximately 40 mm diameter at 2.5 m distance from nozzle;	Complied	p
	- Test duration per square meter of enclosure surface area	3 min	p

201st St. 2nd Industrial City, Riyadh, Saudi Arabia
Tel: +966 920029293 Ext. 1108 Fax: +966 920029296
Email: sales@gcclcsc.com , Website: https://www.gcclcsc.com

	likely to be sprayed: 1min; Minimum test duration: 3 min.;		
	- Distance from nozzle to enclosure surface: between 2.5 m and 3 m.	2.Sm	p
14.3	Acceptance condition	Complied	p
	After the test in accordance with the appropriate requirements of 14.2.1 to 14.2.9, the enclosure shall be inspected for ingress of water.	Complied	p
	It is the responsibility of the relevant technical committee to specify the amount of water which may be allowed to enter the enclosure and the details of a dielectric strength test, if any.	Complied	p
	In general, if any water has entered, it shall not:	Complied	p
	Be sufficient to interfere with the correct operation of the equipment or impair safety;	Not Affect the Operation	p
	Deposit on insulation parts where it could lead to tracking along the creepage distances;	Deposit But Not Affect Creepage	p
	Reach live parts or wingdings not designed to operate when wet.	Not Reach the live Part	p
	Accumulate near the cable end or enter the cable if any.	Far From the cable	p
	If the enclosure is provided with drain-holes, it should be proved be inspection that any water which enters does not accumulate and that it drains away without doing any harm to the equipment.	No drain water	NA
	For enclosure without drain-holes, the relevant product standard shall specify the acceptance conditions if water can accumulate to reach live parts.	-	NA

GCC Lab Conformity Assessment Company
شركة المختبر الخليجي للتحقق والمطابقة
مختبر فحص المنتجات الكهربائية-الرياض
Electrical Products Testing Lab-Riyadh
CR No.: 2050115437

201st St. 2nd Industrial City, Riyadh, Saudi Arabia
Tel: +966 920029293 Ext. 1108 Fax: +966 920029296
Email: sales@gcclcsc.com , Website: https://www.gcclcsc.com

QUALITY CERTIFICATE

Saudi Iron and Steel Company (HADEED)
P.O.Box 10053 Jubail 31961
Kingdom of Saudi Arabia

حديد
hadeed

شـــهادة الجـــــودة

(الشركة السعودية للحديد والصلب (حديد
ص . ب 10053 الجبيل الصناعية 31961
المملكة العربية السعودية

Customer Name and Address اسم الزبون وعنوانه	*Shipping Address* عنوان التسليم
Almusairiey Metallic Industries	**Almusairiey Metallic Industries**
P.O.BOX -->	**P.O.BOX -->**
Eastern High Way Road	**Eastern High Way Road**
14333 Riyadh	**14333 Riyadh**
TEL # 112650880	**TEL # 112650880**

Certificate No.	**F003934926**	رقم الشهادة
Customer No.	**20008750**	رقم الزبون
Sales Order/Item No.	**1410002944/120**	رقم أمر البيع
Customer P.O. No.	**25001957**	رقم أمر الشراء
Date of Issue	**08/12/25**	تاريخ الإصدار
Delivery note No.	**8410133347**	رقم التسليم

Product details **CRCG** خواص المنتج Standard **SASO-ASTM-A653** المواصفات Coating Spec. **G90** مواصفة الزنك Steel Grade **CS-TypeB** درجة الحديد

Thickness(mm) **2.00** السماكة (ملم) Width(mm) **1219** العرض(ملم) Length(mm) الطول(م)

Physical Properties — الخواص الفيزيائيه

Material ID رقم اللفة /رقم التغليف	Heat ID رقم الصبة	Pieces القطع	Net Wt.(MT) صافي الوزن	YS N/mm2 مقاومة الخضوع	UTS N/mm2 مقاومة الشد	EL% نسبة الاستطالة	GL (mm)L/T اختبار القياس	Bend Test إختبار الثني	Hardness الصلادة	ECV اركنسن	Zinc Coat g/m2 التكسية بالزنك	r	n	Ra(Mm) الخشونه	Impact (J) اختبار تصادم	Others أخرى
1625470159	2515095	-	7.56	287	358	36	L0 50	OK	54	-	276	-	-	-	-	-

Chem. Composition % — التركيب الكيميائي%

Heat ID رقم الصبة	C كربون	Mn منجنيز	S كبريت	P فوسفور	Si سيليكون	Al ألومنيوم	N نتروجين	Nb نيوبيوم	V فانيديوم	Ti تيتانيوم	Ca كالسيوم	Cr كروم	Cu نحاس	Mo موليبدنيوم	Sn قصدير	Ni نيكل	CEV مكافئ الكربون	Tramp الشوائب	B بورون
2515095	0.0517	0.171	0.0104	0.007	0.008	0.0366	0.0025	00	0.00093	0.00085	0.0006	0.016	0.0314	0.00351	0.002	0.0219	0.088		0.00001

Impact Test Temperature 'C درجة إختبار التصادم

Bend Test is according to standard إختبار الثني حسب المواصفات المطلوبة

Drop Weight Tear Test إختبار السقوط الحر حسب المواصفات المطلوبة

Hardness Unit وحدة اختبار الصلادة

OHSAS 18001:2007
Occupational Health & Safety Management System

Responsible Care
14001:2013 & ISO 14001:2004
Environmental Management System

Hadeed laboratory accredited for ISO 17025 : 2017
Cert. No. TL-693
مختبرات حديد مطابقة لنظام المواصفات القياسية
ISO 17025 : 2017
TL-693 رقم الشهادة

ISO 9001 Quality Management
ISO 22301 Business Continuity Management

This certificate is generated electronically, stamp and signature are not required

TEST CERTIFICATE AS PER EN10204/3.1
شهادة الإختبار حسب المواصفات الأوروبية

QUALITY CERTIFICATE

Saudi Iron and Steel Company (HADEED)
P.O.Box 10053 Jubail 31961
Kingdom of Saudi Arabia

حديد
hadeed

شـــهادة الجـــــودة

(الشركة السعودية للحديد والصلب (حديد
ص . ب 10053 الجبيل الصناعية 31961
المملكة العربية السعودية

Customer Name and Address اسم الزبون وعنوانه	*Shipping Address* عنوان التسليم
Almusairiey Metallic Industries	**Almusairiey Metallic Industries**
P.O.BOX -->	**P.O.BOX -->**
Eastern High Way Road	**Eastern High Way Road**
14333 Riyadh	**14333 Riyadh**
TEL # 112650880	**TEL # 112650880**

Certificate No.	**F003935046**	رقم الشهادة
Customer No.	**20008750**	رقم الزبون
Sales Order/Item No.	**1410002944/110**	رقم أمر البيع
Customer P.O. No.	**25001957**	رقم أمر الشراء
Date of Issue	**09/12/25**	تاريخ الإصدار
Delivery note No.	**8410133346**	رقم التسليم

Product details **CRCG** خواص المنتج — Standard **SASO-ASTM-A653** المواصفات — Coating Spec. **G90** مواصفة الزنك — Steel Grade **CS-TypeB** درجة الحديد

Thickness(mm) **1.50** السماكة (ملم) — Width(mm) **1219** العرض(ملم) — Length(mm) الطول(م)

Physical Properties — الخواص الفيزيائيه

Material ID رقم اللفة /رقم التغليف	Heat ID رقم الصبة	Pieces القطع	Net Wt.(MT) صافي الوزن	YS N/mm2 مقاومة الخضوع	UTS N/mm2 مقاومة الشد	EL% نسبة الاستطالة	GL (mm)L/T اختبار القياس	Bend Test إختبار الثني	Hardness الصلادة	ECV أركنسن	Zinc Coat g/m2 التكسية بالزنك	r	n	Ra(Mm) الخشونه	Impact (J) اختبار تصادم	Others اخرى
1625470295	2502125	-	7.53	296	358	36	L0 50	OK	56	-	276	-	-	-	-	-
1625470294	2502125	-	7.92	296	358	36	L0 50	OK	56	-	276	-	-	-	-	-

Chem. Composition % — التركيب الكيميائي%

Heat ID رقم الصبة	C كربون	Mn منجنيز	S كبريت	P فوسفور	Si سيليكون	Al ألومنيوم	N نتروجين	Nb نيوبيوم	V فانيديوم	Ti تيتانيوم	Ca كالسيوم	Cr كروم	Cu نحاس	Mo موليبدنيوم	Sn قصدير	Ni نيكل	CEV مكافئ الكربون	Tramp الشوائب	B بورون
2502125	0.0507	0.202	0.0063	0.0034	0.01	0.036	0.0014	00	0.00061	0.00094	0.00036	0.0136	0.0252	0.00499	00	0.0158	0.091		00
2502125	0.0507	0.202	0.0063	0.0034	0.01	0.036	0.0014	00	0.00061	0.00094	0.00036	0.0136	0.0252	0.00499	00	0.0158	0.091		00

Impact Test Temperature °C درجة إختبار التصادم

Bend Test is according to standard اختبار الثني حسب المواصفات المطلوبة

Drop Weight Tear Test اختبار السقوط الحر حسب المواصفات المطلوبة

Hardness Unit وحدة اختبار الصلادة

TEST CERTIFICATE AS PER EN10204/3.1
شهادة الإختبار حسب المواصفات الأوروبية

OHSAS 18001:2007
Occupational Health & Safety Management System

Responsible Care 14001:2013 & ISO 14001:2004 Environmental Management System

Hadeed laboratory accredited for ISO 17025 : 2017
Cert. No. TL-693
مختبرات حديد مطابقة لنظام المواصفات القياسية ISO 17025 : 2017
رقم الشهادة TL-693

ISO 9001 Quality Management
ISO 22301 Business Continuity Management

This certificate is generated electronically, stamp and signature are not required

شركة برج الحضارة للتجارة
AL-HADARA TOWER FOR TRADING CO.

TEST REPORT

CUSIOXER NANE : AL-HUDHARA TOWER TRADING COWANY
1.PINO_: 2_DATE OF PI: 09/07/2025 3 _TEST DATE: 2025-08-30
GOODS DESCRIPTION: ANCHOR BOLT "J"TYPE WITH TWO NUTS +TWO FLAT WASHERS
4. SIZE : M18*500 NUMBER OF SAMPLES TESTED: 5 PCS

Percentage Composition of Chemistry %					
Material	C	Si	Mn	S	P
Q195	0.053	0.113	0.33	0.024	0.017

Mechanical Property :

Inspection Items	Sample	Standard		Test.	Result	Remarks
		Min.	Max.	Min.	Max.	
Tension Strength (Rm/Mpa)	5	315	430	350	400	PASS

Dimensional Inspection

Inspection Items	Sample	Standard		Test.	Result	Remarks
		Min.	Max.	Min.	Max.	
Outer Diameter Of Rod (mm)	5	17.4	18	17.5	18	PASS
Outer Diameter Of Thread (mm)	5	17.4	18	17.5	18	PASS
L (mm)	5	395	405	396	404	PASS
T (mm)	5	95	105	96	103	PASS
W (mm)	5	95	105	96	103	PASS
H (mm)	5	113	125	115	124	PASS


Surfice Finished

Surface Finished	Thickness	Sample	Standard		Test.	Result	Remarks
			Min.	Max.	Min.	Max.	
HOT---DIP GALVANIZING	um	5	50	90	60	90	PASS

Heat Treatment

Rau Material	Tensile Strength	Grade	Remarks
Q195	≥400Mpa	4.8	PASS

TH PRODUCT DESCRIBED ABOVE HAS BEEN TESTED COMPLIES WITH THE TERMS OF ORDER.

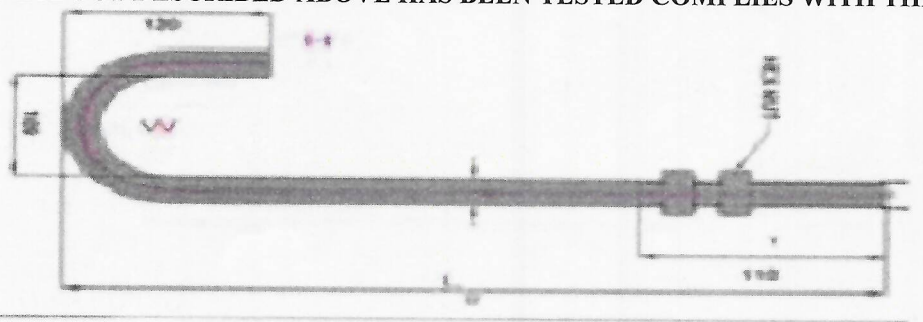

Smart Vision factory

REF tts

Delivery Note

Eng Name	Traffic Tech Security W.L.L.	ON	1896
AraName	0	Contact	
Contact		Mobile	0
Mobile		SO	
SO	230.00	Location	
VAT		DATE	5/17/26
P.O	2026-0023	Status	

Sr	Code	Descriptions	Unit	QTY	DELIVERY	BALANCE
1.00		GME: IP65 Multidoor (Front & Back) ITS ground mounted enclosure U32 (1800mm H x 800mm W x 600mm H) with fan cooling.	NOS	2		
2.00		VAL-MPME: IP66 Enclosure with the pole mount bracket with the dimensions of (559mm H x 438mm W x 470mm D) with sufficient air flow and fan cooling.	NOS	7		
3.00		CD 25X60 - Cable duct	METER	50		
4.00		CD 40X60 - Cable duct	METER	24		
5.00		CD 60X60 - Cable duct	METER	10		
6.00		Acti9 iC60N 1P 6A C Miniature Circuit breaker A9F44106	PCS	24		
7.00		Acti9 iC60N 1P 10A C Miniature Circuit breaker A9F44110	PCS	36		
8.00		Acti9 iC60N 2P 16A C Miniature Circuit breaker	NOS	7		
9.00		Acti 9 iID - RCCB - 2P - 100A -100mA - type AC A9R12291	PCS	4		
10.00		Acti9 iC60N 2P 63A C Miniature Circuit breaker A9F44263	PCS	2		
11.00		Acti9 iC60N - miniature circuit breaker - 2P - 32A - C curve	NOS	4		
12.00		(PoE Ethernet Extender)	NOS	17		
13.00		Wire lugs for 0.75mm	PKT	27		
14.00		Wire lugs for 1.5mm	PKT	27		
15.00		Wire lugs for 2.5mm	PKT	27		
16.00		Wire lugs for 4mm	PKT	5		
17.00		Wire lugs for 10mm	PKT	2		
18.00		CAT 6 Cable Manager	NOS	27		
19.00		12-port RJ45 sockets 10" rack-mount Cat-6A patch panel	PCS	18		
20.00		2U-Adjustable stepless Bracket	NOS	9		
21.00		3U 19" Electrical Distribution Box	NOS	18		
22.00		Steel Plate For Incoming Power Supply (210mm*226mm) W*H	NOS	9		
23.00		Steel Plate For UPS (580mm*280mm) W*H	NOS	9		
24.00		35mm* 2000MM - DIN rail	NOS	56		

Receiver Name:

Prepared BY :

OSAMA ABO RJAILA

(Logistics Officer)

Mobile: 0591271858

Signature:

Mobile:

Iqama:

Date:
