QIDDIYA DEVELOPMENT COMPANY					
DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00007	REVISION NUMBER:	0D	ISSUED BY:	PMO
DOCUMENT TITLE	MIR FORM	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022

Qiddiya

MATERIAL INSPECTION REQUEST (MIR) FORM

Contractor:	HAIF COMPANY
Project:	QPMO-410-CT-00618- ROAD ACCESS TO RESORT CORE
Contract No.:	QI09043311-VO-0004
Material Inspection Request Number:	QRXM114000-HFC-TEC-MIR-ITS-02-RO5-00020

Haif Company | Freyssinet | HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☐	Quality	☐	Project Controls	☐
Civil/Structural	☑	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

MATERIAL DESCRIPTION

Inspection / Test Location:	INTERIM ROAD MAIN LINE-02		
Material Name:	ITS SYSTEMS TRAFFIC CAMERA POLES & BASE PLATE	Quantity:	09 Set.
P.O Number		Delivery Note Number:	TTSDN-HAIF-290726-029
Approved Material Transmittal Number: (Aconex document Approval)	QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00017	Approval Date:	
Inspection Date:	31-Aug-2026	Inspection Start Time:	10:00 AM
ITP:	QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00006	Checklist:	HFC-CKL-9001
Spec's / Dwg. Ref.:	TRAFFIC TECH SECURITY W.L.L	Approved Method Statement Number:	
Attachments:	Test Certificate: ◉ Yes ○ No IFC / Shop Drawings: ○ Yes ◉ No		

DESCRITPTION OF MATERIAL

(PC-FG-OCT-00113)H.D.G Octagonal Camera Pole 15.0m High,6.0mm,7mm thik. With Base plate550*550*30mm (02 set.) & (PC-FG-OCT-00114)H.D.G Octagonal ITS Pole 6.1m High,4.0mm,7mm thik. With Base plate300*300*15mm (07 set.) for Interim Road Main Line-02

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Are Complete Details Mentioned in P.O and Delivery Note?	◉ YES	○ NO	REMARKS	
Complies with Approved ITPs/Checklists?	◉ YES	○ NO	REMARKS	
Signs of Physcial Damage?	○ YES	◉ NO	REMARKS	
Conforms to Approved Material Submittal?	○ YES	○ NO	REMARKS	

Accepted:	◉
Accepted with Comments:	○
Rejected (See Remarks):	○

REMARKS:					
Name:	Moataz Elkhateeb	Signature:		Date:	31-08-2026

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Material requirements?	○ YES	○ NO	Materials Are Stored correctly?	○ YES	○ NO ○ NA

Accepted:	○
Accepted with Comments:	✓
Rejected (See Remarks):	○

REMARKS:	Inspection done for delivered material in the site laydown and found as per delivery note and material approved. Final approval subjected to provide TPL test report for the mentioned material Compliance to project specification.				
Name:	Abdelrahman Hassan	Signature:		Date	31/8/2026

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Haif Company / Freyssinet — HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - **Interim Road Access to Resort Core**	**Project Code:** QRXM114000
Location: 00	**Date:**22-January-2026
Document Title:**Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L** (ITS and CCTV Poles)	**Ref No:** QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00017
	Rev No: 00

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☑ ITS ☐ Civil

Type: ☐ Pre-Qualification ☐ Method Statement ☒ Material Submittal ☐ Sample ☐ Other

Document Description:Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (ITS and CCTV Poles)

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00017	**Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L** (ITS and CCTV Poles)

Enclosure:

Submitted By:	**Received By:**
Name: **Eng. Moataz**	Name:
Signature:	Signature:
Date:22-January-2026	Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments:

1. The mounting heights of all ITS / RWIS / AQM devices shall be in accordance with SHC306, project specification & manufacturers' recommendations to ensure optimal system performance.
2. Structural calculation shall be reviewed by structural engineer.
3. Provide weatherproof, non- degradable heat-resistant rubber to all access doors
4. Pole specifications shall be as per the pole manufacturer's recommendations
5. Galvanization & Compliance certificates to be provided at the stage of MIR.
6. All materials shall be in compliance with project specifications and relevant standards

B: Approved with Comments — Mohammed Yasir Khadeva Ali — Zuhair Fayez Partnership Consultants Riyadh , Saudi Arabia

B: Approved with Comments — Saud Nawab — Zuhair Fayez Partnership Consultants Riyadh , Saudi Arabia

Below portion for Client use only

Comments:

B: Approved with Comments — Zuhair Fayez Partnership Consultants Riyadh , Saudi Arabia

Signed by: Signature: Date:

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Hail Company / Freyssinet / HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
Location: 00	**Date:** 14-June-2026
Document Title: **Inspection & Test Plan for TRAFFIC SURVEILLANCE (CCTV) SYSTEM-PTZ CAMERAS INSTALLATION AND OPERATION**	**Ref No:** QRXM114000-HFC-TEC-ITP-ITS-00005
	Rev No: 00

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☐ Authority ☐ Civil ☒ Others

Type: ☐ Pre-Qualification ☐ Method Statement ☐ Material Submittal ☐ Sample ☒ ITP

Document Description: This is Inspection&Test Plan for TRAFFIC SURVEILLANCE (CCTV) SYSTEM-PTZ CAMERAS INSTALLATION AND OPERATION

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-ITP-ITS-00005	**Inspection&Test Plan for TRAFFIC SURVEILLANCE (CCTV) SYSTEM-PTZ CAMERAS INSTALLATION AND OPERATION**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz Signature: Date: 14-June-2026	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments: All the work shall be carried out in accordance with approved shop drawings, project specifications and relevant standards & codes







Below portion for Client use only

Comments:

Signed by: Signature: Date:

HAIF-FSA JV Inspection & Test Plan						I &TP		APPROVED DATE	DISCIPLINE		
Inteligent Transportation System Works for TRAFFIC SURVEILLANCE (CCTV) SYSTEM-PTZ CAMERAS INSTALLATION AND OPERATION						**HFC-ITP-020**			**ITS**		
PROJECT TITLE: WBS Access Road To Reson Cove (RA2RC)						CONTRACTOR/SUBCONTRACTOR					
WIR No.						CONSTRUCTION- Intelligent Transportation System Works for INSTALLATION AND OPERATION of TRAFFIC SURVEILLANCE (CCTV) SYSTEM-PTZ CAMERAS		HAIF			
ITEM NO.	PROJECT PHASE	TASK / ACTIVITY	Quality Requirements /references/ specifications	Quality Record	INSPECTION RESPONSIBILITY ASSIGNMENTS			REMARKS			
					Contractor	Third Party	Consultant				
1.0 DOCUMENT REVIEW											
1.1		Material Approval & Shop Drawing	QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00005 QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00001-00086	QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00005 QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00001-00086	R		H				
2.0 MATERIAL RECEIVING INSPECTION											
2		Material receiving inspection, protection & storage	QD0002-ADM-TEM-QMS00007[0A] MaterialReceiving Inspection in site HFC-CKL-2001	QD0002-ADM-TEM-QMS00007[0A] MaterialReceivingInspection in site HFC-CKL-2001	H		H	MIR to be submitted			
3.0 WORK INSTALLATION											
3.1		PRE - INSTALLATION	HFC-CKL-2002	HFC-CKL-2002	H		H				
3.2		INSTALLATION	HFC-CKL-2003	HFC-CKL-2003	H		H				
3.3		TESTING	HFC-CKL-2004	HFC-CKL-2004	H		H				
	GENERAL NOTES										
1	Surveillance: QA/QC organization to monitor work in progress without notice from Construction Organization										
2	Witness: QA/QC organization shall be notified of the timing of Inspection or test in advance. However, the inspection or test shall be performed as scheduled if the QA/QC organization representative is not present										
3	Hold: QA/QC organization shall be notified of the timing of inspection or test in advance. Inspection or test shall not be carried out without the QA/QC organization representative in attendance.										
4	If the Main Contractor delegates the assigned responsibility to the Subcontractor, then the Main Contractor will have the same degree of responsibility as assigned to Consultant.										
LEGEND											
H	Hold Point for QC Inspection/ Test				R	Review of Documents					
W	Witness Inspection/T				RH	Review & approval of Documents					
S	Surveillance										
HFC-ITP-020											

Checklist : HFC-CKL-2001	Checklist	APPROVED DATE	DISCIPLINE
Material receiving inspection, protection & storage	HFC-CKL-2001		ITS
PROJECT TITLE: Road Access To Resort Core (RA2RC)			CONTRACTOR/SUBCONTRACTOR
WIR No.	CONSTRUCTION- Intelligent Transportation System Works for INSTALLATION AND OPERATION of TRAFFIC SURVEILLANCE (CCTV) SYSTEM-PTZ CAMERAS		HAIF

ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
1.0	**Material receiving inspection,protection & storage of CONSTRUCTION- Intelligent Transportation System Works for INSTALLATION AND OPERATION of TRAFFIC SURVEILLANCE (CCTV) SYSTEM-PTZ CAMERAS**					
A	Deliver, store, and handle products, using means and methods that will prevent damage, deterioration, and loss, including theft and vandalism. Comply with manufacturer's written instructions.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
B	Delivery and Handling:					
1.0	Schedule delivery to minimize long-term storage at Project site and to prevent overcrowding of construction spaces.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
2.0	Coordinate delivery with installation time to ensure minimum holding time for items that are flammable, hazardous, easily damaged, or sensitive to deterioration, theft, and other losses.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
3.0	Deliver products to Project site in an undamaged condition in manufacturer's original sealed container or other packaging system, complete with labels and instructions for handling, storing, unpacking, protecting, and installing.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
4.0	Inspect products on delivery to determine compliance with the Contract Documents and that products are undamaged and properly protected.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
C	Storage:					
1.0	Provide a secure location and enclosure at Project site for storage of materials and equipment.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
2.0	Store products to allow for inspection and measurement of quantity or counting of units.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
3.0	Store materials in a manner that will not endanger Project structure.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
4.0	Store products that are subject to damage by the elements under cover in a weathertight enclosure above ground, with ventilation adequate to prevent condensation and with adequate protection from wind.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
5.0	Protect foam plastic from exposure to sunlight, except to extent necessary for period of installation and concealment.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
6.0	Comply with product manufacturer's written instructions for temperature, humidity, ventilation, and weather-protection requirements for storage.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
7.0	Protect stored products from damage and liquids from freezing.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				
8.0	Provide a secure location and enclosure at Project site for storage of materials and equipment by Employer's construction forces. Coordinate location with Employer.	project specification QRXP117115-DAH-VORA2R-SPE-INF-Z00000-000001-0H 1.7 PRODUCT DELIVERY, STORAGE AND HANDLING				

Remarks

PM/Contractor			QDC		
Contractor Construction			Third Party (if applicable)		
The work is ready for inspection			Document Reviewed	Work Inspected	Test Records Verified
Name	Signature	Date	Name	Signature	
Contractor QC Inspector			QDC Supervision Consultant		

Form Ref. No. QD002-ADM-TEM-QTY-00003- Rev.0A

Renewable Lighting Factory For Industry L.L.C
Limited Liability Company
CR :1010464201
VAT : 310544184300003

شركة الانارة المتجددة للصناعة ذ.م.م
شركة ذات مسئولية محدودة
السجل التجاري :1010464201
الرقم الضريبي : 310544184300003

Certificate of Compliance

SO- S00426 -2026 RLCO -COC

SO#:	RLCO-S00426	Customer:	شركة تقنيات المرور الامنية
Project :	Qiddiya 2025-TTS-ITS-001	Date:	24-Aug-26
Client Po	POR-2026-0032-1	Delivery Note #:	DN# W/OUT/02576

Renewable Lighting Factory for industries (RLCO) certifies that all the manufacturing stages of this order (RLCO Ref No - RLCO-S00426 & Customer PO# - POR-2026-0032-1) have been carried out as per Approved specifications and drawings.

Item	Item Desc.	Qty (set's)
[PC-FG-OCT-00113]	H.D.G Octagonal Camera Pole 15.0m High, 6.0mm, 7mm thk with Base Plate 550*550*30mm. Painted RAL 7015	2
[PC-FG-OCT-00114]	H.D.G Octagonal ITS Pole 6.1m High, 4.0mm thk with Base Plate 300*300*15mm Painted RAL 7015	7

RMTC Treatability & Verification

Item	MTC - CERTIFICATE REF #	MATRL GRADE	Heat ID	Raw Materials Source (Produced By)
[PC-FG-OCT-00113] - 6mm thk	RE2025070400O&5	ASTM A572/A572M Gr.50	25IR05527400	HBIS GROUP
[PC-FG-OCT-00113] 7mm thk	RE20250704000ss	ASTM A572/A572M Gr.50	25IR05527300	HBIS GROUP
[PC-FG-OCT-00114] 4mm thk	Z3-202406036096830	ASTM A572/A572M Gr.50	24805037	HBIS GROUP

GALVANIZING MTC Traceability & Verification

Delivery Note	Galvanizing test done by	Qty (set's)	Galvanizing Test Report /certificate ref #.	Galvanization Standard
DN -2576	Modern steel coating company	2+7	MSCC/QC/1695	ASTM A123

Powder Coating MTC Traceability & Verification

Delivery Note	Powder Coating test done by	Qty (set's)	PVC Coating Test Report /certificate ref #.	Coating test standard
DN -2576	Renewable Lighting factory Factory RLCO	2+7	RLCO/QC/PCMTC -222	ASTM D522/ ISO 2409 ASTM D2749

Qc Inspector: Jameer Khan

QC Engineer:Karthick Jayakumar

Date: **13-Aug-2026**
Our Ref: **TTSDN-Haif-290726-029**

Delivery Note

To: **HAIF COMPANY** الى:

Ref: **WS045CR-53 (RA2RC – ACCESS ROAD TO RESORT CORE)**

SN	Model No. رقم الموديل	Description الوصـــــف	Unit الوحـدة	Qty الكميـة	Remarks ملاحظـات
MATERIAL SUPPLY (TRAFFIC SIGNALS)					
1		[PC-FG-OCT-00113] H.D.G Octagonal Camera Pole 15.0m High, 6.0mm, 7mm thk with Base Plate 550*550*30mm. Painted RAL 7015	NOS	2	
2		[PC-FG-OCT-00114] H.D.G Octagonal ITS Pole 6.1m High, 4.0mm thk with Base Plate 300*300*15mm Painted RAL 7015	NOS	7	

Delivered By: EHAB BASLA **Date:** **13-08-2026**

Printed Name & Signature

Received By: **Date:**

Printed Name & Signature

Unit No. 38, Building 3990
Anas Bin Malik St., Al Malga District
P.O. Box 13524
6615, Riyadh, Saudi Arabia
E-mail : ttg@traffic-tech.com
Web: www.traffic-tech.com

العليا
الرياض 12241 1
6217 2822
Saudi Arabia
Vat: 311892040800003

MF.W/OUT/02576

Order:	Status:	Scheduled Date:	Project:	Customer Po:
RLCO-S00426	Done	08/13/2026 13:44:40	Qiddiya 2025-TTS-ITS-001	POR-2026-0032-1

PRODUCT	ORDERED	DELIVERED	FROM
[PC-FG-OCT-00113] H.D.G Octagonal Camera Pole 15.0m High, 6.0mm, 7mm thk with Base Plate 550*550*30mm. Painted RAL 7015	unit	2.000000 unit	SC.W/Main Factory (Store)
[PC-FG-OCT-00114] H.D.G Octagonal ITS Pole 6.1m High, 4.0mm thk with Base Plate 300*300*15mm Painted RAL 7015	unit	7.000000 unit	SC.W/Main Factory (Store)

Receiver

Name:	MR EIHAB
Signature:	EHAB
Phone:	055933688
Departure Time:	22/8/2026 8:00 AM

Driver

Name:	~~ZAKARIAH~~ Hazratheerim
Signature:	
Phone:	0505839807
Iqama No:	~~2506493961~~ 2529312346

RLCO QC

+966 11 810 2527
+966 50 557 2062
sales@rlco.com.sa
info@rlco.com.sa
المكتب الرئيسي: الرياض حي الربوة شارع الامير متعب بن عبدالعزيز

CamScanner

合同编号 CONTRACT NO.	1501360021	证明书号 CERTIFICATE NO	RE2025070400055
订货单位 CUSTOMER	河钢股份有限公司邯郸分公司	到站 DESTINATION	新港
收货单位 PURCHASER	河北悦玛物流有限责任公司	车号 TRAIN NO	1651543

邯钢能嘉钢铁有限公司
Hansteel Nengjia Iron&Steel Co.,Ltd.
质 量 证 明 书
CERTIFICATE OF QUALITY

执行标准 EXECUTIVE STANDARD	ASTM A572/A572M-21e1	产品名称 PRODUCT	热轧直发卷	生产许可证号: PRODUCTION LICENSE	

批号 MATERIAL NUMBER	钢种等级 STEEL GRADE	炉号 HEAT No	规格 SIZE mm THICK × WIDTH × LENGTH	数量 QUANTITY	重量 WEIGHT (t)	化学成分 (%) CHEMICAL COMPOSITION % C	Si	Mn	P	S	Als	Nb	V	Ti	Cr	主要缺陷 DEFECTS	生产时间 PRODUCTS DATE
						10-2	10-2	10-2	10-3	10-3	10-3	10-4	10-4	10-3	10-2		
25IR05527200	A572Gr50 一级	50E04658	7 × 1220 × C	1	22.765	18	17	55	9	5	26	1	1	37	2		20250525
25IR05527300	A572Gr50 一级	50E04658	7 × 1220 × C	1	22.850	18	17	55	9	5	26	1	1	37	2		20250525

批号 MATERIAL NUMBER	常规拉伸 TENSILE TEST 方向 *1	温度 *2	屈服强度 YS	抗拉强度 TS	断后伸长EL	屈强比 *3	常规冲击 IMPACT TEST 方向 *1	试样厚度 *4	试验温度 *2	冲击功1 *5	冲击功2 *5	冲击功3 *5	冲击功平均值 *6	金相 MICROSTRUCTURE 铁素体晶粒度 *7	带状组织级别 *8	A粗A HEAVY	A细A THIN	B粗B HEAVY	B细B THIN	C粗C HEAVY	C细C THIN	D粗D HEAVY	D细D THIN	DS	夹杂物总量 *9	弯曲方向	弯心直径	弯曲结果								
		°C	Mpa	Mpa	%			mm	°C	J	J	J	J													*10	*11	*12	*13	*14	*15	*16	*17	*18	*19	*20	*21
25IR05527200	T		441	577	34.0		L	7.50	20	63	83	70	72													T	2a	Qualified								
25IR05527300	T		441	577	34.0		L	7.50	20	63	83	70	72													T	2a	Qualified								

TOTAL: 2 件 WEIGHT(t): 45.615 吨 (t)

备注 REMARK	1、The certificate proved under the examination to meet the contract requirements and technical standards. 2、The steel type, specifications are subjected to the certificate. 3、The quality certificate is available in electronic form. Handwriting, rewriting and no stamping is invalid. 4、Certification in accordance with EN 10204: 2004 3.1 & 2.2 5、Surface quality and shape size of material are all qualified.
注释 REMARKS	

地 址：河北省邯郸市涉县龙西工业园区(邮编ZIPCODE：056400)
ADDRESS:Longxi Industrial Park,Shexian County,Handan City,Hebei Province
证书网址：http://wuliu.hansteel.cn
CERTIFICATE URL

质 量 检 验 负 责 人： 席江涛
PERSON-IN-CHARGE OF QUALITY EXAMINATION: Xi Jiangtao
Tel: (0310)3958393(质量), (0310)3958378(异议)
FAX:

开 证 员： 杨振宁
OPERATOR(SIGNATURE):
开证日期： 20250704
ISSUING DATE:

合同编号 CONTRACT NO.	1501360020	证明书号 CERTIFICATE NO	RE2025070400066
订货单位 CUSTOMER	河钢股份有限公司邯郸分公司	到站 DESTINATION	新港
收货单位 PURCHASER	河北悦玛物流有限责任公司	车号 TRAIN NO	1730476

邯钢能嘉钢铁有限公司

Hansteel Nengjia Iron&Steel Co.,Ltd.

质 量 证 明 书

CERTIFICATE OF QUALITY

执行标准 EXECUTIVE STANDARD	ASTM A572/A572M-21e1	产品名称 PRODUCT	热轧直发卷	生产许可证号: PRODUCTION LICENSE	

批号 MATERIAL NUMBER	钢种等级 STEEL GRADE	炉号 HEAT No	规格 SIZE mm THICK × WIDTH × LENGTH	数量 QUANTITY	重量 WEIGHT (t)	化学成分 (%) CHEMICAL COMPOSITION % C	Si	Mn	P	S	Als	Nb	V	Ti	Cr	主要缺陷 DEFECTS	生产时间 PRODUCTS DATE
						10-2	10-2	10-2	10-3	10-3	10-3	10-4	10-4	10-3	10-2		
25IR05527400	A572Gr50 一级	50E04658	6 × 1220 × C	1	22.795	18	17	55	9	5	26	1	1	37	2		20250525
25IR05527500	A572Gr50 一级	50E04658	6 × 1220 × C	1	22.890	18	17	55	9	5	26	1	1	37	2		20250525

批号 MATERIAL NUMBER	常规拉伸 TENSILE TEST 方向 *1	温度 *2	屈服强度 YS	抗拉强度 TS	断后伸长EL	屈强比 *3	常规冲击 IMPACT TEST 方向 *1	试样厚度 *4	试验温度 *2	冲击功1 *5	冲击功2 *5	冲击功3 *5	冲击功平均值 *6	金相 MICROSTRUCTURE 铁素体晶粒度 *7	带状组织级别 *8	A粗A HEAVY	A细A THIN	B粗B HEAVY	B细B THIN	C粗C HEAVY	C细C THIN	D粗D HEAVY	D细D THIN	DS	夹杂物总量 *9	弯曲方向	弯心直径	弯曲结果	主要缺陷 DEFECTS	生产时间 PRODUCTS DATE
		℃	Mpa	Mpa	%			mm	℃	J	J	J	J													*10	*11	*12	*19	*20	*21
25IR05527400	T		466	588	33.5		L	5.00	20	56	57	56	56													T	2a	Qualified			
25IR05527500	T		466	588	33.5		L	5.00	20	56	57	56	56													T	2a	Qualified			

TOTAL: 2 件 WEIGHT(t): 45.685 吨 (t)

备注 REMARK	1、The certificate proved under the examination to meet the contract requirements and technical standards. 2、The steel type, specifications are subjected to the certificate. 3、The quality certificate is available in electronic form. Handwriting, rewriting and no stamping is invalid. 4、Certification in accordance with EN 10204: 2004 3.1 & 2.2 5、Surface quality and shape size of material are all qualified.
注释 REMARKS	

地 址：河北省邯郸市涉县龙西工业园区(邮编ZIPCODE：056400)
ADDRESS:Longxi Industrial Park,Shexian County,Handan City,Hebei Province
证书网址：http://wuliu.hansteel.cn
CERTIFICATE URL

质 量 检 验 负 责 人： 席江涛
PERSON-IN-CHARGE OF QUALITY EXAMINATION: Xi Jiangtao
Tel：(0310)3958393(质量)，(0310)3958378(异议)
FAX:

开 证 员： 杨振宁
OPERATOR(SIGNATURE):
开证日期： 20250704
ISSUING DATE:

合同编号：CONTRACT No. 0010367567

规格(mm)：DIMENSION 4*1219

标准：SPECIFICATION AS7M A572/A572M-21e1

订货单位：CUSTOMER 唐山钢铁集团有限责任公司

收货单位：PURCHASER 一票制-唐山钢铁集团股份有限公司（曹妃甸通用码头-泽仁货代）

河钢股份有限公司唐山分公司
HBIS COMPANY LIMITED TANGSHAN BRANCH

质量证明书
QUALITY CERTIFICATE

产品名称：热轧钢带
PRODUCT: Hot-rolled steel strip

质量记录编号：TAB OF QUALITY TG-ZLZMS-202

系统编号：SYSTEM No. 0080330679 000050

总重量(t)：TOTAL WEIGHT 48.38

车号：TRAIN No. 冀B13033D

证明书号：CERTIFICATE No. Z3-202406036096830

炉号 HEAT No.	板坯号 SLAB No.	卷号 COIL No.	牌号 GRADE	重量 WEIGHT (t)	化学成分 (%) CHEMICAL COMPOSITION																生产日期 DATE
					C	Si	Mn	P	S	Als	As	Cev	Cr	Cu	Mo	N	Nb	Ni	PCM	Ti	V	
24B05037	24B05037B30	24603CL4310	Grade50	24.36	0.18	0.15	0.80	0.019	0.002	0.033	0.002	0.32	0.02	0.01	0.00	0.0034	0.00	0.01	0.23	0.001	0.00	2024-06-03
24B05037	24B05037A40	24603CL4300	Grade50	24.02	0.18	0.15	0.80	0.019	0.002	0.033	0.002	0.32	0.02	0.01	0.00	0.0034	0.00	0.01	0.23	0.001	0.00	2024-06-03

炉号 HEAT No.	板坯号 SLAB No.	卷号 COIL No.	拉伸试验(横向) TENSILE TEST(TRANSVERSE SAMPLE)				弯曲试验(横向) BEND TEST(TRAN	冲击试验 IMPACT TEST				晶粒度 GRAIN SIZE	带状组织 BANDED STRUCTURE	硬度 HARDNESS	平均极限扩孔率 AVERAGE LIMITING HOLE EXPANSION RATIO
			抗拉强度 T.S.(MPa) R_m	屈服强度 Y.S.(MPa) R_{eL}	伸长率 EL.(%) A_{50mm}	屈强比 RATIO R_{eL}/R_m	180° 弯曲 B.T. d=2.0a	冲击吸收能(J)(℃) IMPACT ABSORBED ENERGY 冲击试样尺寸(mm) SIZE OF SAMPLE			平均值 AVG				
								单值 SINGLE							
24B05037	24B05037B30	24603CL4310	546	408	28.0		合格								
24B05037	24B05037A40	24603CL4300	546	408	28.0		合格								

注释 NOTE Y.S.=YIELD STRENGTH T.S.=TENSILE STRENGTH EL.=ELONGATION B.T.=BEND TEST

备注 REMARKS
1.无质量证明章无效。 Effective with quality prove seal.
2.兹证明本产品根据相应标准和规范进行制造和检验。
We certify that the products have been produced and inspected according to standard and agreement.
3.尺寸、表面合格。 Dimensions, tolerances on dimensions and surface appearance are in accordance with standard.

交货状态：热轧 DELIVERY CONDITION HOT ROLLING

质量证明章 QUALITY PROVE SEAL

5

地址：ADD: 中国河北唐山市乐亭经济开发区 Laoting Economic Development Zone Tangshan Hebei China

URL: www.tangsteel.com.cn

销售电话：SALES TEL +86 0315-2705733 打印人：PRINTER

售后服务电话：AFTER-SALES SERVICE TEL +86 0315-5810896

打印日期：PRINT DATE

发货日期：DELIVERY DATE 2024-06-0

شركة تغليف الحديد العصرية
Modern Steel Coating Co.
رقم الضريبة المضافة ٣٠٠٤٦٥٧٨٧١٠٠٠٠٣

HOT DIP GALVANIZING INSPECTION CERTIFICATE

This Certificate is issued to RENEWABLE LIGHTING FACTORY FOR INDUSTRY L.L.C .

Customer Name	RENEWABLE LIGHTING FACTORY FOR INDUSTRY L.L.C .				
Total Quantity	18	Customer Job #		Report No.	MSCC/QC/ 1695
Min. DFT Req.	AS PER TAB-01-ASTM 123-24	Temperature°C	450	Inspection Date	12-Jul-2026
Applicable Std.	ASTM A 123 / 12-SAMSS 007			Elcometer-456 Serial No.SH13906	

We hereby Certify that the steel articles mentioned herein below have been galvanized, sampled and inspected in accordance with Standard ASTM A123 - 2024 : Zinc Coating on Iron and Steel Products.

Material Details

Sr. #	Description	Qty (Pcs)	Sr. #	Description	Qty (Pcs)
1	[PC -FG-OCT-00114] H.D.G O cctagonal ITS Pole 6.1 m High , 4.0mm thk with Base plate 300*300*15mm painted RAL 7015	14			
2	[PC -FG-OCT-00113] H.D.G O cctagonal Camera Pole 15.0 m High , 6.0mm ,7mm thk with Base plate 550*550*30mm painted RAL 7015	4			

Inspection and Test Details

1. VISUAL INSPECTION

Inspection Description	Inspection Results	
	Yes	Remarks
1. Bare Spots	-	Within Std.
2.Roughness	-	Within Std.
3.White Rust	-	Within Std.
4. Ash Inclusions	-	Within Std.

Inspection Description	Inspection Results		
	Yes	No	Remarks
5.Lumpiness & Runs	-	✓	Within Std.
6.Dross Inclusions/Pimples	-	✓	Within Std.
7.Flux Inclusions/Stains	-	✓	Within Std.
8.Dull Gray	-	✓	Within Std.

2. ADHESION TEST RESULTS (STOUT KNIFE)

Sample #	Result	Remarks
As below Sample	Satisfactory	Passed

3. COATING THICKNESS MEASUREMENTS (in Microns)

Part / Sample #	1	2	3	4	5	Average	Remarks
[PC -FG-OCT-00114] H.D.G O cctagonal ITS Pole 6.1 m High , 4.0mm thk with Base plate 300*300*15mm painted RAL 7015	100	111	106	105	108	104	Acceptable
[PC -FG-OCT-00113] H.D.G O cctagonal Camera Pole 15.0 m High , 6.0mm ,7mm thk with Base plate 550*550*30mm painted RAL 7015	98	107	94	110	103	102	Acceptable
	91	102	90	93	105	98	Acceptable

Tested / Inspected by:	Reviewed / Approved by	Reviewed by:	Reviewed by:
QC Inspector / Engineer	Quality Manager	Customer-QC	Customer / TPI (If applicable)

س.ت ٢٠٥٠٠٧٩٧٥١ – هاتف : ٠١٣٨١٢٠٤٣٩ – فاكس تحويلة ٢٢ – ص.ب ٣٤٩ – الدمام ٣٤٣٣٣ – المملكة العربية السعودية
C.R. 2050079751-Tel: 0138120439-Fax, Ext. 22-P.O. Box 349-Dammam 34333-Kingdom of Saudi Arabia
abdelfattah.nassar@modernsteelcoating.com - www.modernsteelcoating.com

RLCO Renewable Lighting Factory For Industry L.L.C شركة مصنع الإنارة المتجددة للصناعة ذ.م.م	**Coating/Painting -Inspection QC-Lab test report**	Form No.	RLCO/QC/EPC-01
		Rev.No	01
		Issue Date	25.April.2023

SO#	RLCO-S00426	Delivery note#	2576
Client:	Traffic Tech	Certificate #:	RLCO/QC/PCMTC -222
PO#	POR-2026-0032-1	Project:	Qiddiya 2025-TTS-ITS-001

Item description:

[PC-FG-OCT-00113] H.D.G Octagonal Camera Pole 15.0m High, 6.0mm, 7mm thk with Base Plate 550*550*30mm. Painted RAL 7015
[PC-FG-OCT-00114] H.D.G Octagonal ITS Pole 6.1m High, 4.0mm thk with Base Plate 300*300*15mm Painted RAL 7015

No	Characteristics	Required specifications	Observation	Standards/test method	Inspection Method	Acceptence Pass/Fail
1	Surface preparation	Surface roughness	Rughness 20	ASTM D4417	Elcometer	Passed
2		Surface cleanlines (Free of dirt,oxidation,oil, etc.)	Observed ok	SSPC/SP-16	visual	Passed
3	Coating color to std	RAL - 7015	RAL 7015	As per RAL Color Std	visual	Passed
4	Curing condition	180°c - 220°.c for 10 to 20mins	Process control			Passed
5	Gloss	Matt	Matt	EN ISO2813(60')	Reflectometer/ visual	Passed
6	Adhesion test	No delamination	No delamination	ISO 2409/ASTM D3359	Cross cut tape test	Passed
7	Impact resistance test	>24 inch ibs/No crack or delamination	No Crack	ASTM D2794	5/8"ball/Hammer test	Passed
8	Coating DFT	Min Microns	Avg DFT 160 microns	ASTM D7091	visual	Passed
9	Appearance	Coating should be uniform, free of defects, like sagging, pinholes, scratches,damages etc,	Observed ok	-	visual	Passed

Records :

S.No.	Prepared by		Approved by		Date	
	QC Inspector		QC Engineer		2-Aug-26	

رقم طلب الشراء: POR-2026-0032-1
الرقم الضريبي: 3116624281
العنوان: P.O. Box 3782-315, Riyadh 14548, Kingdom of Saudi Arabia
Riyadh

خطاب ضمان

We Renewable Lighting Factory for Industry with CR No. 1010464201, guarantee that all products supplied by us are free from any manufacturing defects that may affect the quality of the product and that these materials are manufactured according to the standard specifications. The following table shows the details of the warranty:

نحن شركة مصنع الإنارة المتجددة للصناعة بسجل تجاري رقم 1010464201، نضمن أن جميع المنتجات التي تم توريدها من قبلنا خالية من أي عيوب تصنيعية قد تؤثر على جودة المنتج وأن هذه المواد مصنعة وفقًا لـ المواصفات القياسية.

والجدول التالي يوضح تفاصيل الضمان:

Warranty Period مدة الضمان	Quantityالكمية	Description الوصف
10 سنوات 10 Years	7	HDG Octagonal ITS Pole 6.1 m High, 4.0mm Thk with Base Plate 300x300x15mm

- يلزم التحقق من الوثيقة عبر الرابط التالي https://mybusiness.chamber.sa/ او تطبيق (بوابة أعمالي)
للهواتف الذكية دون أدنى مسؤولية على الغرفة التجارية عن محتوى الوثيقة.
- تعتبر هذه الوثيقة مصدقة من غرفة الرياض ولا تحتاج الى توقيع او ختم.
- عند التعديل على الوثيقة او محاولة العبث بها تعتبر لاغية وتعرض صاحبها للمسألة القانونية.

الخدمات الإلكترونية E-SERVICES
E-Services Riyadh Chamber © الخدمات الإلكترونية لغرفة الرياض - بوابة أعمالي
920004565
RIYADH EXPO 2030

رابط التحقق : https://mybusiness.chamber.sa/verify/verifyopenletter.aspx?transkey=f4c033b1-3c92-463e-976d-c52e86cc99dd

غرفة الرياض
Riyadh Chamber
بوابة أعمالي - خدمات التصديق الإلكتروني

رقم الوثيقة :
28320740

HDG Octagonal Camera Pole 15.0 m High, 6.0mm, 7mm, Thk with Base Plate 550x550x30mm	2	10 سنوات 10Years

لا يمكن قبول مطالبة الضمان للأسباب التالية:

- التعامل غير السليم مع البضائع الموردة أثناء التفريغ.
- الأضرار الناجمة عن ملامسة المواد الكيميائية والأسمدة والمياه التي تحتوي على عوامل مسببة للتآكل
- أي ضرر ناتج عن الحوادث (قوى خارجية، تأثيرات)، إساءة استخدام، سوء استخدام في الموقع
- عدم تنظيف الألواح الشمسية (شهرياً)
- الشروط والاحكام:

- 1-يبدأ الضمان من تاريخ تسليم المواد في الموقع13\8\2026
- 2-يطلب من العميل ارجاع البضائع التي يوجد فيها أضرار أو أعطال إلى مصنع RLCO للمراجعة وفحص سبب العطل.
- 3-يجب إبلاغ RLCO كتابيا بأي أوجه قصور في غضون أسبوع من اكتشاف العطل.
- 4-يتم تطبيق الضمان على البضائع الموردة عند استلام جميع المبالغ المستحقة من السلع المباعة.
- 5-يجب إعادة البضائع التالفة إلى المصنع . والمصنع غير مسؤول عن تكاليف النقل.
- 6-تقع مسؤولية استلام المواد واعادة التركيب على العميل بالكامل.

:The warranty claim cannot be accepted for the following reasons

- .Improper handling of the supplied goods during unloading 13\8\2026
- Damage caused by contact with chemicals, fertilizers and water containing corrosive agents
- Any damage caused by accidents (external forces, impacts), misuse, misuse on site
- Failure to clean the solar panels (monthly)

:Terms and Conditions

- The warranty starts from the date of delivery of the materials-1
- The customer is requested to return the goods that have damages or malfunctions to-2 .RLCO factory for review and examination of the cause of the malfunction
- Any Issues must be reported to RLCO in writing within a week of discovering the-3 .malfunction
- The warranty is applied to the supplied goods upon receipt of all amounts due from the-4 .sold goods
- Damaged goods must be returned to the factory. The factory is not responsible for-5 .transportation costs
- .The customer is fully responsible for receiving the materials and re-installing-6

الخدمات الإلكترونية E-SERVICES
E-Services Riyadh Chamber © الخدمات الإلكترونية لغرفة الرياض - بوابة أعمالي
920004565
RIYADH EXPO 2030

- يلزم التحقق من الوثيقة عبر الرابط التالي https://mybusiness.chamber.sa/ او تطبيق (بوابة أعمالي) للهواتف الذكية دون أدنى مسؤولية على الغرفة التجارية عن محتوى الوثيقة.
- تعتبر هذه الوثيقة مصدقة من غرفة الرياض ولا تحتاج الى توقيع او ختم.
- عند التعديل على الوثيقة او محاولة العبث بها تعتبر لاغية وتعرض صاحبها للمسألة القانونية.

رابط التحقق : https://mybusiness.chamber.sa/verify/verifyopenletter.aspx?transkey=f4c033b1-3c92-463e-976d-c52c86cc99dd

غرفة الرياض
Riyadh Chamber
بوابة أعمالي - خدمات التصديق الإلكتروني

رقم الوثيقة :

28320740

محرره : السيد نصرالله فتحي مصطفى الاردني صفته :مدير عام

- يلزم التحقق من الوثيقة عبر الرابط التالي https://mybusiness.chamber.sa/ او تطبيق (بوابة أعمالي) للهواتف الذكية دون أدنى مسؤولية على الغرفة التجارية عن محتوى الوثيقة.
- تعتبر هذه الوثيقة مصدقة من غرفة الرياض ولا تحتاج الى توقيع او ختم.
- عند التعديل على الوثيقة او محاولة العبث بها تعتبر لاغية وتعرض صاحبها للمسألة القانونية.

الخدمات الإلكترونية
E-SERVICES
الخدمات الإلكترونية لغرفة الرياض - بوابة أعمالي © E-Services Riyadh Chamber
920004565


RIYADH EXPO 2030

رابط التحقق : https://mybusiness.chamber.sa/verify/verifyopenletter.aspx?transkey=f4c033b1-3c92-463e-976d-c52c86cc99dd


1. ITS poles shall be in accordance with the poles manufacturer's recommendations.
2. Galvanization & Compliance certificates with the standards to be provided
3. For other comments refer to drawing #QRXM114000-HFC-DRW-SDW-ITS-02-R05-00024

B: Approved with Comments
comments overleaf/attached


Zuhair Fayez Partnership Consultants
Riyadh - Saudi Arabia

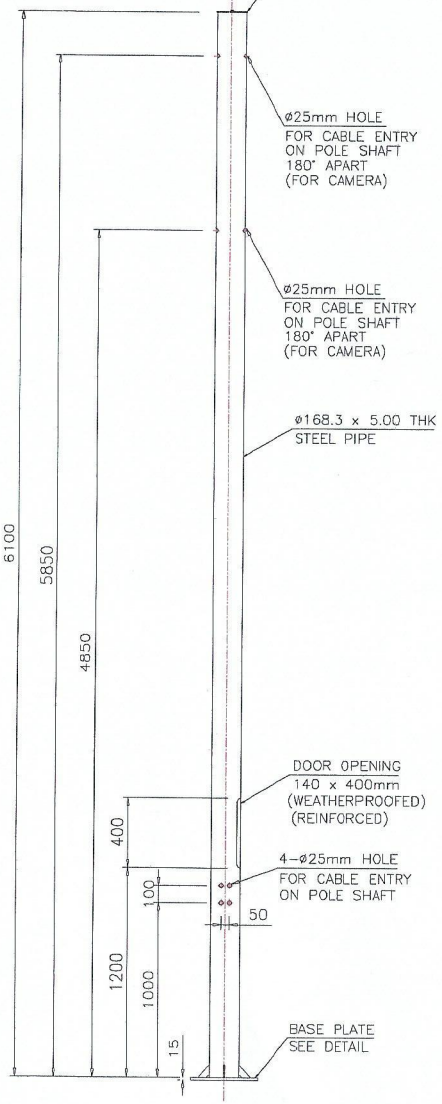


ITS POLE - 6.1M

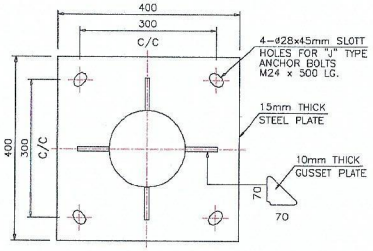

BASE PLATE DETAIL




ANCHOR BOLT DETAIL

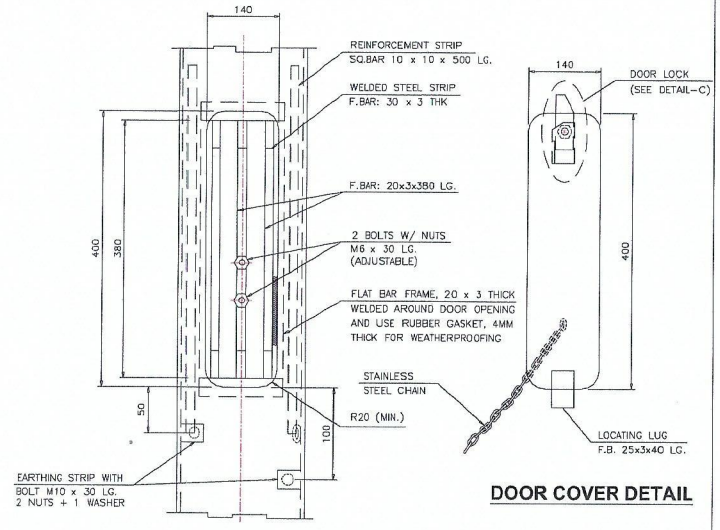


DOOR OPENING DETAIL


DOOR COVER DETAIL



BASE PLATE/ SHAFT WELDING DETAIL



DETAIL - C (DOOR LOCK)

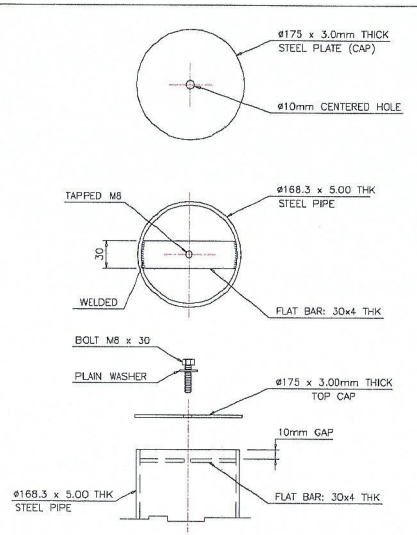

TOP CAP DETAIL

NOTES:


1. ALL DIMENSIONS ARE IN MILLIMETERS.
2. FINISH HOT DIPPED GALVANIZED IN ACCORDING TO ASTM A123.
3. MATERIAL SPECIFICATION :
   3.1 PIPE : ASTM A500 G-A OR EQUIV.
   3.2 OTHERS = ASTM A36, GRADE 36, OR EQUIV.
4. DESIGN : B.S. EN 40-3
5. DESIGN WIND SPEED : 160 KM/HR.
6. FOUNDATION DESIGN TO BE PROVIDED IN SEPARATE SUBMISSION

Qiddiya

Consultant's information

HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com


Zuhair Fayez Partnership



Notes:
1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3. THIS DRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.

REFERENCE I.F.C DESIGN DRAWING NO:
1. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002
2. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000001
3. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000002
4. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000005
5. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000006
6. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000001
7. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000002
8. QRXP117115-DAH-VORA2R-DWG-ICT-R3-Z00000-2000000

LEGEND:



Rev. No.	Date	Description	Appr.
00	04-11-2025	FOR REVIEW AND APPROVAL	--
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--

Consultant
Contractor
Hail Company
ITS Contractor
TRAFFIC TECH
Project:
Qiddiya

Job title: Road Access To Resort Core


Drawing title: SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-2
TYPICAL ITS POLE DETAILS - 6.1M

Sheet number: SHEET 19 / 19


Scale: NTS

Drawn: M.Sayed | Checked: M.Sayed
Designed: | Approved:


Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-R05-00066
Revision: 00

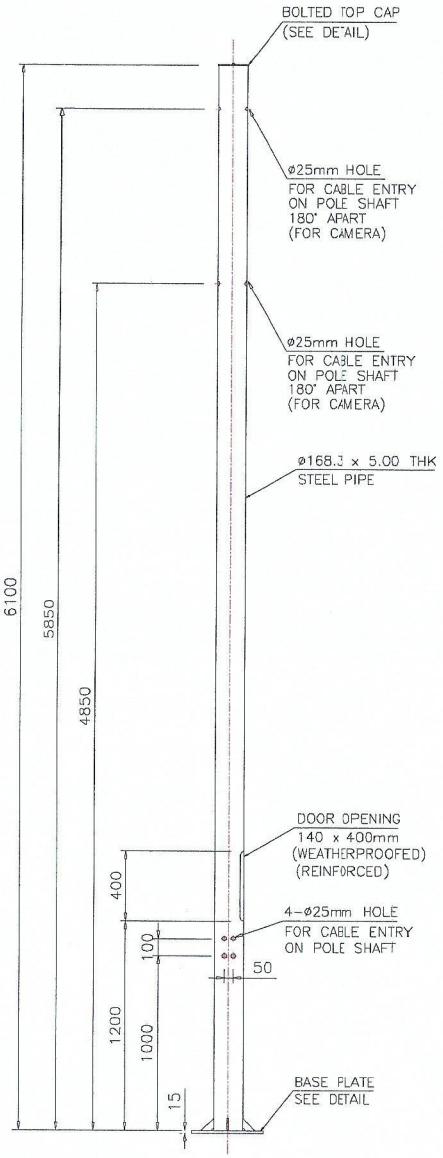


ITS POLE - 6.1M

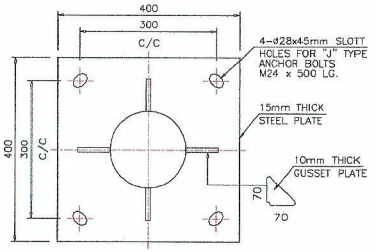

BASE PLATE DETAIL




ANCHOR BOLT DETAIL

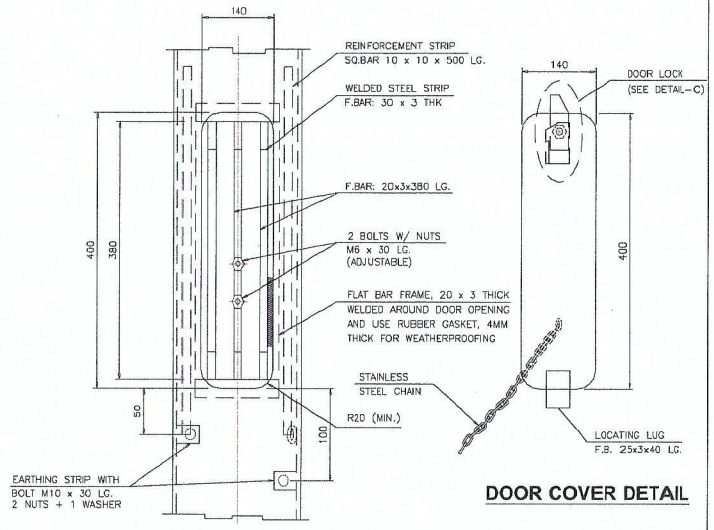


DOOR COVER DETAIL

DOOR OPENING DETAIL


1.ITS poles shall be in accordance with the pole manufacturer's recommendations.
2. Galvanization & Compliance certificates with the standards to be provided
3. For other comments refer to drawing #QRXM114000-HFC-DRW-SDW-ITS-02-ROS-00015



BASE PLATE/ SHAFT WELDING DETAIL



DETAIL - C (DOOR LOCK)

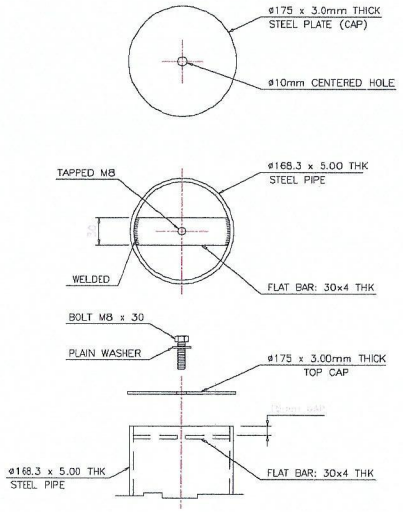

TOP CAP DETAIL

NOTES:

1. ALL DIMENSIONS ARE IN MILLIMETERS.
2. FINISH HOT DIPPED GALVANIZED IN ACCORDING TO ASTM A123.
3. MATERIAL SPECIFICATION :
   3.1 PIPE : ASTM A500 G-A OR EQUIV.
   3.2 OTHERS = ASTM A36, GRADE 36, OR EQUIV.
4. DESIGN : B.S. EN 40-3
5. DESIGN WIND SPEED : 160 KM/HR.
6. FOUNDATION DESIGN TO BE PROVIDED IN SEPARATE SUBMISSION

القديـة
Qiddiya

Consultant's information

HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com

Zuhair Fayez Partnership



Notes:
1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3. THIS DRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.


REFERENCE I.F.C DESIGN DRAWING NO:
1. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000001
2. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000001
3. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000005
4. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000006
5. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000001
6. QRXP117115-DAH-VORA2R-DWG-ICT-R3-Z00000-2000000

LEGEND:




Rev. No.	Date	Description	Appr.
00	06-10-2025	FOR REVIEW AND APPROVAL	B
01	04-11-2025	FOR REVIEW AND APPROVAL	--
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--


Consultant | Project:
Contractor: Hail Company
ITS Contractor: TRAFFIC TECH
Job title: Road Access To Resort Core
Drawing title: SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-1
TYPICAL ITS POLE DETAILS - 6.1M
Sheet number: SHEET 18 / 18
Scale: NTS
Drawn: M.Sayed | Checked: M.Sayed
Designed: | Approved:
Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-ROS-00056
Revision: 01

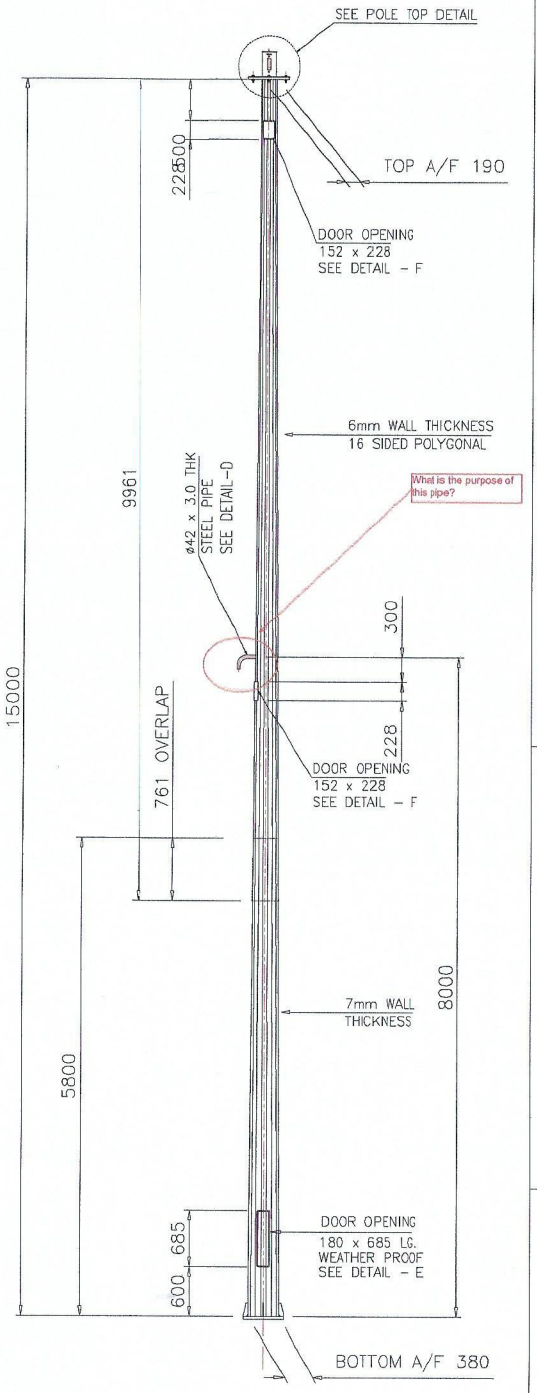


ITS POLE - 15M




TEMPLATE / ANCHOR PLATE




ANCHOR BOLT DETAIL




BASE PLATE DETAIL




DETAIL - B
TENON BASE

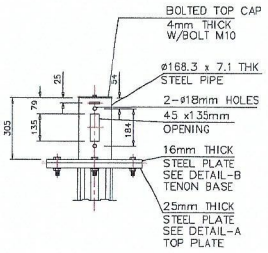


POLE TOP DETAIL




DETAIL - A



PLAN




DETAIL - C




DETAIL - D


1.ITS poles shall be in accordance with the pole manufacturer's recommendations.
2. Submmission & Compliance certificates with the standard to be provided
3. For other commentes refer to drawing #QRXM114XX-HFC-DRW-SDW-ITS-02-R05-00055

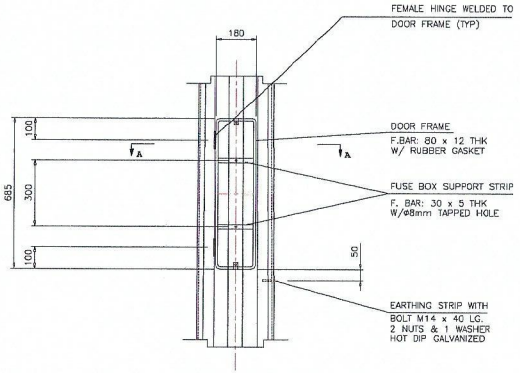


DETAIL - E
DOOR OPENING DETAIL

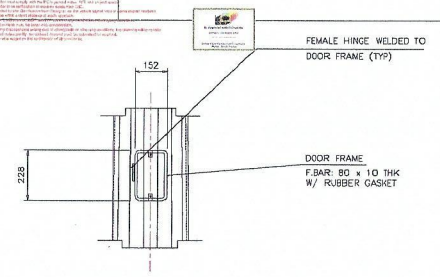

DETAIL - F
DOOR OPENING DETAIL



SECTION A-A



DETAIL - Y


NOTES:
1. ALL DIMENSIONS ARE IN MILLIMETERS.
2. FINISH HOT DIPPED GALVANIZED IN ACCORDANCE TO ASTM A123. FOR STRUCTURE, ASTM 153 FOR HARDWARE
3. MATERIAL SPECIFICATION : ASTM A36 GRADE 36 OR EQUIV.
   3.1 MAST SHAFT & ANCHOR BOLTS = STEEL GRADE Fe 510C TO EN 10025 OR EQUIV.
   3.2 BASE PLATE = STEEL GRADE Fe 510C TO EN 10025 OR EQUIV.
   3.3 OTHERS = ASTM A36 GRADE 36 OR EQUIV.
4. DESIGN : B.S. EN 40-3
5. DESIGN WIND SPEED : 160 KM/HR.
6. FOUNDATION DESIGN TO BE PROVIDED IN SEPARATE SUBMISSION.

القديه
Qiddiya

Consultant's information

HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com


Zuhair Fayez Partnership



Notes:
1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3. THIS DRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.

REFERENCE I.F.C DESIGN DRAWING NO:
1. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000001
2. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000001
3. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000005
4. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000006
5. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000001
6. QRXP117115-DAH-VORA2R-DWG-ICT-R3-Z00000-2000000

LEGEND:



Rev. No.	Date	Description	Appr.
00	06-10-2025	FOR REVIEW AND APPROVAL	B
01	04-11-2025	FOR REVIEW AND APPROVAL	
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--

Consultant
Contractor
Hail Company
ITS Contractor
TRAFFIC TECH

Project:
القديه
Qiddiya

Job title: Road Access To Resort Core


Drawing title:
SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-1
TYPICAL ITS POLE DETAILS - 15M

Sheet number:
SHEET 17 / 18


Scale: NTS

Drawn: M.Sayed | Checked: M.Sayed
Designed: | Approved:


Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-R05-00055
Revision: 01

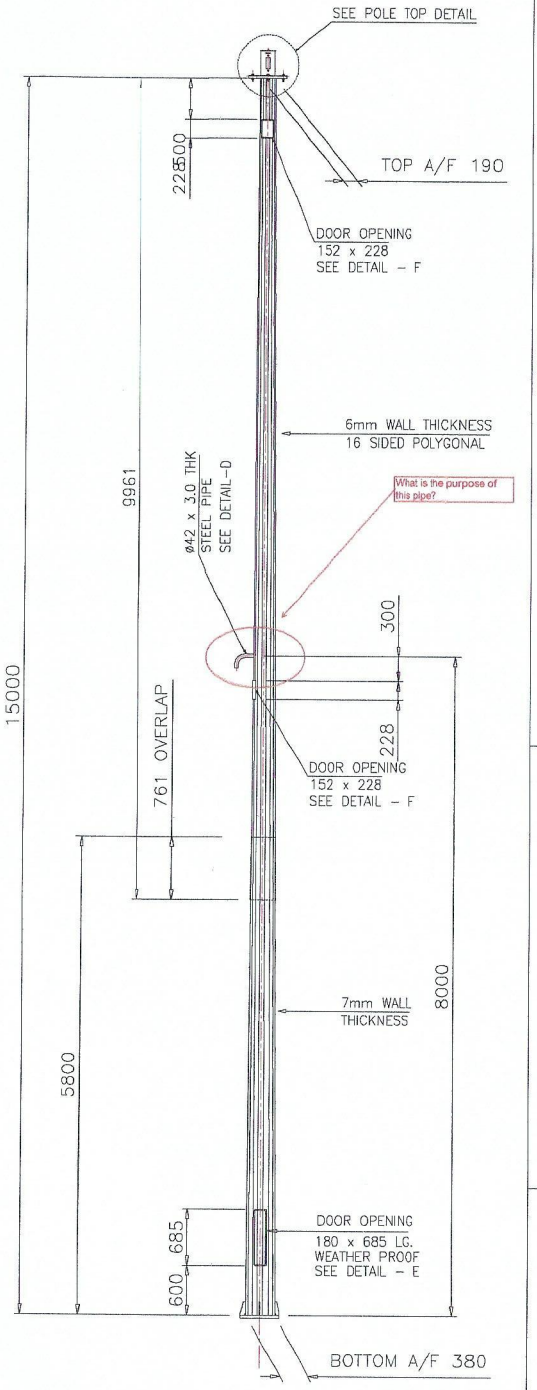


ITS POLE -15M




TEMPLATE / ANCHOR PLATE




ANCHOR BOLT DETAIL




BASE PLATE DETAIL




DETAIL - B
TENON BASE

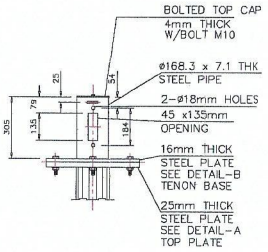


POLE TOP DETAIL




DETAIL - A




PLAN




DETAIL - C




DETAIL - D

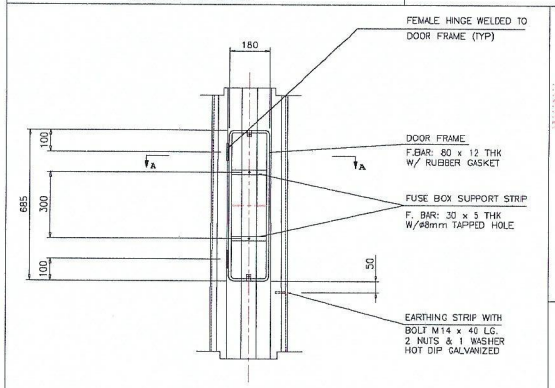


DETAIL - E
DOOR OPENING DETAIL

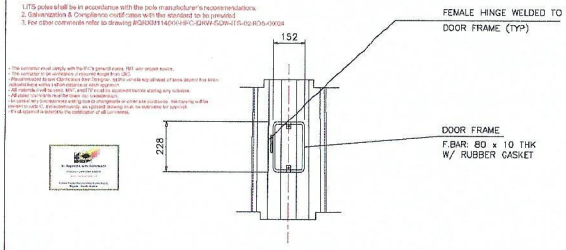

DETAIL - F
DOOR OPENING DETAIL



DETAIL - Y



SECTION A-A


NOTES:
1. ALL DIMENSIONS ARE IN MILLIMETERS.
2. FINISH HOT DIPPED GALVANIZED IN ACCORDANCE TO ASTM A123. FOR STRUCTURE, ASTM 153 FOR HARDWARE
3. MATERIAL SPECIFICATION : ASTM A36 GRADE 36 OR EQUIV.
   3.1 MAST SHAFT & ANCHOR BOLTS = STEEL GRADE Fe 510C TO EN 10025 OR EQUIV.
   3.2 BASE PLATE = STEEL GRADE Fe 510C TO EN 10025 OR EQUIV.
   3.3 OTHERS = ASTM A36 GRADE 36 OR EQUIV.
4. DESIGN : B.S. EN 40-3
5. DESIGN WIND SPEED : 160 KM/HR.
6. FOUNDATION DESIGN TO BE PROVIDED IN SEPARATE SUBMISSION.

القديه
Qiddiya

Consultant's information

HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com

Zuhair Fayez Partnership



Notes:
1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3. THIS DRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.

REFERENCE I.F.C DESIGN DRAWING NO:
1. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002
2. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000001
3. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000002
4. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000005
5. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000006
6. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000001
7. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000002
8. QRXP117115-DAH-VORA2R-DWG-ICT-R3-Z00000-2000000

LEGEND:

Rev. No.	Date	Description	Appr.
00	04-11-2025	FOR REVIEW AND APPROVAL	--
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--

Consultant

Contractor
Hail Company

ITS Contractor
TRAFFIC TECH

Project:
القديه Qiddiya

Job title: Road Access To Resort Core

Drawing title:
SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-2
TYPICAL ITS POLE DETAILS - 15M

Sheet number:
SHEET 18 / 19

Scale:NTS

Drawn: M.Sayed | Checked: M.Sayed
Designed: | Approved:

Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-R05-00065
Revision: 00



