| QIDDIYA DEVELOPMENT COMPANY | | | | | | |
|---|---|---|---|---|---|---|
| DOCUMENT NUMBER: | QDC-ADM-TEM-QMS-00007 | REVISION NUMBER: | 00 | ISSUED BY: | PMO | Qiddiya |
| DOCUMENT TITLE | MIR FORM | DOCUMENT TYPE: | FORM | DATE ISSUED: | MAY-08-2022 | |

# MATERIAL INSPECTION REQUEST (MIR) FORM

| | |
|---|---|
| Contractor: | HAIF COMPANY |
| Project: | QPMO-410-CT-00618- ROAD ACCESS TO RESORT CORE |
| Contract No.: | QI09043311-VO-0004 |
| Material Inspection Request Number: | QRXM114000-HFC-TEC-MIR-ITS-02-RO5-00024 |

شركة حيف Haif Company | Freyssinet | HAIF-FREYSSINET JV

**Discipline**

| | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|
| Architecture | ☐ | Mechanical | ☐ | Information Technology | ☑ | Quality | ☐ | Project Controls | ☐ |
| Civil/Structural | ☐ | Electrical | ☐ | Landscape | ☐ | Safety | ☐ | Construction Management | ☐ |
| Other | ☐ | | | | | | | | |

**MATERIAL DESCRIPTION**

| | | | |
|---|---|---|---|
| Inspection / Test Location: | INTERIM ROAD MAIN LINE-02 | | |
| Material Name: | ATMS | Quantity: | 01 Nos. |
| P.O Number | | Delivery Note Number: | TTSDN-HAIF-290726-032 |
| Approved Material Transmittal Number: (Aconex document Approval) | QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00003 | Approval Date: | |
| Inspection Date: | 20-Oct-2026 | Inspection Start Time: | 10:00 AM |
| ITP: | QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00001 | Checklist: | HFC-CKL-7001 |
| Spec's / Dwg. Ref.: | TRAFFIC TECH SECURITY W.L.L | Approved Method Statement Number: | |
| Attachments: | Test Certificate: ◉ Yes ○ No<br>IFC / Shop Drawings: ○ Yes ◉ No | | |

**DESCRITPTION OF MATERIAL**

Advanced Transportation Management System (ATMS) GUI - Based Enterprise Server Traffic Software Solution ( 01 NOS. )
Interim Road Main Line-02

**CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:**

| | | | |
|---|---|---|---|
| Are Complete Details Mentioned in P.O and Delivery Note? | ◉ YES ○ NO | REMARKS | |
| Complies with Approved ITPs/Checklists? | ◉ YES ○ NO | REMARKS | |
| Signs of Physcial Damage? | ○ YES ◉ NO | REMARKS | |
| Conforms to Approved Material Submittal? | ○ YES ○ NO | REMARKS | |

| | |
|---|---|
| Accepted: | ◉ |
| Accepted with Comments: | ○ |
| Rejected (See Remarks): | ○ |

| | | | | | |
|---|---|---|---|---|---|
| REMARKS: | | | | | |
| Name: | Moataz Elkhateeb | Signature: | | Date: | 20-10-2026 |

**QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:**

| | | | |
|---|---|---|---|
| Contractor Has complied with Material requirements? | ○ YES ○ NO | Materials Are Stored correctly? | ○ YES ○ NO ○ NA |

| | |
|---|---|
| Accepted: | ○ |
| Accepted with Comments: | ○ |
| Rejected (See Remarks): | ○ |

| | | | | | |
|---|---|---|---|---|---|
| REMARKS: | | | | | |
| Name: | | Signature: | | Date | |

**FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.**
**CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.**

This document is the property of Qiddiya Development Company, 2022

| Client: | Consultant: | Contractor: |
|---|---|---|
| Qiddiya | Zuhair Fayez Partnership | Haif Company / Freyssinet — HAIF-FREYSSINET JV |

# TECHNICAL DOCUMENTS

| | |
|---|---|
| **Project Name:** Package 3 - **Interim Road Access to Resort Core** | **Project Code:** QRXM114000 |
| **Location:** 00 | **Date:**18-October2025 |
| Document Title:**Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (ATMS)** | **Ref No:** QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00003 |
| | **Rev No:** 00 |

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☑ ITS ☐ Civil

Type: ☐ Pre-Qualification ☐ Method Statement ☒ Material Submittal ☐ Sample ☐ Other

Document Description:Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (ATMS)

| Doc. Ref. No. | Title |
|---|---|
| QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00003 | **Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (ATMS)** |

Enclosure:

| **Submitted By:** | **Received By:** |
|---|---|
| Name: **Eng. Moataz**<br>Signature:<br>Date:18-October2025 | Name:<br>Signature:<br>Date: |

**Below portion for Consultant Supervision use only**

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments:

B: Approved with Comments — Zuhair Fayez Partnership Consultants, Riyadh , Saudi Arabia

~~This is a conditional approval, subject to compliance with the following comments, project specification and QIC acceptance.~~

1.The ~~DMV Control Center shall support NTCIP protocols and shall be compliant with ONVIF standards for~~ interoperability with ITS field devices and CCTV systems

2.How many CCTV cameras, DMS, vehicle detection cameras, RFID detectors, and other ITS equipment can DMV control center manage?

3. Is it scalable to control more ITS equipment in the future apart from current project scope?

4.Provide at least three user official references with a minimum one year of performance experience.

5.~~Does the DMV Control Center operate on a local license, allowing access for multiple government~~ agencies and locations?

6.Is it ~~independently licensed with no expiration and no online verification required?~~

7.Ensure that all ITS subsystems listed in the project BOQ can be integrated with the DMV control system, and ~~indicate other systems that can also be integrated~~

8.How many simultaneous users can the system support without performance degradation, and can it be ~~scaled in the future to accommodate more users?~~

**Below portion for Client use only**

B: Approved with Comments — Zuhair Fayez Partnership Consultants, Riyadh , Saudi Arabia

Signed by: Signature: Date:

| Client: | Consultant: | Contractor: |
|---|---|---|
| Qiddiya | Zuhair Fayez Partnership | Haif Company / Freyssinet — HAIF-FREYSSINET JV |

# TECHNICAL DOCUMENTS

| | |
|---|---|
| **Project Name: Package 3 - Interim Road Access to Resort Core** | **Project Code:** QRXM114000 |
| **Location:** 00 | **Date:** 26-March-2026 |
| Document Title: **Inspection & Test Plan for RWIS and AQM** | **Ref No:** QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00001 |
| | **Rev No:** 00 |

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☐ Authority ☒ ICT

Type: ☐ Pre-Qualification ☐ Method Statement ☐ Material Submittal ☐ Sample ☒ ITP

Document Description: This is Inspection & Test Plan for for RWIS and AQM

| Doc. Ref. No. | Title |
|---|---|
| QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00001 | **Inspection & Test Plan for for RWIS and AQM** |

Enclosure:

| **Submitted By:** | **Received By:** |
|---|---|
| Name: Eng. Moataz<br>Signature:<br>Date: 26-march-2026 | Name:<br>Signature: |

**Below portion for Consultant Supervision use only**

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments:

1.All the work shall be carried out in accordance with project specification.
2.Performance & operational tests shall be conducted for countinous 24hr period as mentioned in project specification.










**Below portion for Client use only**

Comments:

Signed by: Signature: Date:

| HAIF-FSA JV Inspection & Test Plan | | | | | | I &TP | APPROVED DATE | DISCIPLINE ITS | |
|---|---|---|---|---|---|---|---|---|---|
| Intelligent Transportation System Works for RWIS and AQM INSTALLATION AND OPERATION | | | | | | HFC-ITP-0070 | | | |
| PROJECT TITLE:W8S Access Road To Resort Core (RA2RC) | | | | | | CONTRACTOR/SUBCONTRACTOR | | | |
| WIR No. | | | | | | CONSTRUCTION- Intelligent Transportation System Works for INSTALLATION AND OPERATION RWIS and AQM | HAIF | | |
| ITEM NO. | PROJECT PHASE | TASK / ACTIVITY | Quality Requirements /references/ specifications | Quality Record | INSPECTION RESPONSIBILITY ASSIGNMENTS | | REMARKS | | |
| | | | | | Contractor | Consultant | | | |
| 1.0 DOCUMENT REVIEW | | | | | | | | | |
| 1 | | Material Approval & Shop Drawing | QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00002<br>QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00001-00086 | QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00002<br>QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00001-00086 | R | H | | | |
| 2.0 MATERIAL RECEIVING INSPECTION | | | | | | | | | |
| 2 | | Material receiving inspection, protection & storage | QD0002-ADM-TEM-QMS00007[0A] MaterialReceiving Inspection in site HFC-CKL-4001 | QD0002-ADM-TEM-QMS00007[0A] MaterialReceivingInspection in siteHFC-CKL-4001 | H | H | MIR to be submitted | | |
| 3.0 WORK INSTALLATION | | | | | | | | | |
| 3.1 | | PRE - INSTALLATION | HFC-CKL-7001 | HFC-CKL-7001 | H | H | | | |
| 3.2 | | INSTALLATION | HFC-CKL-7002 | HFC-CKL-7002 | H | H | | | |
| 3.3 | | TESTING | HFC-CKL-7003 | HFC-CKL-7003 | H | H | | | |

## GENERAL NOTES

1. Surveillance: QA/QC organization to monitor work in progress without notice from Construction Organization
2. Witness: QA/QC organization shall be notified of the timing of Inspection or test in advance. However, the inspection or test shall be performed as scheduled if the QA/QC organization representative is not present.
3. Hold: QA/QC organization shall be notified of the timing of inspection or test in advance. Inspection or test shall not be carried out without the QA/QC organization representative in attendance.
4. If the Main Contractor delegates the assigned responsibility to the Subcontractor, then the Main Contractor will have the same degree of responsibility as assigned to Consultant.

LEGEND

| | | | |
|---|---|---|---|
| H | Hold Point for QC Inspection/ Test | R | Review of Documents |
| W | Witness Inspection/T | RH | Review & approval of Documents |
| S | Surveillance | | |

HFC-ITP-030

Checklist : HFC-CKL-4001

Material receiving inspection, protection & storage

PROJECT TITLE: Road Access To Resort Core (RA2RC)

ITP/ Ref.

Checklist: HFC-CKL-7001

APPROVED DATE

DISCIPLINE: ITS

WBS

CONTRACTOR/SUBCONTRACTOR

CONSTRUCTION- Intelligent Transportation System Works for INSTALLATION AND OPERATION of RWIS and AQM

HAIF

| ITEM NO. | Check Points & Acceptance Criteria | Reference | Pass | Fail | Not Applicable | Re-Inspection |
|---|---|---|---|---|---|---|
| 1.0 | **Material receiving inspection,protection & storage of ITS Devices (RWIS and AQM)** | | | | | |
| | | | | | | |
| 1.1 | Deliver ITS Device in packaging, protected, complying with applicable Standard. | project specification SECTION 137720 - ROADWAY WEATHER INFORMATION SYSTEM (RWIS and AQM) | | | | |
| 1.2 | Store equipment in a dry location. Protect from weather,fumes, water, debris,direct exposure to the sunlight, ultraviolet,etc | project specification SECTION 137720 - ROADWAY WEATHER INFORMATION SYSTEM (RWIS and AQM) | | | | |
| 1.3 | Provide necessary protection if required as per manufacturer's recommendations. | project specification SECTION 137720 - ROADWAY WEATHER INFORMATION SYSTEM (RWIS and AQM) | | | | |
| 1.4 | Handle equipment and devices with care, to avoid abrasion, puncturing and tearing housing, paint. | project specification SECTION 137720 - ROADWAY WEATHER INFORMATION SYSTEM (RWIS and AQM) | | | | |

Remarks

| PM/Contractor | | | QDC | |
|---|---|---|---|---|
| Contractor Construction | | | Third Party (if applicable) | |
| The work is ready for inspection | | | Document Reviewed / Work Inspected / Test Records Verified | |
| Name | Signature | Date | Name | Signature |
| | | | | |
| Contractor QC Inspector | | | QDC Supervision Consultant | |

Form Ref. No. QD0002-ADM-TEM-QTY-0003- Rev.0A

TRAFFIC TECH
www.traffic-tech.com

تقنيات المرور الأمنية ذ.م.م.
TRAFFIC TECH SECURITY W.L.L.

Date: 14-Oct-2026
Our Ref: TTSDN-Haif-290726-032

# Delivery Note

To: HAIF COMPANY ---------- الى:

Ref: WS045CR-53 (RA2RC – ACCESS ROAD TO RESORT CORE)

| SN | Model No. رقم الموديل | Description الوصـــــف | Unit الوحـدة | Qty الكميـة | Remarks ملاحظـات |
|---|---|---|---|---|---|
| MATERIAL SUPPLY (TRAFFIC SIGNALS) | | | | | |
| 1 | | Advanced Transportation Management System (ATMS) GUI– Based Enterprise Server Traffic Software Solution , Interim Road Main Line02 | PCS | 1 | |

**Delivered By:** Nasarudheen Sha ---------- **Date:** 14-10-2026 ----------

Printed Name & Signature

**Received By:** ---------- **Date:** ----------

Printed Name & Signature

Building 8, Floor 6
Olaya Street
P.O. Box 13524
Riyadh Saudi Arabia

E-mail : ttsa@traffic-tech.com
Web: www.traffic-tech.com
CR No. : 1010882732
VAT No : 311892040800003

# DMV Control Center


DMV Control Center

DMV Control Center is modular application software designed to provide a secure, integrated solution for managing diverse equipment, such as variable message signs (VMS), sports scoreboards, public transport displays, weather stations, cameras, parking systems, etc. Devices connected to the DMV Control Center utilize standardized communication protocols and communication channels, including Ethernet or GPRS/3G/4G/5G.

DMV Control Center functions as both a web portal and a SCADA server, enabling remote management, monitoring, and control of multiple devices.

The system is accessible through any web browser, providing operational flexibility.

The interface is user-friendly, featuring geographical maps or custom layout views for better visualization and control – simple, clear, and intuitive.

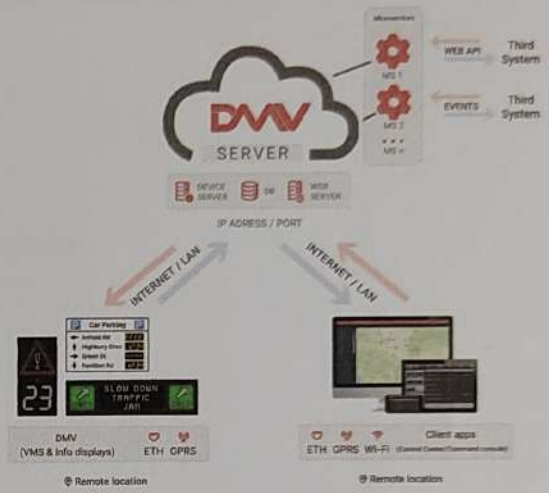


## DMV Control Center server

- **Server Platform:**

The system can be hosted on a local server or a public server (e.g., AWS Cloud), and it supports both Windows and Linux, providing flexible deployment options.

- **Database:**

A database stores data from devices, enabling the collection, tracking, and analysis of information from various connected devices.

- **Administration Web App:**

A web-based application is available for administration, enabling users to manage both users and devices via a user-friendly interface, accessible from any web browser.

- **Universal Software Platform:**

The software is designed to be universal, meaning it can integrate with various types of devices, including all DMV signs, weather stations, traffic counters, cameras, and parking systems, ensuring broad compatibility with existing infrastructure.




## DMV Control Center software

- **Web Application:**

The system is accessible via a web application available in any web browser, offering flexibility in use.

- **User-Friendly Interface:**

The interface is user-friendly, featuring geographical maps or custom layout views for better visualization and control. The system is simple, clear, and intuitive to use. Devices are monitored and controlled via "Techniques", which represent the functions specific to the device. The Technique bar, which displays all relevant functions of a selected device, appears on the right side of the screen after the device is selected.



## DMV Control Center Modules

DMV Control Center, **modular software**, offers the flexibility to choose the modules that best suit your needs. These modules were developed to integrate various devices and systems, each with its specific functionalities.
Each module has a price and can be ordered separately, ensuring a transparent cost structure.

There is a **Basic Module** (which is mandatory) that has to be combined with at least one of the following modules:
**Variable Message Signs (VMS) Module, Traffic data module, Meteo module, Video module, Parking guidance module...**

## DMV Control Center Basic Module

includes functionalities that all users need regardless of which other modules they use.

- Displaying each device on the geographic map or custom layout view
- Easy filtering, searching, and online status indication in the units list
- Notifications (Pop-up notifications, Ring-style alerts, Modal windows, Map markers, E-mail notifications...)
- Maintenance and Self-Diagnostics
- Logs and Events History Monitoring
- The Administration Panel




## DMV Control Center VMS Module

is designed to give users flexible control and monitoring of Variable Message Signs:

- Easy creation and editing of Panels and Scenarios
- Display Scenario Change on Individual VMS


DMV
Login
DELL

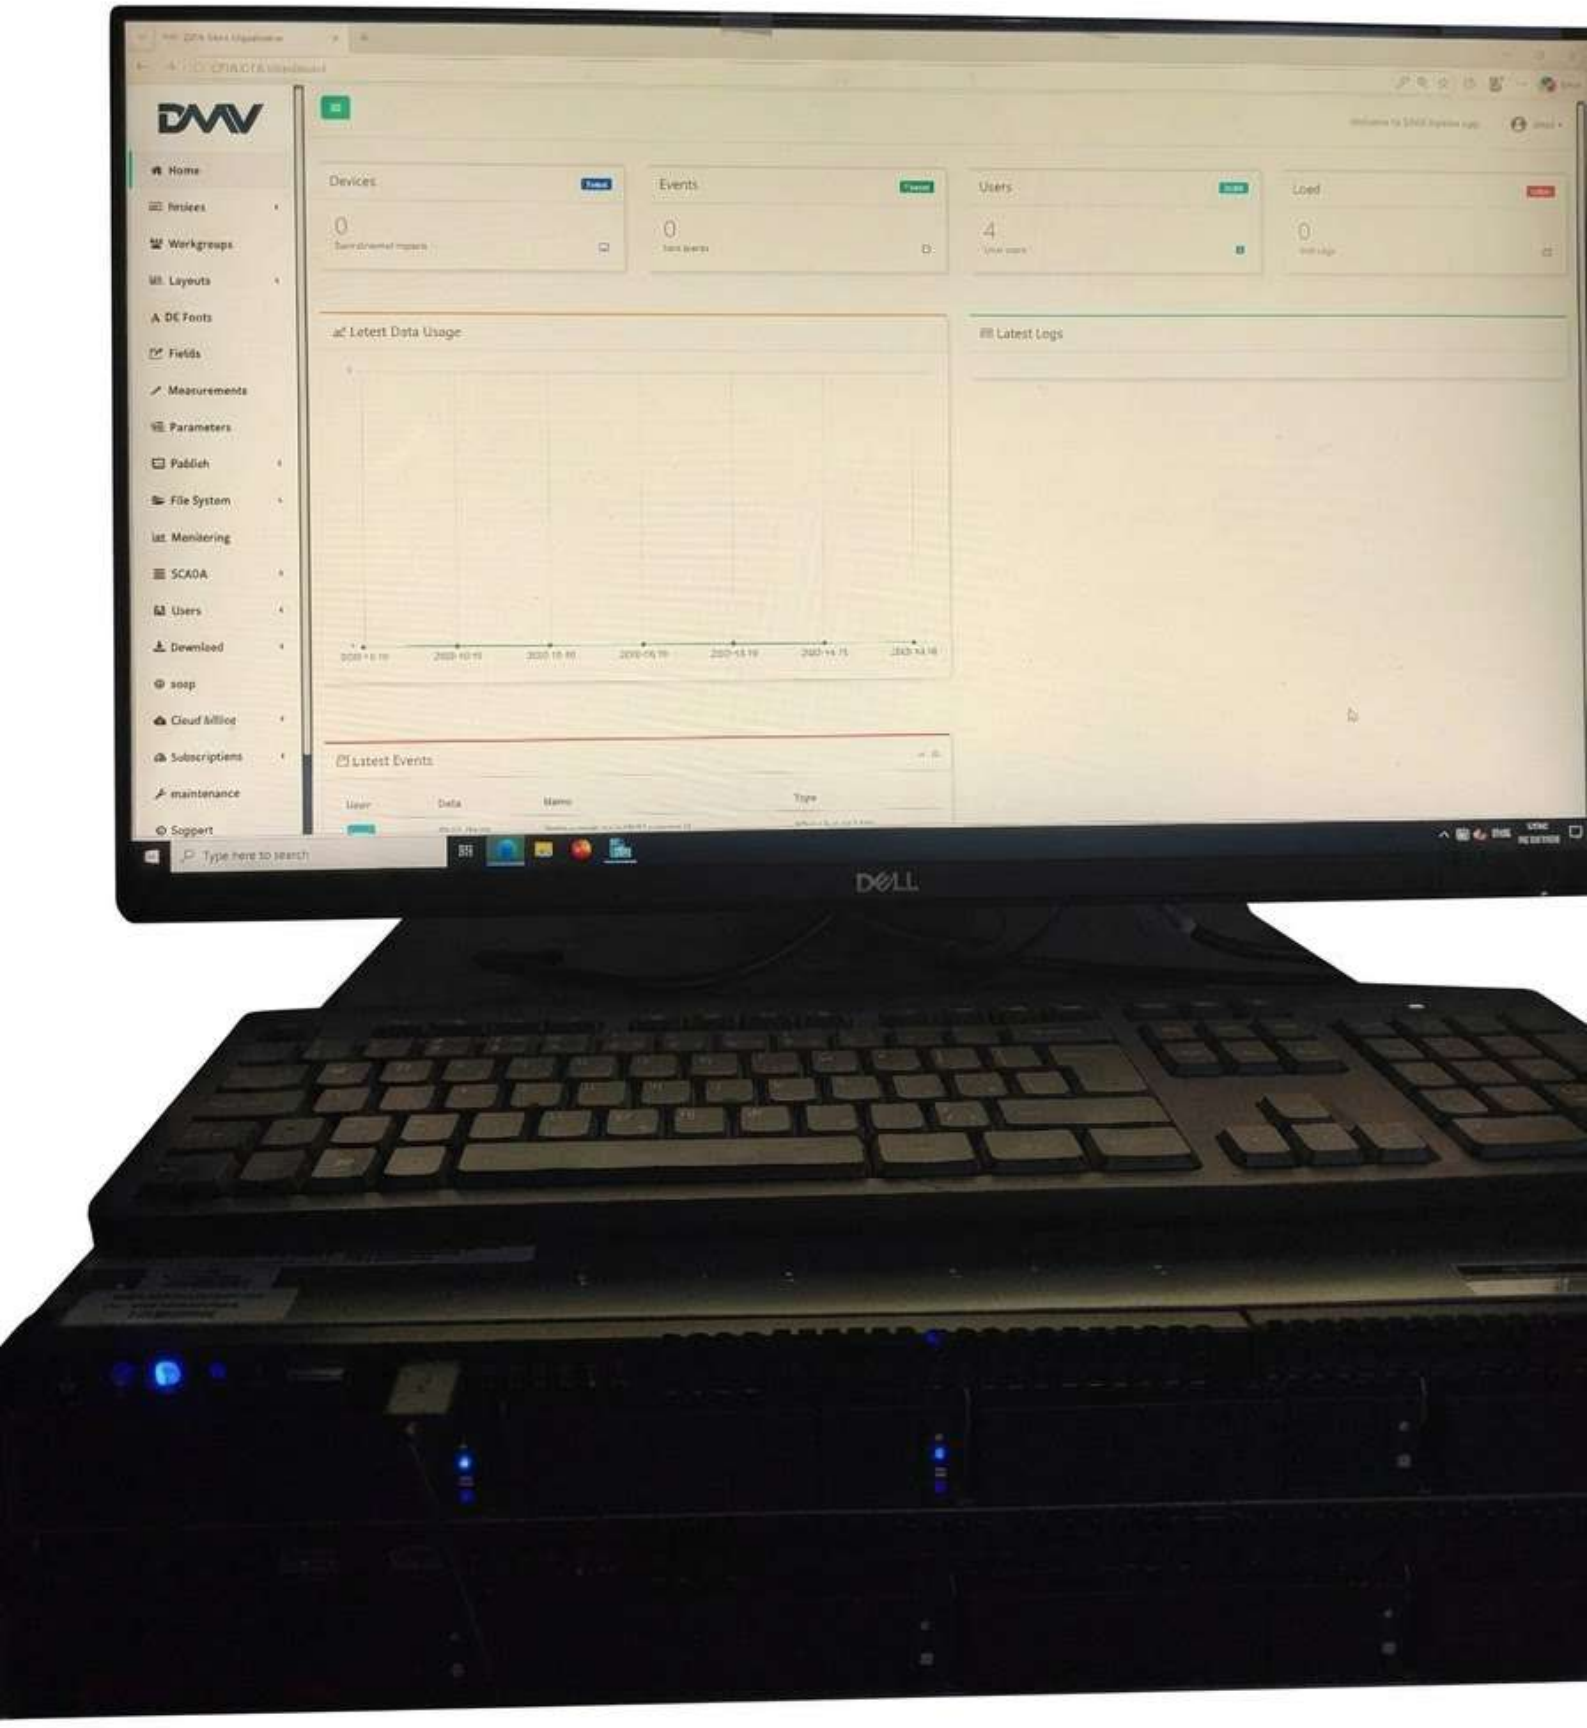
Home
Devices
Workgroups
Layouts
DC Fonts
Fields
Measurements
Parameters
Publish
File System
Monitoring
SCADA
Users
Download
soap
Cloud billing
Subscriptions
maintenance
Support
Devices
0
Events
0
Users
4
Load
0
Latest Data Usage
Latest Logs
Latest Events
User
Data
Name
Type
Type here to search
DELL
