QIDDIYA DEVELOPMENT COMPANY

DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00004	REVISION NUMBER:	OD	ISSUED BY:	PMO
DOCUMENT TITLE	**WIR FORM**	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022

WORK INSPECTION REQUEST (WIR) FORM

Contractor:	HAIF-FREYSSINET JV
Project:	RA2RC
Contract No.:	QPMO-410-CT-00618
Work Inspection Request Number:	QRXM114000-HFC-TEC-WIR-ITS-02-RO5-00047

HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☐	Quality	☐	Project Controls	☐
Civil / Structural	☑	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

WORK DESCRIPTION

Inspection / Test Location:	**INTERIM ROAD Sta. (JUNCTION -1)**		
GIS/GPS GeoTag Coordinates (If applicable)			
Inspection Date:	20-Jun-2026	**Inspection Start Time:**	9:30 am
ITP:	QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00003	**Checklist:**	HFC-CKL-6003
Spec's / Dwg. Ref.:	QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00015	**Approved Method Statement Number:**	QRXM114000-HFC-TEC-MST-ITS-02-RO5-00001

Attachments: ☑ **Drawings** ☑ **Data Sheets** ☐ **TQs/RFI** ☐ **OTHER** QRXM114000-HFC-DRW-SDW-CIV-02-RO5-00001

DESCRITPTION OF WORK

Inspection request for Installing ITS Red Light Camera 6.1m.Pole With Accessories (4 Pcs.) Junction-1 at Access to Resort core interim Road. As per attached drawing.

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Complies with Approved ITPs/Checklists?	● YES	○ NO	○ NA	**REMARKS**	
All Strucutral Embedded Items Cleared?	○ YES	○ NO	○ NA	**WIR Number**	
Embedded Electrical items Cleared by Electrical QC?	○ YES	○ NO	○ NA	**WIR Number**	
Embedded Mechanical Items Cleared by Mechanical QC?	○ YES	○ NO	○ NA	**WIR Number**	

Accepted: ●

Accepted with Comments (See Remarks): ○

Rejected (See Remarks): ○

REMARKS:

Name:	Moataz Elkhateeb	**Signature:**		**Date:**	20-06-2026

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Project spec requirements?	○ YES ○ NO	Okay to Proceed with next activity?	○ YES ○ NO ○ NA

Accepted: ○

Accepted with Comments (See Remarks): ☑

Rejected (See Remarks): ○

REMARKS:
① Provide inside components of enclosure.
② Final approval is subject to the acceptance of Testing & commissioning and QIC/law enforcement agency.

Name:	M. YASIR.	**Signature:**		**Date**	20/06/2026.

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

Client: Qiddiya	**Consultant:** Zuhair Fayez Partnership	**Contractor:** Haif Company Freyssinet HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
Location: 00	**Date:** 08-April-2026
Document Title: **Inspection & Test Plan for Red Light Camera Installation and Operation**	**Ref No:** QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00003
	Rev No: 00

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☐ Authority ☒ ITS

Type: ☐ Pre-Qualification ☐ Method Statement ☐ Material Submittal ☐ Sample ☒ ITP

Document Description: This is Inspection & Test Plan for Red Light Camera Installation and Operation

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00003	**Inspection & Test Plan for Red Light Camera Installation and Operation**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz Signature: Date: 08-Apr-2026	Name: Signature:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments: All the work shall be carried out in accordance with project specification and applcable standards & codes.

A: Approved
QI09043311-UPR TBN17&TN505
Saud Nawab
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

A: Approved
QI09043311-UPR TBN17&TN505
Muhammad Yasir Khadim Ali
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

A: Approved
QI09043311-UPR TBN17&TN505
[illegible]
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

Below portion for Client use only

Comments:

Signed by: Signature: Date:

Checklist : HFC-CK.-6003

INSTALLATION OF RED LIGHT CAMERA

PROJECT TITLE: Road Access To Resort Core (RA2RC)

WIR No.

Checklist	APPROVED DATE	DISCIPLINE
HFC-CKL-6003		ITS
WBS	CONTRACTOR/SUBCONTRACTOR	

CONSTRUCTION-
Intelligent Transportation System
Works for INSTALLATION AND
OPERATION of
RED LIGHT CAMERA

HAIF

ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
1.0	INSTALLATION OF ITS DEVICES - RED LIGHT CAMERA					
1.1	All equipment shall be firmly secured in place unless requirements of portability dictate otherwise.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / A / 1	✓			
1.2	Equipment is to be laid out properly in communication rooms in a way to reserve relevant space for maintenance activities. This space shall also account for any future expansion of the system.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / A / 2	✓			
1.3	Installation shall be performed in accordance with the applicable standards, requirements, manufacturers' guidelines and any authorities having jurisdiction.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / A / 3	✓			
1.4	All boxes, equipment, etc. shall be plumb and square.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / A / 4	✓			
1.5	The Contractor shall take such precautions that are necessary to prevent and guard against electromagnetic interference.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / A / 5	✓			
1.6	After the proper layout of all equipment is accomplished, all components are to be labeled and marked.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / A / 6	✓			
1.7	During installation, consideration shall be given to operational efficiency as well as the overall aesthetic factors.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / A / 7	✓			
1.8	The Contractor shall supply and install all fittings and accessories, whether or not specified, required for proper, safe, and reliable operation of the system.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / A / 8	✓			
1.9	The Contractor shall ensure that safe ingress and egress from all work areas are maintained during movement and installation of equipment/materials.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / A / 9	✓			
1.10	For Red Light camera structure details, refer to structural drawings for foundation details.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / A / 10	✓			
1.11	The Contractor shall install the red-light camera cameras on the support structures as per manufacturer's instructions.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / A / 11	✓			
1.12	Wiring within Enclosures: Bundle, lace, and train cables to terminal points with no excess and without exceeding manufacturer's limitations on bending radii. Provide and use lacing bars and distribution spools.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / B / 1	✓			
1.13	Install manufactured conduit sweeps and long-radius elbows whenever possible.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / B / 2	✓			
1.14	Terminate conductors; no cable shall contain un-terminated elements. Make terminations only at outlets and terminals.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / B / 3	✓			
1.15	Splices, Taps, and Terminations: Arrange on numbered terminal strips in junction, pull, and outlet boxes; terminal cabinets; and equipment enclosures. Cables may not be spliced.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / B / 4	✓			
1.16	Secure and support cables at intervals not exceeding 760 mm (30 inches) and not more than 150 mm (6 inches) from cabinets, boxes, fittings, outlets, racks, frames, and terminals.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / B / 5	✓			
1.17	Do not install bruised, kinked, scored, deformed, or abraded cable. Do not splice cable between termination, tap, or junction points. Remove and discard cable if damaged during installation and replace it with new cable.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / B / 6	✓			
1.18	Visually inspect wire and cable for faulty insulation prior to installation.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / B / 7	✓			
1.19	Protect cable ends at all times with acceptable end caps except during actual termination.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / B / 8	✓			
1.20	After installation, and before termination, all wiring and cabling shall be checked and tested to ensure there are no grounds, opens, or shorts on any conductors or shields.	Project Specification SECTION 137740 - 17 RED LIGHT CAMERA SYSTEM 3.1 / B / 9	✓			
1.21	Install LAN cables using techniques, practices, and methods that are consistent with Category 6A rating of components and fiber-optic rating of components, and that ensure Class EA and fiber-optic performance of completed and linked signal paths, end to end.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / B / 10	✓			
1.22	Install tamper switches on components indicated to receive tamper switches, arranged to detect unauthorized entry into system-component enclosures and mounted in self-protected, inconspicuous positions.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / B / 11	✓			

1.23	For units that are mounted outdoors, in damp locations, or where exposed to weather, install consistent with requirements of weatherproof rating.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / C / 1	✓		
1.24	Provide a typed schedule of all data ports according to each related room jack designation for all Telecommunications Rooms.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / D / 1	✓		
1.25	Provide labeling for all the cables terminated at the traffic signal cabinet.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / D / 2	✓		
1.26	Ground cable shields and equipment to eliminate shock hazard and to minimize ground loops, common-mode returns, noise pickup, cross talk, and other impairments.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / E / 1	✓		
1.27	Conductors: Sizes and types as recommended in writing by system manufacturer unless otherwise indicated.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / F / 1	✓		
1.28	Control and Signal Cables: Install unshielded, twisted-pair cable unless otherwise indicated or if manufacturer recommends shielded cable.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / F / 2	✓		
1.29	Identify distributors, racks, rack-mounted equipment, bonding conductors, backbone cabling subsystems, horizontal cabling subsystem, patch cables, access points and earth busbars.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / F / 3	✓		
1.30	Color-code cross-connect fields. Apply colors to voice and data service backboards, connections, covers, and labels.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / F / 4	✓		
1.31	For installations outside buildings, label cables, jointing chambers and cabinets with a unique identifier to enable tracing in both directions.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / F / 5	✓		
1.32	Labeling of optical fiber installations should be such that the polarization of duplex optical fiber connections is known and consistent throughout the installation.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / F / 6	✓		
1.33	Identification within Connector Fields in Equipment Rooms and Wiring Closets: Label each connector patch cord, and each discrete unit of cable-terminating and connecting hardware. Where similar jacks and plugs are used for both voice and data communication cabling, use a different color for jacks and plugs of each service.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / F / 7			
1.34	Patch cords shall be labeled on each end specifying the source and destination of the cord.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / F / 8	✓		
1.35	Long cable runs in underground ducts shall be labeled at 50 meters intervals.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / F / 9	✓		
1.36	Labels shall be preprinted or computer-printed type with printing area and font color that contrasts with cable jacket color but still complies with requirements in ANSI/TIA-606-B and EN 50174-1.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / F / 10	✓		
1.37	Splices, Taps, and Terminations: Make connections only on numbered terminal strips in junction, pull, and outlet boxes; terminal cabinets; and equipment enclosures.	Project Specification SECTION 137740 - 18 RED LIGHT CAMERA SYSTEM 3.1 / G	✓		

Remarks

PM/Contractor			**QDC**		
Contractor Construction			**Third Party (if applicable)**		
The work is ready for inspection			**Document Reviewed**	**Work Inspected**	**Test Records Verified**
Name	Signature	Date	Name	Signature	
[illegible]			M. YASIR.	20/06/2026.	
	Contractor QC Inspector			QDC Supervision Consultant	

Form Ref. No. QD0002-AIM-TEM-QTY-00003– Rev.0A

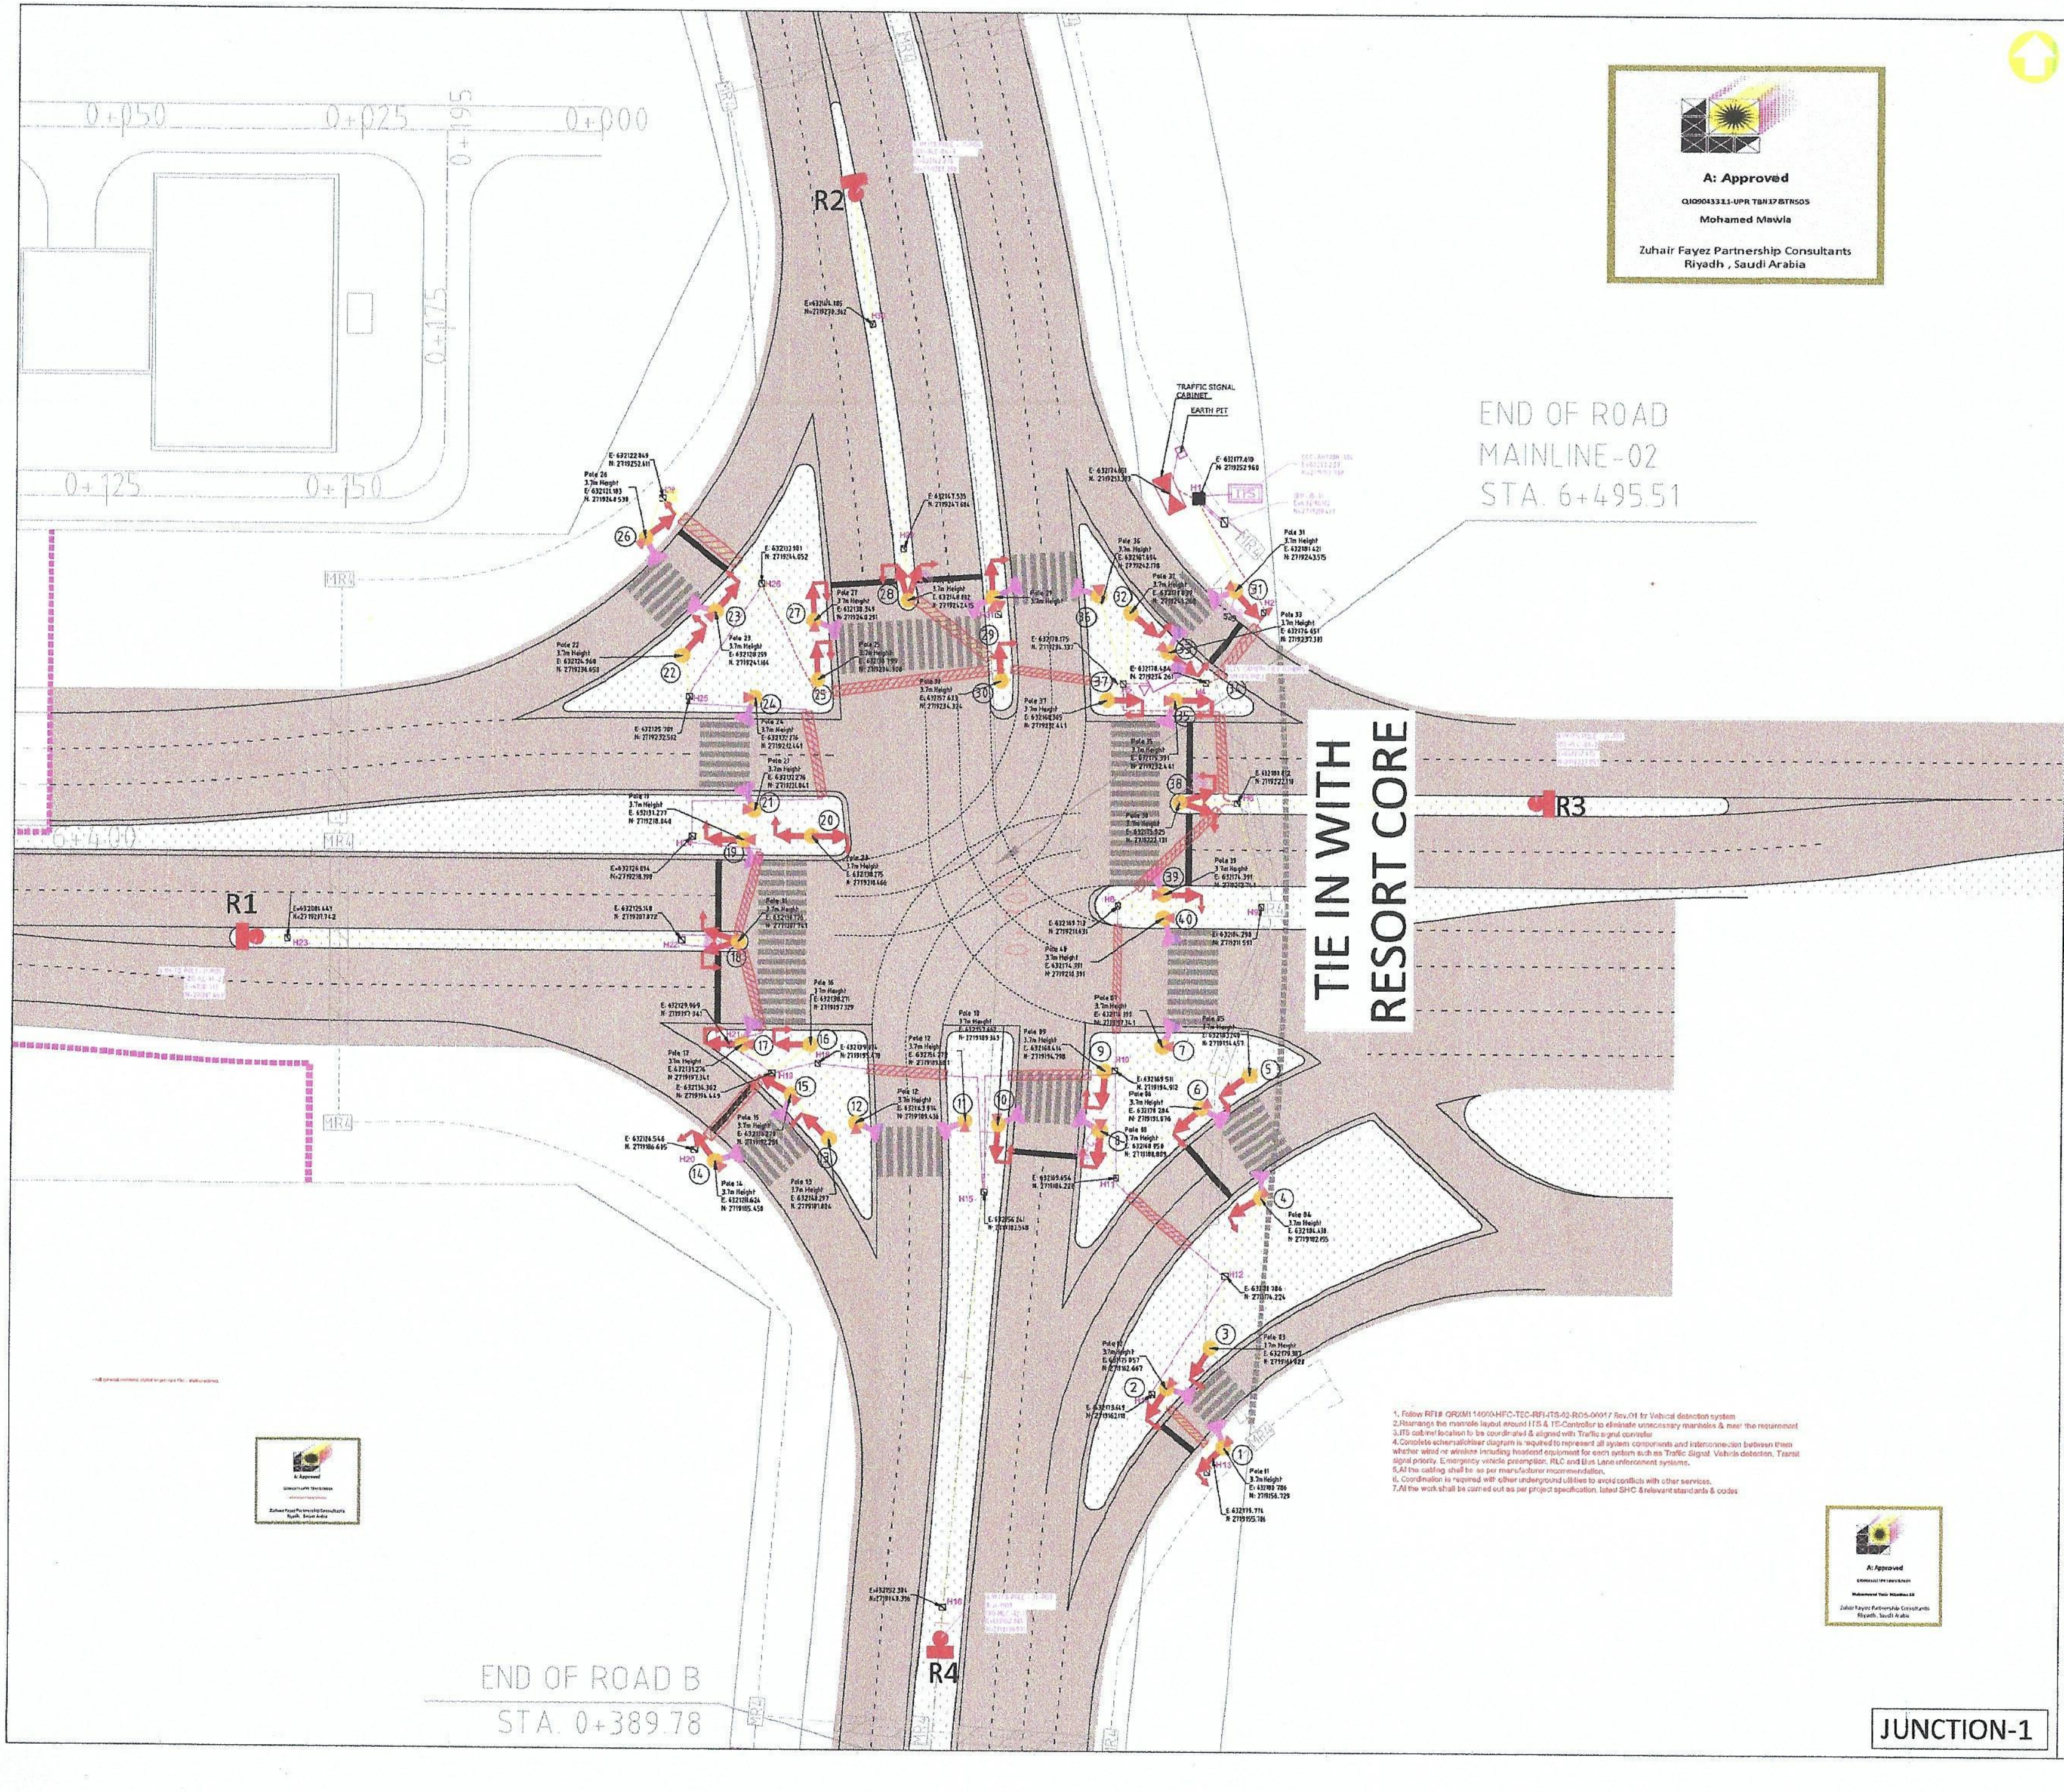

A: Approved

QIO904331 1-UPR TBN17BTNSOS

Mohamed Mawla

Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

1. Follow RFI# QRXM114000-HFC-TEC-RFI-ITS-02-RO5-00017 Rev.01 for Vehical detection system
2. Rearrange the manhole layout around ITS & TS-Controller to eliminate unnecessary manholes & meet the requirement
3. ITS cabinet location to be coordinated & aligned with Traffic signal controller
4. Complete schematic/riser diagram is required to represent all system components and interconnection between them whether wired or wireless including headend equipment for each system such as Traffic Signal, Vehicle detection, Transit signal priority, Emergency vehicle preemption, RLC and Bus Lane enforcement systems.
5. All the cabling shall be as per manufacturer recommendation.
6. Coordination is required with other underground utilities to avoid conflicts with other services.
7. All the work shall be carried out as per project specification, latest SHC & relevant standards & codes

Qiddiya

Consultant's information

HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com

Zuhair Fayez Partnership

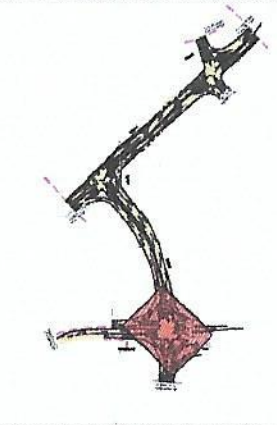

Notes:

1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3. THIS DRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.

REFERENCE I.F.C DESIGN DRAWING NO:

1. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000001
2. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000001
3. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000005
4. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000006
5. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000001
6. QRXP117115-DAH-VORA2R-DWG-ICT-R3-Z00000-2000000

LEGEND:

- SIGNAL PEDESTAL : 3.7m HEIGHT
- VEHICLE SIGNAL HEAD - CIRCULAR ASPECTS
- VEHICLE SIGNAL HEAD - THROUGH ASPECTS
- VEHICLE SIGNAL HEAD - RIGHT TURN ASPECTS
- VEHICLE SIGNAL HEAD - LEFT TURN ASPECTS
- PEDESTRIAN HEAD SIGNAL
- PEDESTRIAN PUSH BUTTON
- Ⓝ SIGNAL PEDESTAL/GANTRY NUMBER
- ■ JUNCTION BOX TYPE 1 : (1200x800x1000)
- JUNCTION BOX TYPE 2 : (900x600x1000)
- JUNCTION BOX (JB)
- GLOBAL POSITIONING SYSTEM ANTENNA
- IX-WAY HDPE DUCT SAND ENCASED (BY OTHERS)
- IX-WAY HDPE DUCT ROAD CROSSING CONCRETE ENCASED (BY OTHERS)
- MANHOLE TYPE MR4 (BY OTHERS)
- CONCRETE ENCASED DUCT BANK
- UNPLASTICISED POLYVINYL CHLORIDE DUCT, 8 ø110mm
- UNPLASTICISED POLYVINYL CHLORIDE DUCT, 6 ø110mm
- UNPLASTICISED POLYVINYL CHLORIDE DUCT, 4 ø110mm
- UNPLASTICISED POLYVINYL CHLORIDE DUCT, 2 ø110mm
- UNPLASTICISED POLYVINYL CHLORIDE DUCT, 1 ø110mm
- CLOSED CIRCUIT TELEVISION POLE . 15m HEIGHT
- CLOSED CIRCUIT TELEVISION CAMERA (BY OTHERS)
- VEHICLE DETECTION SYSTEM
- TRAFFIC SIGNAL CABINET
- ITS CABINET GROUND MOUNTED ENCLOSURE (GME)
- RED LIGHT 1-CAMERA WITH IR ILLUMINATOR (RLC)

(01) - LPR - 01 - 1
- NUMBER OF DEVICES ON THE SAME LOCATION
- DEVICE No. IN THE CORRESPONDING SHEET.
- DEVICE ABBREVIATION
- SHEET No.

Rev. No.	Date	Description	Appr.
00	30-8-2025	FOR REVIEW AND APPROVAL	C
01	06-10-2025	FOR REVIEW AND APPROVAL	B
02	04-11-2025	FOR REVIEW AND APPROVAL	B
03	04-02-2026	FINAL REVISION	
--	--	--	--
--	--	--	--
--	--	--	--

Consultant

Project:

Qiddiya

Contractor

شركة هيف
Haif Company

ITS Contractor

TRAFFIC TECH
www.traffic-tech.com

Job title: Road Access To Resort Core

Drawing title:

SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-1

Sheet number:

SHEET 1 / 18

Scale:1:1000 @ A0

Drawn: M.Elsayed

Checked: M.Abuzaid

Designed:

Approved:

Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00015

Revision 03
