QIDDIYA DEVELOPMENT COMPANY						
DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00004	REVISION NUMBER:	OD	ISSUED BY:	PMO	Qiddiya
DOCUMENT TITLE	WIR FORM	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022	

WORK INSPECTION REQUEST (WIR) FORM

Contractor:	HAIF-FREYSSINET JV
Project:	RA2RC
Contract No.:	QPMO-410-CT-00618
Work Inspection Request Number:	QRXM114000-HFC-TEC-WIR-ITS-02-RO5-00070

HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☐	Quality	☐	Project Controls	☐
Civil / Structural	☑	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

WORK DESCRIPTION

Inspection / Test Location:	INTERIM ROAD Sta. JUNCTION -02 &03 Aera		
GIS/GPS GeoTag Coordinates (If applicable)			
Inspection Date:	19-Jul-2026	Inspection Start Time:	10:00 am
ITP:	QRXM114000-HFC-TEC-ITP-ITS-00007	Checklist:	HFC-CKL-1002
Spec's / Dwg. Ref.:	QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00015 ,24,33	Approved Method Statement Number:	QRXM114000-HFC-TEC-MST-CIV-02-RO5-00009
Attachments:	☑ Drawings ☐ Data Sheets ☐ TQs/RFI ☐ OTHER QRXM114000-HFC-DRW-SDW-CIV-02-RO5-00001		

DESCRITPTION OF WORK

Inspection request for Installing of ITS Cabinet 9 Nos, at Interim Road (Upgrade) and Junction 01 & 02 & 03 area.Size, (H1800 x SW800 x XD600),MMIP65,GIG90 Sheet),at Access to Resort core interim Road Mainline-02.As per Attached Drawing

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Complies with Approved ITPs/Checklists?	◉ YES ○ NO ○ NA	REMARKS	
All Strucutral Embedded Items Cleared?	○ YES ○ NO ○ NA	WIR Number	
Embedded Electrical items Cleared by Electrical QC?	○ YES ○ NO ○ NA	WIR Number	
Embedded Mechanical Items Cleared by Mechanical QC?	○ YES ○ NO ○ NA	WIR Number	

Accepted:	◉
Accepted with Comments (See Remarks):	○
Rejected (See Remarks):	○

REMARKS:					
Name:	Naseem Ahmed	Signature:	Naseem Ahmed	Date:	19-07-2026

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Project spec requirements?	☑ YES ○ NO	Okay to Proceed with next activity?	☑ YES ○ NO ○ NA

Accepted:	○
Accepted with Comments (See Remarks):	☑
Rejected (See Remarks):	○

REMARKS:	QIC confirms that the above activity/document was inspected & approved by former CSC (ZHP). All associated responsibilities, liabilities, and obligations remain solely with ZHP.				
Name:	Zawar Ahmad	Signature:		Date	12/8/26

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

Dawn role is strictly limited to documentation review & shall not constitute acceptance of any such responsibilities or liabilities. Final approval is for QIC.

Client:	Consultant:	Contractor:
Qiddiya		HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - **Interim Road Access to Resort Core**	**Project Code:** QRXM114000
Location: 00	**Date:** 24-December-2025
Document Title:**Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (**ITS Cabinets)	**Ref No:** QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00012
	Rev No: 01

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☑ ITS ☐ Civil

Type: ☐ Pre-Qualification ☐ Method Statement ☒ Material Submittal ☐ Sample ☐ Other

Document Description:Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (ITS Cabinets)

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00012	**Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (ITS Cabinets)**

Enclosure:

Submitted By:	**Received By:**
Name: **Eng. Moataz** Signature: Date:24-December-2025	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments: For comments refer to the CRS

Below portion for Client use only

Comments:

Signed by: Signature: Date:

Client:	Consultant:	Contractor:
Qiddiya		شركة هيف Haif Company

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
Location: RA2RC \ Qiddiya INTERM ROAD	**Date:** 18-May-2026
Document Title: Method of Statement for Installation and Commissioning of Intelligent Transportation System Equipment and Devices.	**Ref No: QRXM114000-HFC-TEC-MST-ITS-02-RO5-00001**
	Rev No: 01

Department: ☐ Architectural ☐ Civil/Structural ☐ Electrical ☐ Mechanical ☒ ITS ☐ Others

Type: ☐ Pre-Qualification ☒ Method Statement ☐ Material Submittal ☐ Sample ☐ Other

Document Description: Method of Statement for Installation and Commissioning of Intelligent Transportation System Equipment and Devices.

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-MST-ITS-02-RO5-00001	**Method of Statement for Installation and Commissioning of Intelligent Transportation System Equipment and Devices.**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz Signature: Date: 18-May-2026	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments:

1.Attach approved ITP

2.All the work shall be carried out in accordance with project specification & applicable standards & codes









Below portion for Client use only

Comments:

Signed by: Signature: Date:

QIDDIYA DEVELOPMENT COMPANY

DOCUMENT NUMBER:	QD-XXX-TRY-QAC-0007	REVISION NUMBER:	02	ISSUED BY:	QDC
DOCUMENT TITLE:	MIR FORM	REVISION TYPE:	Minor	DATE ISSUED:	09/05/2023

MATERIAL INSPECTION REQUEST (MIR) FORM

Contractor:	HAIF COMPANY
Project:	DRNO-4*9-CT-0018- ROAD ACCESS TO RESORT CORE
Contract No.:	QR9043311/WD-0004
Material Inspection Request Number:	QRXM114000-HFC-TEC-MIR-ITS-02-RO5-00014

HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☐	Quality	☐	Project Controls	☐
Civil/Structural	☑	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

MATERIAL DESCRIPTION

Inspection / Test Location:	INTERIM ROAD MAIN LINE-02		
Material Name:	ITS CABINETS WITH ACCESSORIES	Quantity:	09 Nos.
P.O Number		Delivery Note Number:	TTSDN-HAIF-280426-024
Approved Material Transmittal Number: (Owner Reviewer Approved)	QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00012	Approval Date:	
Inspection Date:	30-Jun-2026	Inspection Start Time:	11:00 AM
ITP:	QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00007	Checklist:	HFC-CKL-1001
Spec's / Dwg. Ref.:	TRAFFIC TECH SECURITY W.L.L	Approved Method Statement Number:	
Attachments:	Test Certificate: ◉ Yes ○ No IFC / Shop Drawings: ○ Yes ◉ No		

DESCRIPTION OF MATERIAL

Control Enclosure SS WMB-841PWX1010MMD IP 65 GI/PC Sheet - Powder Coating Finish, DOUBLE Insulated Layer 1 Fan 220V Filter ,CNC ROAM GASKET (07 Nos.) Control Enclosure M1800SWE0606D60/MM IP 65 GI/PC Sheet - Powder Coating Finish DOUBLE Insulated Layer 2 Fan 220V Filter ,CNC ROAM GASKET (02 Nos.) Interim Road Main Line-02

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Are Complete Details Mentioned in P.O and Delivery Note?	◉ YES ○ NO	REMARKS	
Complies with Approved ITPs/Checklists?	◉ YES ○ NO	REMARKS	
Signs of Physical Damage?	○ YES ◉ NO	REMARKS	
Conforms to Approved Material Submittal?	○ YES ○ NO	REMARKS	
Accepted:			◉
Accepted with Comments:			○
Rejected (See Remarks):			○
REMARKS:			
Name:	Moataz Elkhateeb	Signature:	Date: 30-06-2026

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Material requirements?	○ YES ○ NO	Materials Are Stored correctly?	✓ YES ○ NO ○ NA
Accepted:			○
Accepted with Comments:			○
Rejected (See Remarks):			○
REMARKS:	Comply with the comments mentioned on attached supporting documents.		
Name:	M. YASIR	Signature:	Date: 30/06/2026.

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Haif Company / Freyssinet — HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
Location: 00	**Date:** 14 -June-2026
Document Title: **Inspection & Test Plan for Intelligent Transportation System Works for ITS CABINET SYSTEM INSTALLATION AND OPERATION**	**Ref No:** QRXM114000-HFC-TEC-ITP-ITS-00007
	Rev No: 00

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☐ Authority ☐ Civil ☒ Others

Type: ☐ Pre-Qualification ☐ Method Statement ☐ Material Submittal ☐ Sample ☒ ITP

Document Description: This is Inspection&Test Plan for Intelligent Transportation System Works for ITS CABINET SYSTEM INSTALLATION AND OPERATION

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-ITP-ITS-00007	**Inspection&Test Plan for Intelligent Transportation System Works for ITS CABINET SYSTEM INSTALLATION AND OPERATION**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz Signature: Date: 14-June-2026	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments: All the work shall be carried out in accordance with approved shop drawings, project specifications and relevant standards & codes

A: Approved
Muhammad Yasir Khadima Ali
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

A: Approved
Saud Nawab
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

A: Approved
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

Below portion for Client use only

Comments:

Signed by: Signature: Date:

HAIF-FSA JV Inspection & Test Plan						I &TP		APPROVED DATE	DISCIPLINE
Inteligent Transportation System Works forITS CABINET SYSTEM INSTALLATION AND OPERATION						**HFC-ITP-0010**			**ITS**
PROJECT TITLE:WBS Access Road To Resort Core (RA4RC)						CONTRACTOR/SUBCONTRACTOR			
WIR No.						CONSTRUCTION-Intelligent Transportation System Works for INSTALLATION AND OPERATION of ITS CABINET		HAIF	

ITEM NO.	PROJECT PHASE	TASK / ACTIVITY	Quality Requirements /references/ specifications	Quality Record	INSPECTION RESPONSIBILITY ASSIGNMENTS			REMARKS
					Contractor	Third Party	Consultant	
1.0 DOCUMENT REVIEW								
1		Material Approval & Shop Drawing	QRXM114000-HFC-TEC-MAT-ITS-04-RO5-000014 QRXM114000-HFC-DRW-SDW-ITS-04-RO5-00001-00086	QRXM114000-HFC-TEC-MAT-ITS-04-RO5-000014 QRXM114000-HFC-DRW-SDW-ITS-04-RO5-00001-00086	R		H	
4.0 MATERIAL RECEIVING INSPECTION								
4		Material receiving inspection, protection & storage	QD0004-ADM-TEM-QMS00007[0A] MaterialReceiving Inspection in site HFC-CKL-1001	QD0004-ADM-TEM-QMS00007[0A] MaterialReceivingInspection in site HFC-CKL-1001	H		H	MIR to be submitted
3.0 WORK INSTALLATION								
3.1		PRE - INSTALLATION	HFC-CKL-1002	HFC-CKL-1002	H		H	
3.4		INSTALLATION	HFC-CKL-1003	HFC-CKL-1003	H		H	
3.3		TESTING	HFC-CKL-1004	HFC-CKL-1004	H		H	

GENERAL NOTES

1	Surveillance: QA/QC organization to monitor work in progress without notice from Construction Organization
4	Witness: QA/QC organization shall be notified of the timing of Inspection or test in advance. However, the inspection or test shall be performed as scheduled if the QA/QC organization representative is not present
3	Hold: QA/QC organization shall be notified of the timing of inspection or test in advance. Inspection or test shall not be carried out without the QA/QC organization representative in attendance.
4	If the Main Contractor delegates the assigned responsibility to the Subcontractor, then the Main Contractor will have the same degree of responsibility as assigned to Consultant.

LEGEND

H	Hold Point for QC Inspection/ Test	R	Review of Documents
W	Witness Inspection/T	RH	Review & approval of Documents
S	Surveillance		

Checklist : HFC-CKL-1002	Checklist	APPROVED DATE	DISCIPLINE
PRE-INSTALLATION OF ITS CABINET	HFC-CKL-1002		ITS
PROJECT TITLE: Road Access To Resort Core (RA4RC)	WBS	CONTRACTOR/SUBCONTRACTOR	
WIR No.	CONSTRUCTION- Intelligent Transportation System Works for INSTALLATION AND OPERATION of ITS CABINET	HAIF	

ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
1.0	**PRE INSTALLATION OF ITS CABINET**					
1.1	During the design stage Factory Acceptance Test (FAT) procedures shall be described to ensure the ITS equipment has been completed to the required functionality, safety and quality and meets all the contractual specifications the following points shall be included.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			
1.2	FAT shall be undertaken on the equipment due to be shipped to the Competent Authority and Government Authorities to fulfill their operational requirement and not an alternative product.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			
1.3	The factory acceptance test procedures described in the design shall include is used to:	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)				
1.4	Proof of functionality, quality, and integrity with a comprehensive checking process against the product specifications. • Verification of all-important documents	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			
1.5	Verification of all-important documents (manuals, instructions, plans, drawings) to ensure they accurately reflect the requirements and the equipment operation.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			
1.6	Performance of the equipment as expected under the testable range of foreseeable conditions, including misuse and errors.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)				
1.7	Consideration that the FAT shall be witnessed by the Competent Authority and Government Authorities.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			
1.8	In the description of procedures FAT shall be specific to the product being tested but shall include the following as a minimum.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)				
1.9	• Pre-inspection testing and inspection.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			
1.10	• Pre-configuration of settings and software.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)				
1.1	• Preparation of a test register.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			
1.1	• Review of drawings and documentation.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)				
1.1	• Interface testing.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			
1.1	• Full communications testing.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)				
1.2	• Full cycle of powering up, logging on, logging off and powering down.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			
1.16	• Full cycle of powering up, logging on, logging off and powering down.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)				
1.17	Description of the event of a test failing for any reason, the equipment's provider analysis of the fault. If the fault is irresolvable, then an exception shall be logged in the test register. At the end of the FAT, the completed tests should be evaluated by the test team including any test failures that occurred. An evaluation meeting shall agree on the nature of any faults encountered and discuss if the FAT should be continued.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			
1.2	One of the following actions shall be considered on the design procedures described dependent on the extent of the fault:	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			
1.2	• The FAT can be completed if the faults are minor, and the system shall be considered acceptable, subject to the fault being fixed during warranty. A FAT shall also be repeated on a new version of the system incorporating a fix for the fault.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			
1.2	• Testing faults resulting from test procedure error or operator error shall be repeated. The test may be repeated immediately if the error is detected at the time of the FAT.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)				
1.2	• Major faults during the FAT shall lead to abandoning the FAT and rescheduling it for a later date pending the fault being resolved appropriately by the equipment provider.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			
1.2	• The FAT tests specified shall be repeated for the SAT.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.3. Factory acceptance test (FAT)	✓			

Remarks

PM/Contractor	QDC
Contractor Construction	**Third Party (if applicable)**

Checklist : HFC-CKL-1002	Checklist	APPROVED DATE	DISCIPLINE
PRE-INSTALLATION OF ITS CABINET	HFC-CKL-1002		ITS
PROJECT TITLE: Road Access To Resort Core (RA4RC)	WBS	CONTRACTOR/SUBCONTRACTOR	
WIR No.	CONSTRUCTION- Intelligent Transportation System Works for INSTALLATION AND OPERATION of ITS CABINET	HAIF	

ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection

The work is ready for inspection			Document Reviewed	Work Inspected	Test Records Verified
Name: Muharis	Signature	Date: 17/7/26	Name: Zawar Ahmad	Signature: 12/8/26	
Contractor QC Inspector			QDC Supervision Consultant		

Form Ref. No. QD0004-ADM-TEM-QTY-00003– Rev.0A

Document Properties

Event Log

Tell us what you think

Update Document

History

Rev: 04 09/03/2026
A - Approved #40
Received on: QIC-WTRAN-194336

Rev: 03 27/01/2026
B - Approved with Comments #32
Received on: QIC-WTRAN-191569

Rev: 02 31/12/2025
B - Approved with Comments #24
Received on: QIC-WTRAN-189495

Rev: 01 19/11/2025
C - Revise and Resubmit #16
Received on: QIC-WTRAN-187095

Rev: 00 04/11/2025
C - Revise and Resubmit #8
Received on: QIC-WTRAN-186653

QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00078 - PDF
ITS SHOP DRAWINGS (UPGRADE) ITS COMMUNICATION CABINET - Sheet -05

Viewer | Properties | Packages | Related Items | Sent | Downloaded

PDF

QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00078_04.pdf
(1.6MB)


Download File

Download with Markup Summary


Confidentiality

Type Drawing	Sub-Document Type Drawing - Shop Drawings
Floor Level 00 - Non-Specific	Revision 04
Status A - Approved	Discipline Intelligent Transportation System
Issued for Construction Documentation	Originator Code HFC - Haif and Freyssinet Consortium
Project Code QRXM114000 - Interim Road Access to Resort Core	Contract C00618VO01 - RA2RC Interim Road
Area - Geographical / Zone 02 - Roads	Venue - Building / Facilities RO5 - RA2RC
Sub-Venue Category	Confidential No
Print Size	Reference
Date Created	Revision Date 15/02/2026
Scheduled Completion Date	Required for Handover
Review Source WF-074540	Review Status A - Approved
Version 40	


H = 1800mm x W = 800mm x D = 600mm

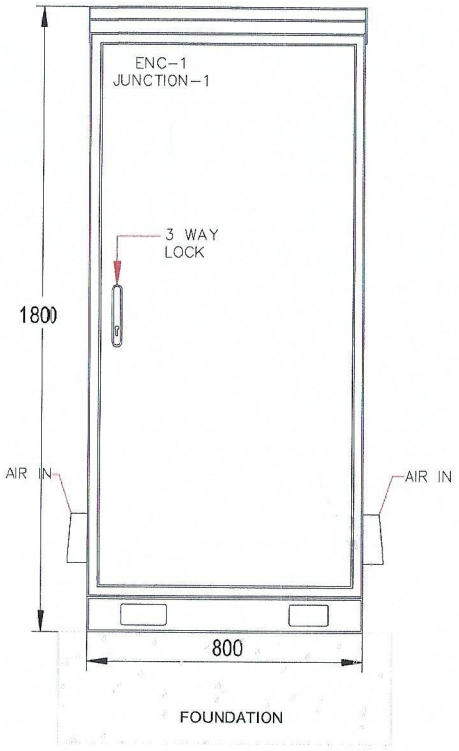


FRONT VIEW

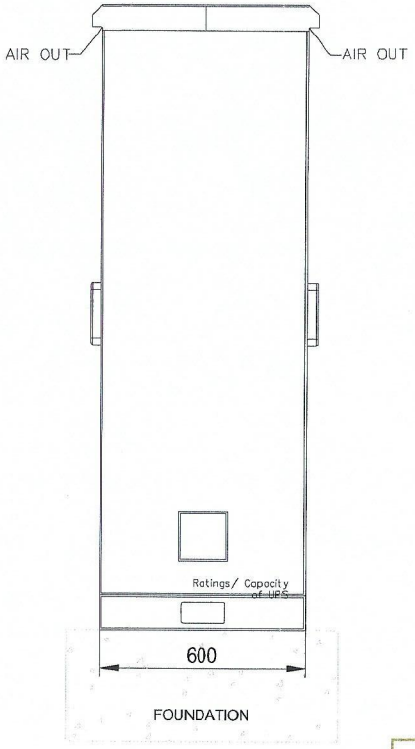

SIDE VIEW

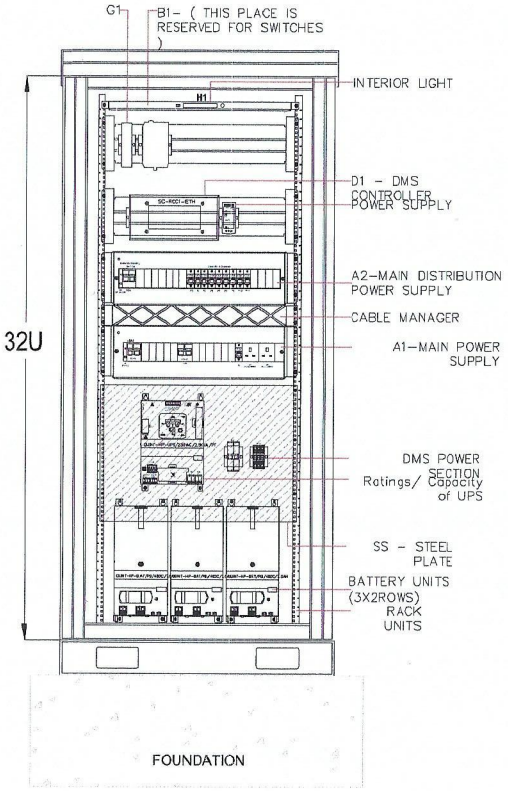

FRONT (INTERAL VIEW)

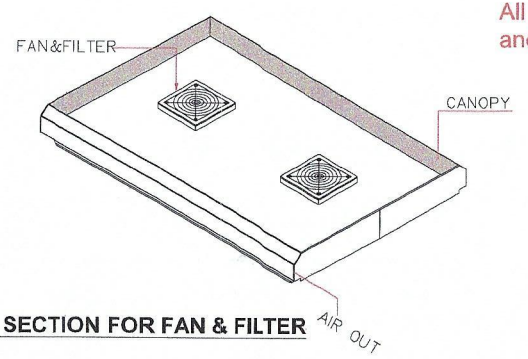

CROSS SECTION FOR FAN & FILTER

All the work shall be carried out in accordance with project specification and relevant standards & codes

UPS & BATTERY CALLCULATIONS

REQUIRED NO OF UPS	QTY: 1 – {TEMP: 60 °C } QUINT-HP-UPS/230AC/2.5KVA/PT
REQUIRED NO OF BATTERIES	QTY: 6 – {TEMP: 40 °C} QUINT-HP-BAT/PB/48DC/7.0AH/PT
BATTERY CAPACITY (AH)	= LOAD (VA) X BACKUP TIME (H) X SAFETY FACTOR / (BATTERY VOLTAGE (V) X EFFICIENCY OF UPS) = (2300 x 0.5 x 1.6) / (48 x 0.95) = 40.35AH


Reference shall be provided for 2300VA load

ITS CABINET

NOTES
1. UNLESS OTHERWISE SPECIFIED, DIMENSIONS ARE IN MILLIMETERS.
2. DRAWING SHALL NOT BE SCALED. ONLY WRITTEN DIMENSION SHALL BE FOLLOWED.
3. THE DRAWINGS SHALL BE READ IN CONJUNCTION WITH ALL RELEVANT DOCUMENTS AND PROJECT SPECIFICATIONS.
4. THE DUCTS CONNECTION DIRECTION TO BE AS PER SITE PLANS.
5. CABINETS TO BE PLACED SO THAT MAINTENANCE CREW FACE THE APPROACHING TRAFFIC WHILE WORKING.

القدية
Qiddiya

Consultant's Information
HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com
Zuhair Fayez Partnership



Notes:
1). All DIMENSIONS ARE IN METERS UNLESS OTHERWISE NOTED

REFERENCE I.F.C DRAWING NO:
QRXP117115-DAH-VORA2R-DWG-ITS-R2-Z00000-200000 TO 2000007
QRXP117115-DAH-VORA2R-DWG-ITS-R2-Z00000-5000004
QRXP117115-DAH-VORA2R-DWG-ITS-R2-Z00000-5000005

LEGEND:

Rev. No.	Date	Description	Appr.
00	20-10-2025	FOR REVIEW AND APPROVAL	C
01	09-11-2025	FOR REVIEW AND APPROVAL	C
02	28-12-2025	FOR REVIEW AND APPROVAL	B
03	14-01-2026	FIRST REVIEW	B
04	15-02-2026	FINAL REVIEW	
--	--	--	--
--	--	--	--

Consultant
Contractor
ITS Contractor
Project:

Job title: ROAD ACCESS TO RESORT CORE

Drawing title:
ITS SHOP DRAWINGS (UPGRADE)
ITS COMMUNICATION CABINET

Sheet number: SHEET 1 / 1

Scale: NTS

Drawn: M.Elsayed | Checked: M.Abuzaid
Designed: | Approved:


Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-R05-00078
Revision: 04

ITS Cabinets

5pcs for DMS

1pc for RWIS

3pcs for Junctions 1,2,3

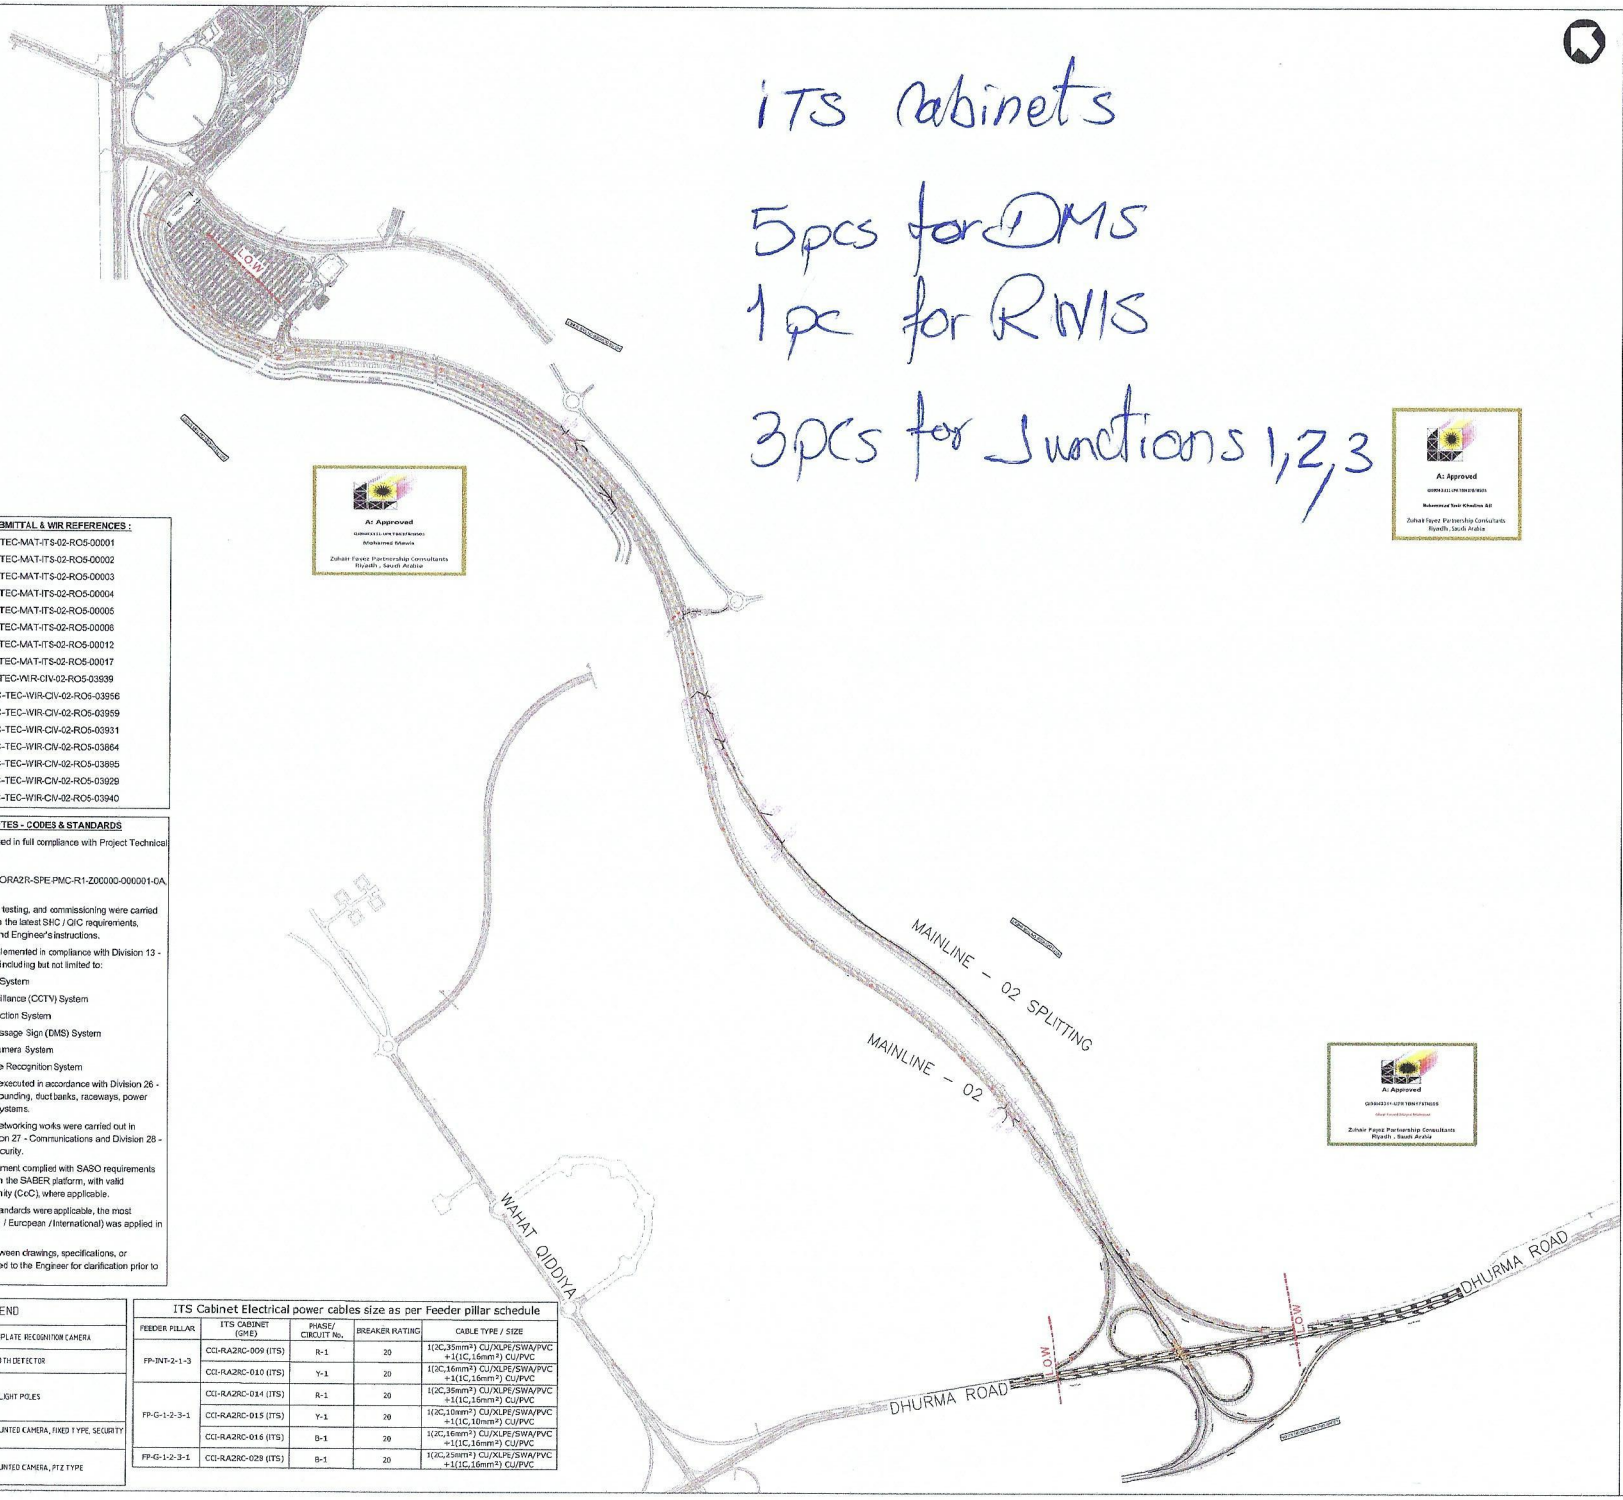

MATERIAL SUBMITTAL & WIR REFERENCES :

1. QRXM114000-HFC-TEC-MAT-ITS-02-R05-00001
2. QRXM114000-HFC-TEC-MAT-ITS-02-R05-00002
3. QRXM114000-HFC-TEC-MAT-ITS-02-R05-00003
4. QRXM114000-HFC-TEC-MAT-ITS-02-R05-00004
5. QRXM114000-HFC-TEC-MAT-ITS-02-R05-00005
6. QRXM114000-HFC-TEC-MAT-ITS-02-R05-00006
7. QRXM114000-HFC-TEC-MAT-ITS-02-R05-00012
8. QRXM114000-HFC-TEC-MAT-ITS-02-R05-00017
9. QRXM-114000HFC-TEC-WIR-CIV-02-R05-03939
10. QRXM-114000HFC-TEC-WIR-CIV-02-R05-03956
11. QRXM114000-HFC-TEC-WIR-CIV-02-R05-03959
12. QRXM114000-HFC-TEC-WIR-CIV-02-R05-03931
13. QRXM114000-HFC-TEC-WIR-CIV-02-R05-03864
14. QRXM114000-HFC-TEC-WIR-CIV-02-R05-03865
15. QRXM114000-HFC-TEC-WIR-CIV-02-R05-03929
16. QRXM114000-HFC-TEC-WIR-CIV-02-R05-03940

GENERAL NOTES - CODES & STANDARDS

1. All works were executed in full compliance with Project Technical Specifications (Ref: QRXP117 115-DAH-VORA2R-SPE-PMC-R1-Z00000-000001-0A, March 2025).
2. Installation, materials, testing, and commissioning were carried out in accordance with the latest SHC / QIC requirements, approved drawings, and Engineer's instructions.
3. ITS systems were implemented in compliance with Division 13 - Special Construction, including but not limited to:
   - 137700 - ITS Cabinet System
   - 137710 - Traffic Surveillance (CCTV) System
   - 137715 - Vehicle Detection System
   - 137730 - Dynamic Message Sign (DMS) System
   - 137740 - Red Light Camera System
   - 137760 - License Plate Recognition System
4. Electrical works were executed in accordance with Division 26 - Electrical, including grounding, duct banks, raceways, power supply, and earthing systems.
5. Communication and networking works were carried out in compliance with Division 27 - Communications and Division 28 - Electronic Safety & Security.
6. All products and equipment complied with SASO requirements and were registered on the SABER platform, with valid Certificates of Conformity (CoC), where applicable.
7. Where international standards were applicable, the most stringent standard (US / European / International) was applied in case of conflict.
8. Any discrepancies between drawings, specifications, or standards were reported to the Engineer for clarification prior to execution.

ITS LEGEND	
	LICENSE PLATE RECOGNITION CAMERA
	BLUETOOTH DETECTOR
	STREET LIGHT POLES
FIXED	POLE MOUNTED CAMERA, FIXED TYPE, SECURITY
PTZ	POLE MOUNTED CAMERA, PTZ TYPE

ITS Cabinet Electrical power cables size as per Feeder pillar schedule


FEEDER PILLAR	ITS CABINET (GME)	PHASE/ CIRCUIT No.	BREAKER RATING	CABLE TYPE / SIZE
FP-INT-2-1-3	CCI-RA2RC-009 (ITS)	R-1	20	1(2C,35mm²) CU/XLPE/SWA/PVC +1(1C,16mm²) CU/PVC
	CCI-RA2RC-010 (ITS)	Y-1	20	1(2C,16mm²) CU/XLPE/SWA/PVC +1(1C,16mm²) CU/PVC
FP-G-1-2-3-1	CCI-RA2RC-014 (ITS)	R-1	20	1(2C,35mm²) CU/XLPE/SWA/PVC +1(1C,16mm²) CU/PVC
	CCI-RA2RC-015 (ITS)	Y-1	20	1(2C,10mm²) CU/XLPE/SWA/PVC +1(1C,10mm²) CU/PVC
	CCI-RA2RC-016 (ITS)	B-1	20	1(2C,16mm²) CU/XLPE/SWA/PVC +1(1C,16mm²) CU/PVC
FP-G-1-2-3-1	CCI-RA2RC-029 (ITS)	B-1	20	1(2C,25mm²) CU/XLPE/SWA/PVC +1(1C,16mm²) CU/PVC

القديـــة
Qiddiya

Consultant's information

HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com

Zuhair Fayez Partnership



Notes:
1). All DIMENSIONS ARE IN METERS UNLESS OTHERWISE NOTED

REFERENCE SHOP DRAWING NO:
1-QRXM114000-HFC-DRW-SDW-ITS-02-R05-00001

AS-BUILT

LEGEND:

- JUNCTION BOX TYPE 2 (JB)
- 4W — UPVC DUCT, 4 #100mm (POWER & COMMUNICATION)
- 2W — UPVC DUCT, 2 #50dia (POWER & COMMUNICATION)
- ITS POWER & COMMUNICATION CABLE
- VARIABLE MESSAGE SIGN (VMS)
- ITS CABINET GROUND MOUNTED ENCLOSURE (GME)
- ROADWAY WEATHER INFORMATION SYSTEM (RWIS) WITH AQM
- 6S-WAY 110mm HDPE DUCT BANK SAND ENCASED
- 6C-WAY 110mm HDPE DUCT BANK ROAD CROSSING CONCRETE ENCASED
- MANHOLE TYPE JRC1L-E
- VMS - 01 — SHEET No / DEVICE ABBREVIATION / DEVICE No IN THE CORRESPONDING SHEET

Rev. No.	Date	Description	Appr.
00	9-2-2026	FOR REVIEW AND APPROVAL	
01	14-04-2026	FOR REVIEW AND APPROVAL	
02	30-04-2026	FOR REVIEW AND APPROVAL	
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--

Consultant
Contractor — شركة مرفق Hail Company
ITS Contractor — TRAFFIC TECH
Project: القديـــة Qiddiya

Job title: ROAD ACCESS TO RESORT CORE

Drawing title: AS-BUILT FOR ITS (UPGRADE) LOCATION PLAN

Sheet number: SHEET 1 OF 17

Scale: 1:7500 @ A0

Drawn: M.Elsayed	Checked: M.Abuzaid
Designed:	Approved:

Drawing number: QRXM114000-HFC-DRW-ASB-ITS-02-R05-00001

Revision: 02
