QIDDIYA DEVELOPMENT COMPANY						
DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00004	REVISION NUMBER:	00	ISSUED BY:	PMO	Qiddiya
DOCUMENT TITLE	WIR FORM	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022	

WORK INSPECTION REQUEST (WIR) FORM

Contractor:	HAIF-FREYSSINET JV
Project:	RA2RC & JUCTTION
Contract No.:	QPMO-410-CT-00618
Work Inspection Request Number:	QRXM114000-HFC-TEC-WIR-ITS-02-RO5-00086

شركة حايف Haif Company — HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☑	Quality	☐	Project Controls	☐
Civil / Structural	☐	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

WORK DESCRIPTION

Inspection / Test Location:	Interim Road (Connection points for Traffic controller), Main Line-02		
GIS/GPS GeoTag Coordinates (If applicable)			
Inspection Date:	29-Sep-2026	Inspection Start Time:	9:00 am
ITP:	QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00006	Checklist:	HFC-CKL-9003
Spec's / Dwg. Ref.:	QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00005 1,61,71	Approved Method Statement Number:	QRXM114000-HFC-TEC-MST-ITS-02-RO5-00001
Attachments:	☑ Drawings ☐ Data Sheets ☐ TQs/RFI ☐ OTHER		

DESCRITPTION OF WORK

Inspection request for installation of Connection points for Traffic controller, at Upgrade and Junction area, at Interim Road Main Line -02

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Complies with Approved ITPs/Checklists?	◉ YES ○ NO ○ NA	REMARKS	
All Strucutral Embedded Items Cleared?	◉ YES ○ NO ○ NA	WIR Number	
Embedded Electrical Items Cleared by Electrical QC?	◉ YES ○ NO ○ NA	WIR Number	
Embedded Mechanical Items Cleared by Mechanical QC?	◉ YES ○ NO ○ NA	WIR Number	

Accepted:	◉
Accepted with Comments (See Remarks):	○
Rejected (See Remarks):	○

REMARKS:					
Name:	Naseem Ahmed	Signature:	Naseem	Date:	29/9/26

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Project spec requirements?	◉ YES ○ NO	Okay to Proceed with next activity?	◉ YES ○ NO ○ NA

Accepted:	◉
Accepted with Comments (See Remarks):	○
Rejected (See Remarks):	○

REMARKS:					
Name:		Signature:		Date	

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Haif Company / Freyssinet — HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
Location: 00	**Date:** 4 -June-2026
Document Title: **Inspection & Test Plan for Inteligent Transportation System Works for TRAFFIC SIGNAL SYSTEM**	**Ref No:** QRXM114000-HFC-TEC-ITP-ITS-00006
	Rev No: 00

Department: ☐ Architectural ☐ Structural ☒ Electrical ☐ Mechanical ☐ Authority ☐ Civil

Type: ☐ Pre-Qualification ☐ Method Statement ☐ Material Submittal ☐ Sample ☒ ITP

Document Description: This is Inspection&Test Plan for Inspection&Test Plan for Inteligent Transportation system Works for TRAFFIC SIGNAL SYSTEM

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-ITP-ITS-00005	**Inspection&Test Plan for Inteligent Transportation system Works for TRAFFIC SIGNAL SYSTEM**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz Signature: Date: 4 -June-2026	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments: All the work shall be carried out inaccordance with project specification, relevant standards & codes and manufacturer recommendations.







Below portion for Client use only

Comments:

Signed by: Signature: Date:

HAIF-FSA JV Inspection & Test Plan	I &TP	APPROVED DATE	DISCIPLINE
Intelligent Transportation System Works for TRAFFIC SIGNAL SYSTEM	**HFC-ITP-090**		**ITS**
PROJECT TITLE:WBS	CONTRACTOR/SUBCONTRACTOR		
WIR No.	CONSTRUCTION- Intelligent Transportation System Works for TRAFFIC SIGNAL SYSTEM	HAIF	

ITEM NO.	PROJECT PHASE	TASK / ACTIVITY	Quality Requirements /references/ specifications	Quality Record	INSPECTION RESPONSIBILITY ASSIGNMENTS			REMARKS
					Contractor	Third Party	Consultant	
1.0 DOCUMENT REVIEW								
1.7		Material Approval & Shop Drawing - Vehicle Video Detection System	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0B Section 137714 VEHICLE DETECTION SYSTEM IFC Drawing QRXP117115-DAH-VORA2R-DWG-GEN-R3-Z00000-5000006	QRXM114000-HFC-TEC-MAT-ITS-02-R05-00010 Material Approval Request for VEHICLE VIDEO DETECTION SYSTEM Approved SHOP DRAWINGS: QRXM114000-HFC-DRW-SDW-ITS-02-R05-00019-R02 QRXM114000-HFC-DRW-SDW-ITS-02-R05-00031-R01 QRXM114000-HFC-DRW-SDW-ITS-02-R05-00044-R01	R		H	
2.0 MATERIAL RECEIVING INSPECTION								
2		Material receiving inspection, protection & storage	QD0002-ADM-TEM-QMS00007[0A] MaterialReceiving Inspection in site HFC-CKL-9001	QD0002-ADM-TEM-QMS00007[0A] MaterialReceivingInspection in site HFC-CKL-9001	H		H	MIR to be submitted
3.0 WORK INSTALLATION								
3.1		PRE - INSTALLATION	HFC-CKL-9002	HFC-CKL-9002	H		H	
3.2		INSTALLATION	HFC-CKL-9003	HFC-CKL-9003	H		H	
3.3		TESTING	HFC-CKL-9004	HFC-CKL-9004	H		H	

GENERAL NOTES

1	Surveillance: QA/QC organization to monitor work in progress without notice from Construction Organization
2	Witness: QA/QC organization shall be notified of the timing of Inspection or test in advance. However, the inspection or test shall be performed as scheduled if the QA/QC organization representative is not present
3	Hold: QA/QC organization shall be notified of the timing of inspection or test in advance. Inspection or test shall not be carried out without the QA/QC organization representative in attendance.
4	If the Main Contractor delegates the assigned responsibility to the Subcontractor, then the Main Contractor will have the same degree of responsibility as assigned to Consultant.

LEGEND

H	Hold Point for QC Inspection/ Test	R	Review of Documents
W	Witness Inspection/T	RH	Review & approval of Documents
S	Surveillance		

Checklist : HFC-CKL-9003

INSTALLATION OF TRAFFIC SIGNAL SYSTEM

PROJECT TITLE: Road Access To Resort Core (RA2RC)

WIR No

Checklist	APPROVED DATE	DISCIPLINE
HFC-CKL-9003		ITS
WBS	CONTRACTOR/SUBCONTRACTOR	

CONSTRUCTION-
Intelligent Transportation System Works for
INSTALLATION AND OPERATION of
TRAFFIC SIGNAL SYSTEM


HAIF

ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
1.0	**INSTALLATION OF TRAFFIC SIGNAL SYSTEM - EMERGENCY VEHICLE PRE-EMPTION SYSTEM (EVPS)**					
ITEM NO.	**Check Points & Acceptance Criteria**	**Reference**	**Pass**	**Fail**	**Not Applicable**	**Re-Inspection**
5.0	**INSTALLATION OF TRAFFIC SIGNAL SYSTEM - TRAFFIC SIGNAL CONTROLLER**					
5.1	Are all Shop Drawings, Method Statement and Material Submittals were approved ?	SHC 306 SECTION 12,TRAFFIC SIGNALS, 12.2.3.TRAFFIC SIGNAL CONTROLS SPECIFICATIONS	✓			
5.2	Are all TRAFFIC SIGNAL CONTROLLERS and installed as per approved Material Submittals?	SHC 306 SECTION 12,TRAFFIC SIGNALS, 12.2.3.TRAFFIC SIGNAL CONTROLS SPECIFICATIONS	✓			
5.3	Are all TRAFFIC SIGNAL CONTROLLERS material quantity as per approved Material Submittals and Shop Drawings?	SHC 306 SECTION 12,TRAFFIC SIGNALS, 12.2.3.TRAFFIC SIGNAL CONTROLS SPECIFICATIONS	✓			
5.4	Is installation performed in accordance with the applicable standards, requirements, manufacturers' guidelines and any authorities having jurisdiction	SHC 306 SECTION 12,TRAFFIC SIGNALS, 12.2.3.TRAFFIC SIGNAL CONTROLS SPECIFICATIONS	✓			
5.5	Are the TRAFFIC SIGNAL CONTROLLER foundations installed as per approved shop drawings?	SHC 306 SECTION 12,TRAFFIC SIGNALS, 12.2.3.TRAFFIC SIGNAL CONTROLS SPECIFICATIONS	✓			
5.6	Is the TRAFFIC SIGNAL CONTROLLER levelled and plumbed?	SHC 306 SECTION 12,TRAFFIC SIGNALS, 12.2.3.TRAFFIC SIGNAL CONTROLS SPECIFICATIONS	✓			
5.7	Are the wirings within the controller cabinet neatly arranged,spaced and placed or enclosed in plastic tubing?	SHC 306 SECTION 12,TRAFFIC SIGNALS, 12.2.3.TRAFFIC SIGNAL CONTROLS SPECIFICATIONS	✓			
5.8	Are all the wirings inside the cabinet properly terminated?	SHC 306 SECTION 12,TRAFFIC SIGNALS, 12.2.3.TRAFFIC SIGNAL CONTROLS SPECIFICATIONS	✓			
5.9	Does the controller cabinet provided with surge arrester as per specifications and approved shop drawings?	SHC 306 SECTION 12,TRAFFIC SIGNALS, 12.2.3.TRAFFIC SIGNAL CONTROLS SPECIFICATIONS	✓			
5.10	Are the cables properly labeled as per approved shop drawings?	SHC 306 SECTION 12,TRAFFIC SIGNALS, 12.2.3.TRAFFIC SIGNAL CONTROLS SPECIFICATIONS	✓			
5.11	To be done prior to switching-on of the intersection	SHC 306 SECTION 12,TRAFFIC SIGNALS, 12.2.3.TRAFFIC SIGNAL CONTROLS SPECIFICATIONS	✓			

Remarks

PM/Contractor			**QDC**		
Contractor Construction			**Third Party (if applicable)**		
The work is ready for inspection			**Document Reviewed**	**Work Inspected**	**Test Records Verified**
Name	Signature	Date	Name	Signature	
Contractor QC Inspector		29/9/26	QDC Supervision Consultant		

Form Ref. No. QD0002-AD-FRM-QUT-00003 Rev. 00

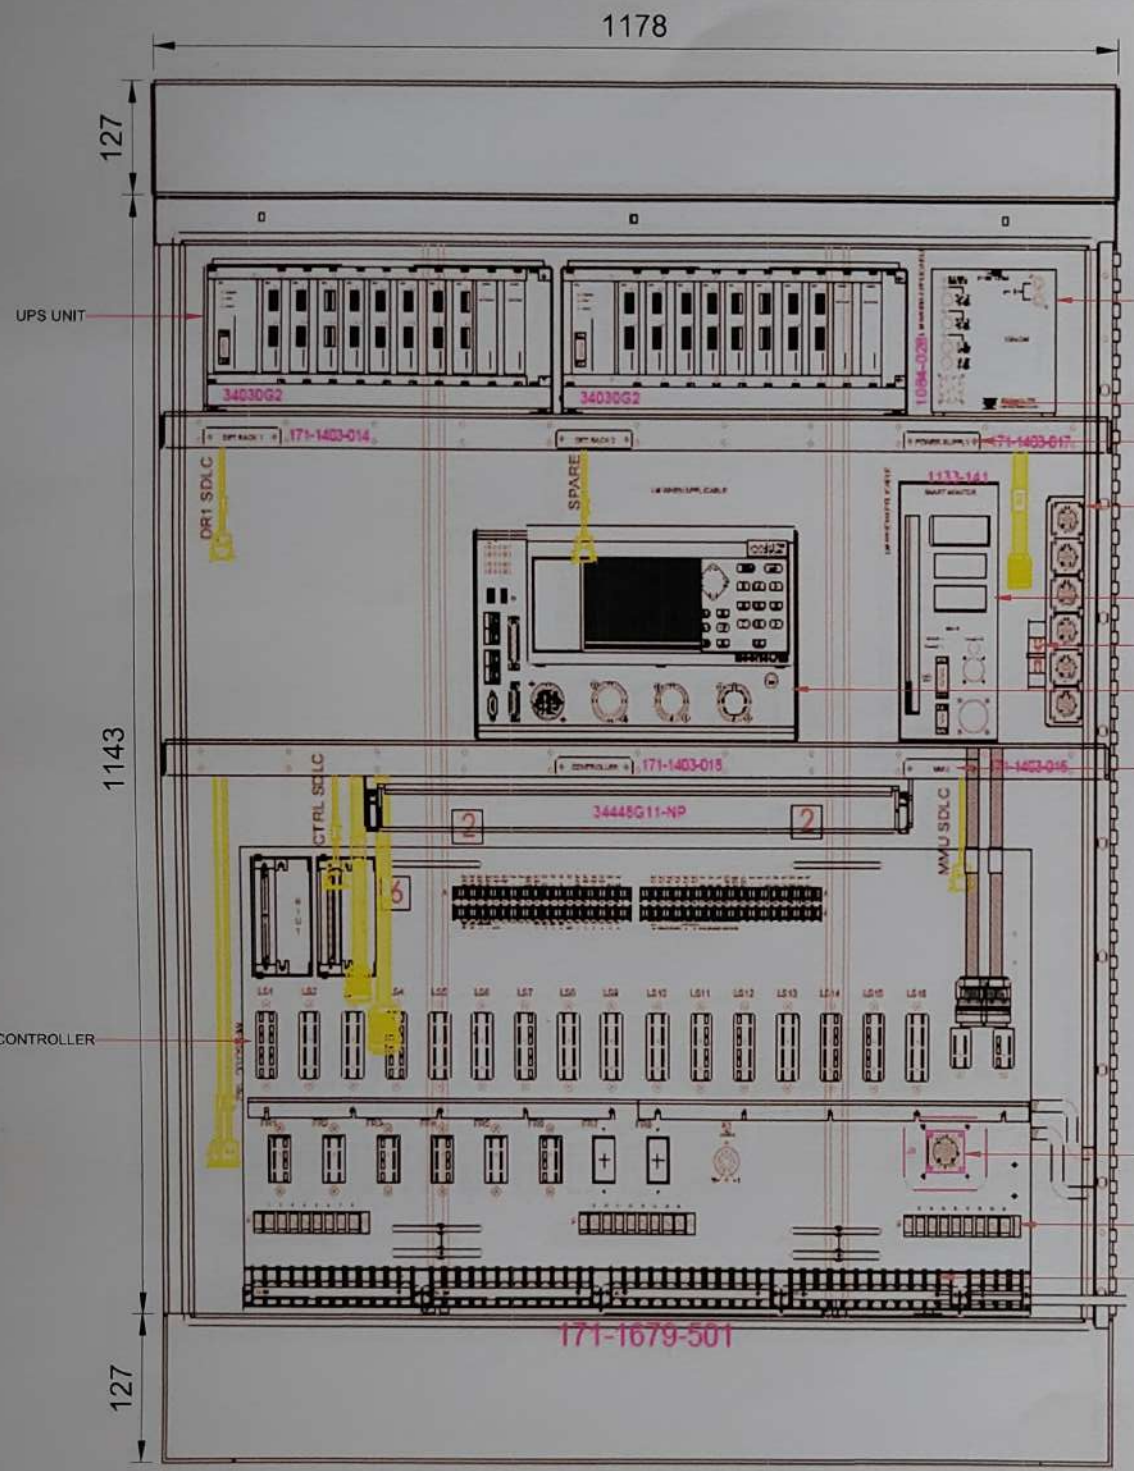

For comments refer to drawing #QRXM114000-HFC-DRW-SDW-ITS-02-ROS-00015

القدية
Qiddiya

Consultant's information

HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com

Zuhair Fayez Partnership

Notes:
1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3. THIS DRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.

REFERENCE I.F.C DESIGN DRAWING NO:
1. QRXP117113-OAH-VORA2R-DWG-ITS-R3-Z00000-Z000001
2. QRXP117113-OAH-VORA2R-DWG-ITS-R3-Z00000-S000001
3. QRXP117113-OAH-VORA2R-DWG-ITS-R3-Z00000-S000005
4. QRXP117113-OAH-VORA2R-DWG-ITS-R3-Z00000-S000006
5. QRXP117115-OAH-VORA2R-DWG-ITS-R3-Z00000-600001
6. QRXP117113-OAH-VORA2R-DWG-ICT-R3-Z00000-Z000000

LEGEND:

Rev. No.	Date	Description	Appr.
00	26-10-2025	FOR REVIEW AND APPROVAL	B
01	04-11-2025	FOR REVIEW AND APPROVAL	C
02	29-12-2025	FOR REVIEW AND APPROVAL	B
03	04-02-2026	FENAL REVISION	---
---	---	---	---
---	---	---	---
---	---	---	---

Consultant
Contractor
Mall Company
ITS Contractor
TRAFFIC
Project:
القدية Qiddiya

Job title: Road Access To Resort Core

Drawing title:
SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-1
TYPICAL INTERNAL ARRANGEMENT OF CONTROLLER CABINET

Sheet number:
SHEET 13 / 18

Scale: NTS

Drawn: M.Elbayed	Checked: M.Abuzaid
Designed:	Approved:

Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-ROS-00051
Revision: 03

NOTE:
MATERIAL SUBMITTAL REFERENCE NUMBER :
QRXM114000-HFC-TEC-MAT-ITS-02-ROS-00016

Specifications	TS2 Type T-P44 / Plug-N-Go
Dimensions	55 in H X 44 in W X 26 in D
Finish	Natural finish in/out
Material	Aluminum 0.125 in (5052-H32 aluminum)
Ship Weight	300 lbs.
