QIDDIYA DEVELOPMENT COMPANY					
DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00004	REVISION NUMBER:	00	ISSUED BY:	PMO
DOCUMENT TITLE	WIR FORM	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022

Qiddiya

WORK INSPECTION REQUEST (WIR) FORM

Contractor:	HAIF-FREYSSINET JV
Project:	RA2RC
Contract No.:	QPMO-410-CT-00618
Work Inspection Request Number:	QRXM114000-HFC-TEC-WIR-ITS-02-RO5-00090

شركة هيف Haif Company — Freyssinet — HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☑	Quality	☐	Project Controls	☐
Civil / Structural	☐	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

WORK DESCRIPTION

Inspection / Test Location:	INTERIM ROAD Sta. (Traffic signal Gantry)		
GIS/GPS GeoTag Coordinates (If applicable)			
Inspection Date:	04-Oct-2026	Inspection Start Time:	11:00 am
ITP:	QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00006	Checklist:	HFC-CKL-9003
Spec's / Dwg. Ref.:	QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00028 ,37,38	Approved Method Statement Number:	QRXM114000-HFC-TEC-MST-ITS-02-RO5-00002
Attachments:	☑ Drawings ☐ Data Sheets ☐ TQs/RFI ☐ OTHER		

DESCRITPTION OF WORK

Inspection request for Installation of Traffic signal Gantry (Cantilever), Junction-2 (13 mtr) , Junction-3 (12 mtr) and Junction-3 (16 mtr), at Access to Resort core interim Road. As per attached drawing.

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Complies with Approved ITPs/Checklists?	◉ YES ○ NO ○ NA	REMARKS	
All Strucutral Embedded Items Cleared?	○ YES ○ NO ○ NA	WIR Number	
Embedded Electrical items Cleared by Electrical QC?	○ YES ○ NO ○ NA	WIR Number	
Embedded Mechanical Items Cleared by Mechanical QC?	○ YES ○ NO ○ NA	WIR Number	

Accepted:	◉
Accepted with Comments (See Remarks):	○
Rejected (See Remarks):	○

REMARKS:					
Name:	Naseem Ahmed	Signature:	Naseem	Date:	4/10/26

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Project spec requirements?	○ YES ○ NO	Okay to Proceed with next activity?	○ YES ○ NO ○ NA

Accepted:	○
Accepted with Comments (See Remarks):	✓
Rejected (See Remarks):	○

REMARKS:	* final approval after signal heads installation * Cmply to all comments on the MAR Submission				
Name:	Mahmoud	Signature:		Date	4/10/26

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

* Any modifications to the shops drawings after approval are not considered.

Client:	Consultant:	Contractor:
Qiddiya		شركة هيف Haif Company

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
**Location: RA2RC ** Qiddiya INTERM ROAD	**Date:** 13-June-2026
Document Title: Method of Statement for Traffic Signal System Installation and Commissioning	Ref No: QRXM114000-HFC-TEC-MST-ITS-02-RO5-00002
	Rev No: 00

Department: ☐ Architectural ☐ Civil/Structural Electrical ☐ Mechanical ☐ Authority ☒ Others

Type: ☐ Pre-Qualification ☒ Method Statement ☐ Material Submittal ☐ Sample ☐ Other

Document Description: Method of Statement for Traffic Signal System Installation and Commissioning

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-MST-ITS-02-RO5-00002	**Method of Statement for Traffic Signal System Installation and Commissioning**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz Signature: Date: 13- June-2026	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments: All the work shall be carried out in accordance with approved shop drawings, project specifications & relevant standards & codes

Refer to the supplementary file "Traffic_Signal_MS_HSE_Comments_Sheet-16-06-2026.xlsx"









Below portion for Client use only

Comments:

Signed by: Signature: Date:

QIDDIYA DEVELOPMENT COMPANY						
DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00007	REVISION NUMBER:	0D	ISSUED BY:	PMO	Qiddiya
DOCUMENT TITLE	MIR FORM	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022	

MATERIAL INSPECTION REQUEST (MIR) FORM

Contractor:	HAIF COMPANY
Project:	QPMO-410-CT-00618- ROAD ACCESS TO RESORT CORE
Contract No.:	QI09043311-VO-0004
Material Inspection Request Number:	QRXM114000-HFC-TEC-MIR-ITS-02-RO5-00018

HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☐	Quality	☐	Project Controls	☐
Civil/Structural	☑	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

MATERIAL DESCRIPTION

Inspection / Test Location:	INTERIM ROAD MAIN LINE-02		
Material Name:	ITS SYSTEMS TRAFFIC SIGNALS POLES	Quantity:	04 No.
P.O Number		Delivery Note Number:	TTSDN-HAIF-290726-026
Approved Material Transmittal Number: (Aconex document Approval)	QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00015	Approval Date:	
Inspection Date:	30-Jul-2026	Inspection Start Time:	10:00 AM
ITP:	QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00006	Checklist:	HFC-CKL-9001
Spec's / Dwg. Ref.:	TRAFFIC TECH SECURITY W.L.L	Approved Method Statement Number:	
Attachments:	Test Certificate: ◉ Yes ○ No		
	IFC / Shop Drawings: ○ Yes ◉ No		

DESCRIPTION OF MATERIAL

6.42 Octagonal Traffic Signal Pole W Nos.1.0 Cantilever Arm 15.5 Mtrs & Base Plate Only (1 Nos.) 6.42M Octagonal Traffic Signal Pole W Nos.1.0 Cantilever Arm 16 Mtrs & Base Plate Only (1 Nos.) 6.42 M Octagonal Traffic Signal Pole W Nos.1.0 Cantilever Arm 12 Mtrs & Base Plate Only (1 Nos.) 6.42 Octagonal Traffic Signal Pole W Nos.1.0 Cantilever Arm 13 Mtrs & Base Plate Only (1 Nos.) for Interim Road Main Line-02

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Are Complete Details Mentioned in P.O and Delivery Note?	◉ YES ○ NO	REMARKS	
Complies with Approved ITPs/Checklists?	◉ YES ○ NO	REMARKS	
Signs of Physcial Damage?	○ YES ◉ NO	REMARKS	
Conforms to Approved Material Submittal?	○ YES ○ NO	REMARKS	
Accepted:			◉
Accepted with Comments:			○
Rejected (See Remarks):			○
REMARKS:			
Name:	Moataz Elkhateeb	Signature:	Date: 30-07-2026

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Material requirements?	○ YES ○ NO	Materials Are Stored correctly?	○ YES ○ NO ○ NA
Accepted:			○
Accepted with Comments:			☑
Rejected (See Remarks):			○
REMARKS:	Inspection done for aforementioned material in the site store open and found as per delivery note and material approval. Final approval subjected to provide quality test from TPL Comply the specifications		
Name:	Abdelrahman Hassan	Signature:	Date: 30/7/2026

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

Client:	Consultant:	Contractor:
Qiddiya		Half Company HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - **Interim Road Access to Resort Core**	**Project Code:** QRXM114000
Location: 00	**Date:** 21-September-2025
Document Title:**Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (Traffic Signal Controller)**	**Ref No:** QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00007 **Rev No:** 00

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☑ ITS ☐ Civil

Type: ☐ Pre-Qualification ☐ Method Statement ☒ Material Submittal ☐ Sample ☐ Other

Document Description:Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (Traffic Signal Controller)

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00007	**Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (Traffic Signal Controller)**

Enclosure:

Submitted By:	**Received By:**
Name: **Eng. Moataz** Signature: Date:21-September-2025	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments:

Refer to letter No. QRXM114000-ZFP-COR-LTR-ADM-00036; the proposed Traffic Signal Controller based on Australian standard SCATS is rejected and shall be installed only on a temporary basis for the opening of the Resort Core. The permanent Traffic Signal Controller shall comply with NEMA standards and shall be submitted for approval, with no additional cost to the Client. The Contractor/Supplier is hereby instructed to strictly adhere to the referenced letter and ensure full compliance with the following comments for the permanent Traffic Signal Controller.

1.Provide technical comparison sheet against project specification.
2.Clarify the system type (isolated or interconnected) and specify the controller type (Type-1, Type-2, Type-3)
3.SASO/SABER certificate to be provided
4.Provide Riser Diagram of Traffic signal system
5.ITP to be submitted separately
6.SAT test procedure to be provided
7.Provide reference that the subject material has Category C1 as mentioned in the submittal.

Below portion for Client use only

Comments:

Signed by: Signature: Date:

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Haif Company / Freyssinet / HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
Location: 00	**Date:** 4 -June-2026
Document Title: **Inspection & Test Plan for Inteligent Transportation System Works for TRAFFIC SIGNAL SYSTEM**	**Ref No:** QRXM114000-HFC-TEC-ITP-ITS-00006
	Rev No: 00

Department: ☐ Architectural ☐ Structural ☒ Electrical ☐ Mechanical ☐ Authority ☐ Civil

Type: ☐ Pre-Qualification ☐ Method Statement ☐ Material Submittal ☐ Sample ☒ ITP

Document Description: This is Inspection&Test Plan for Inspection&Test Plan for Inteligent Transportation system Works for TRAFFIC SIGNAL SYSTEM

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-ITP-ITS-00006	**Inspection&Test Plan for Inteligent Transportation system Works for TRAFFIC SIGNAL SYSTEM**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz Signature: Date: 4 -June-2026	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments: All the work shall be carried out inaccordance with project specification, relevant standards & codes and manufacturer recommendations.

A: Approved
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

A: Approved
Saud Nawab
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

A: Approved
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

Below portion for Client use only

Comments:

Signed by: Signature: Date:

HAIF-FSA JV Inspection & Test Plan

Inteligent Transportation System Works for TRAFFIC SIGNAL SYSTEM

PROJECT TITLE:WBS Access Road To Resort Core (RA2RC)

WIR No.

I &TP	APPROVED DATE	DISCIPLINE
HFC-ITP-090		ITS

CONTRACTOR/SUBCONTRACTOR

CONSTRUCTION-
Intelligent Transportation System Works for TRAFFIC SIGNAL SYSTEM — HAIF

ITEM NO.	PROJECT PHASE	TASK / ACTIVITY	Quality Requirements /references/ specifications	Quality Record	INSPECTION RESPONSIBILITY ASSIGNMENTS			REMARKS
					Contractor	Third Party	Consultant	
1.0 DOCUMENT REVIEW								
1.7		Material Approval & Shop Drawing - Vehicle Video Detection System	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0B Section 137714 VEHICLE DETECTION SYSTEM IFC Drawing QRXP117115-DAH-VORA2R-DWG-GEN-R3-Z00000-5000006	QRXM114000-HFC-TEC-MAT-ITS-02-R05-00010 Material Approval Request for VEHICLE VIDEO DETECTION SYSTEM Approved SHOP DRAWINGS: QRXM114000-HFC-DRW-SDW-ITS-02-R05-00019-R02 QRXM114000-HFC-DRW-SDW-ITS-02-R05-00031-R01 QRXM114000-HFC-DRW-SDW-ITS-02-R05-00044-R01	R		H	
2.0 MATERIAL RECEIVING INSPECTION								
2		Material receiving inspection, protection & storage	QD0002-ADM-TEM-QMS00007[0A] MaterialReceiving Inspection in site HFC-CKL-9001	QD0002-ADM-TEM-QMS00007[0A] MaterialReceivingInspection in site HFC-CKL-9001	H		H	MIR to be submitted
3.0 WORK INSTALLATION								
3.1		PRE - INSTALLATION	HFC-CKL-9002	HFC-CKL-9002	H		H	
3.2		INSTALLATION	HFC-CKL-9003	HFC-CKL-9003	H		H	
3.3		TESTING	HFC-CKL-9004	HFC-CKL-9004	H		H	

GENERAL NOTES

1	Surveillance: QA/QC organization to monitor work in progress without notice from Construction Organization
2	Witness: QA/QC organization shall be notified of the timing of Inspection or test in advance. However, the inspection or test shall be performed as scheduled if the QA/QC organization representative is not present
3	Hold: QA/QC organization shall be notified of the timing of inspection or test in advance. Inspection or test shall not be carried out without the QA/QC organization representative in attendance.
4	If the Main Contractor delegates the assigned responsibility to the Subcontractor, then the Main Contractor will have the same degree of responsibility as assigned to Consultant.

LEGEND

H	Hold Point for QC Inspection/ Test	R	Review of Documents
W	Witness Inspection/T	RH	Review & approval of Documents
S	Surveillance		

HFC-ITP-090

Checklist : HFC-CKL-9003

INSTALLATION OF TRAFFIC SIGNAL SYSTEM

PROJECT TITLE: Road Access To Resort Core (RA2RC)	Checklist: HFC-CKL-9003	APPROVED DATE:	DISCIPLINE: ITS
WIR No.	WBS:	CONTRACTOR/SUBCONTRACTOR:	

CONSTRUCTION- Intelligent Transportation System Works for INSTALLATION AND OPERATION of TRAFFIC SIGNAL SYSTEM — HAIF

ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
1.0	**INSTALLATION OF TRAFFIC SIGNAL SYSTEM - EMERGENCY VEHICLE PRE-EMPTION SYSTEM (EVPS)**					
ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
6.0	**INSTALLATION OF TRAFFIC SIGNAL SYSTEM - TRAFFIC SIGNAL POLE & GANTRIES**					
6.1	Are all Shop Drawings, Method Statement and Material Submittals were approved ?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2.2.SUPPORTING STRUCTURE SPECIFICATIONS	✓			
6.2	Are all TRAFFIC SIGNAL POLE AND GANTRIES installed as per approved Material Submittals?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2.2.SUPPORTING STRUCTURE SPECIFICATIONS	✓			
6.3	Are all TRAFFIC SIGNAL POLE AND GANTRIES material quantity as per approved Material Submittals and Shop Drawings?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2.2.SUPPORTING STRUCTURE SPECIFICATIONS	✓			
6.4	Is installation performed in accordance with the applicable standards, requirements, manufacturers' guidelines and any authorities having jurisdiction	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2.2.SUPPORTING STRUCTURE SPECIFICATIONS	✓			
6.5	Setting out and installation of foundations were installed as per approved Shop Drawings?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2.2.SUPPORTING STRUCTURE SPECIFICATIONS	✓			
6.6	Are the Poles/Gantries were tightened, and fixed on the foundation's anchor bolts?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2.2.SUPPORTING STRUCTURE SPECIFICATIONS	✓			
6.7	Are the Poles/Gantries leveled and plumbed?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2.2.SUPPORTING STRUCTURE SPECIFICATIONS	✓			
6.8	Are the serial numbers of test report verified and matching with material	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2.2.SUPPORTING STRUCTURE SPECIFICATIONS	✓			

Remarks

PM/Contractor				QDC			
Contractor Construction				Third Party (if applicable)			
The work is ready for inspection				Document Reviewed		Work Inspected	Test Records Verified
Name		Signature	Date	Name		Signature	
Faruq Abu Zaid	Contractor QC Inspector		5/8/26	Mahmoud	QDC Supervision Consultant		11/10/26

Form Ref. No. QD0002-ADM-TEM-QTY-00003– Rev.0A

QIDDIYA DEVELOPMENT COMPANY

DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00004	REVISION NUMBER:	0D	ISSUED BY:	PMO
DOCUMENT TITLE	WIR FORM	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022

WORK INSPECTION REQUEST (WIR) FORM

Contractor:	HAIF-FREYSSINET JV
Project:	RA2RC
Contract No.:	QPMO-410-CT-00618
Work Inspection Request Number:	QRXM114000-HFC-TEC-WIR-ITS-02-RO5-00042

HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☐	Quality	☐	Project Controls	☐
Civil / Structural	☑	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

WORK DESCRIPTION

Inspection / Test Location:	INTERIM ROAD Sta. JUNCTION -2 Aera		
GIS/GPS GeoTag Coordinates (If applicable)			
Inspection Date:	10-Jun-2026	Inspection Start Time:	10:30 am
ITP:	QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00006	Checklist:	HFC-CKL-9002
Spec's / Dwg. Ref.:	QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00015	Approved Method Statement Number:	QRXM114000-HFC-TEC-MST-CIV-02-RO5-00004
Attachments:	☑ Drawings ☑ Data Sheets ☐ TQs/RFI ☐ OTHER QRXM114000-HFC-DRW-SDW-CIV-02-RO5-00001		

DESCRITPTION OF WORK

Inspection request for Installing ITS Traffic Signal Cabinet Foundation Junction -2 & ITS Cabinet Ground Mounted Enclosure Foundation (GME) Junction -2 & Concrete Foundation of ITS Traffic Signal Pole 6.42m with Cantilever ARM 13m Junction -2 at Access to Resort core interim Road. ,Main Line-02 , As per attached drawing.

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Complies with Approved ITPs/Checklists?	◉ YES ○ NO ○ NA	REMARKS	
All Strucutral Embedded Items Cleared?	○ YES ○ NO ○ NA	WIR Number	
Embedded Electrical Items Cleared by Electrical QC?	○ YES ○ NO ○ NA	WIR Number	
Embedded Mechanical Items Cleared by Mechanical QC?	○ YES ○ NO ○ NA	WIR Number	

Accepted:	◉
Accepted with Comments (See Remarks):	○
Rejected (See Remarks):	○

REMARKS:					
Name:	Moataz Elkhateeb	Signature:		Date:	10-06-2026

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Project spec requirements?	☑ YES ○ NO	Okay to Proceed with next activity?	☑ YES ○ NO ○ NA


Accepted:	
Accepted with Comments (See Remarks):	☑
Rejected (See Remarks):	○

REMARKS:	Survey + Checked and found ok				
Name:	Mohammed Eltayeb	Signature:		Date	10/6/2026

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

installed one piece at junction 2 steel Gantry 13m

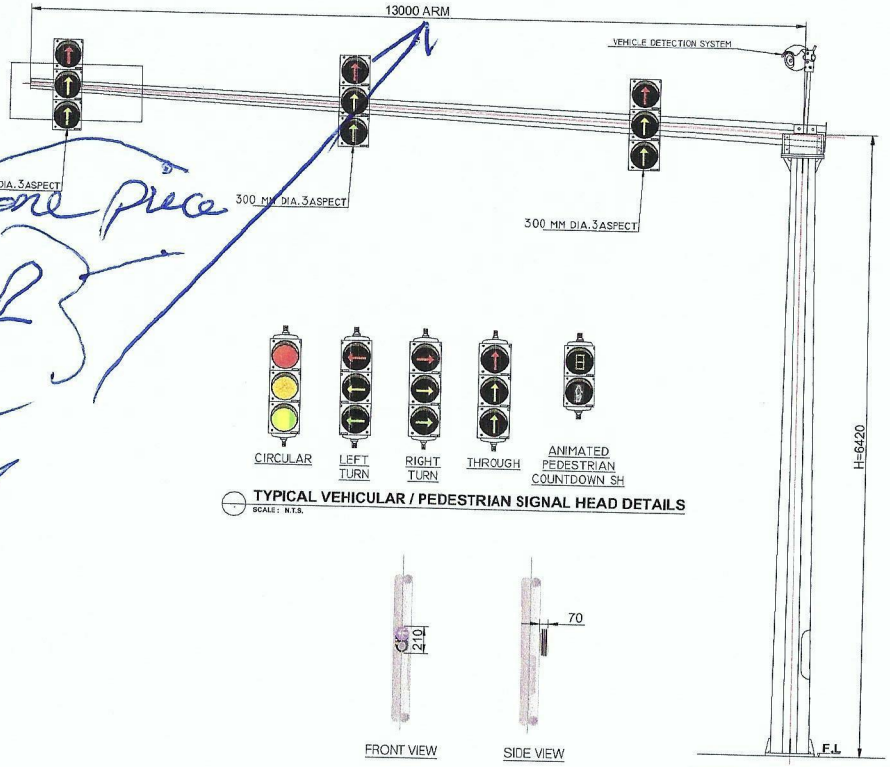


TYPICAL VEHICULAR / PEDESTRIAN SIGNAL HEAD DETAILS
SCALE: N.T.S.

DETAIL-A: PUSH BUTTON
SCALE: N.T.S.

TYPICAL SIGNAL GANTRY (CANTILEVER) DETAIL GANTRY NO - 17




For comments refer to the drawing # QRXM114000-HFC-DRW-SDW-ITS-02-R05-00024




Notes:
1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3. THIS DRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.


REFERENCE T.F.C DESIGN DRAWING NO:
1. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002
2. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000001
3. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000002
4. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000005
5. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000006
6. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000001
7. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000002
8. QRXP117115-DAH-VORA2R-DWG-ICT-R3-Z00000-2000000

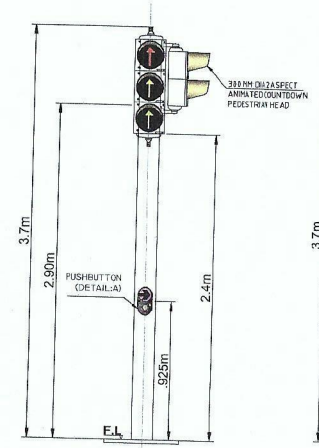


3.7m TRAFFIC SIGNAL HEADS, PED HEADS & PUSHBUTTON MOUNTING TYPICAL DETAILS
SCALE: N.T.S.

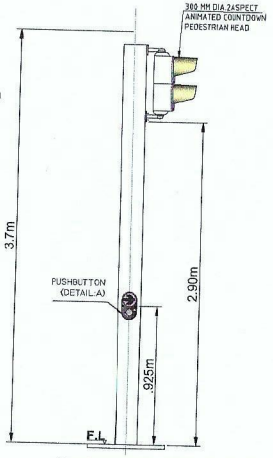

3.7m PED HEADS & PUSHBUTTON MOUNTING TYPICAL DETAILS
SCALE: N.T.S.

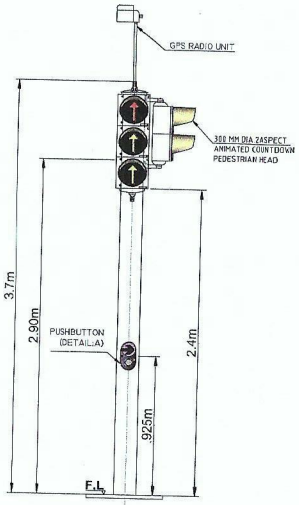

3.7m TYPICAL GPS RADIO UNIT INSTALLATION
SCALE: N.T.S.

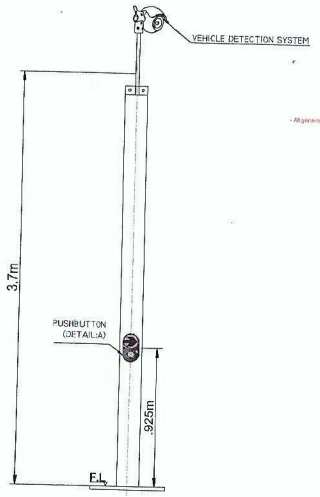

3.7m TYPICAL VEHICLE DETECTION CAMERA INSTALLATION
SCALE: N.T.S.

All general comments stated on drawing and previous Rev. shall considered.



Qiddiya

Consultant's Information

HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com

Zuhair Fayez Partnership

Rev. No.	Date	Description	Appr.
00	30-8-2025	FOR REVIEW AND APPROVAL	C
01	04-11-2025	FOR REVIEW AND APPROVAL	C
02	28-12-2025	FOR REVIEW AND APPROVAL	B
03	04-02-2026	FINAL REVISION	
--	--	--	--
--	--	--	--
--	--	--	--

Consultant
Contractor
ITS Contractor
Project:

Job title: Road Access To Resort Core

Drawing title:
SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-2
TYPICAL DETAILS+GPS RADIO UNIT ON 3.7m TRAFFIC SIGNAL POLE

Sheet number:
SHEET 5 / 19

Scale: NTS

Drawn: M.Elsayed | Checked: M.Abuzaid
Designed: | Approved:


Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-R05-00028
Revision: 03


26
3
8

16m Gantry installed at junction 3


steel Calumn on Cantilever

S1

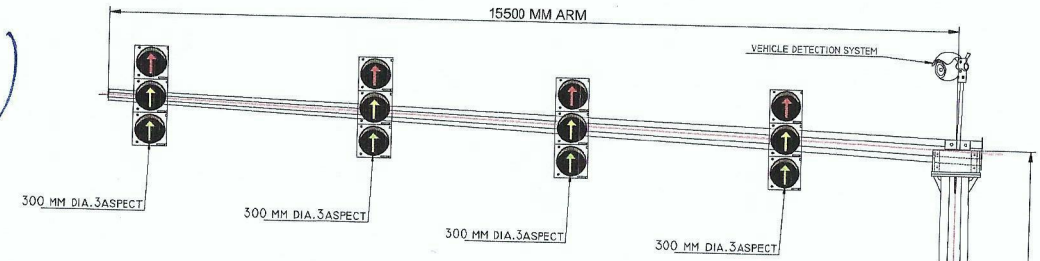


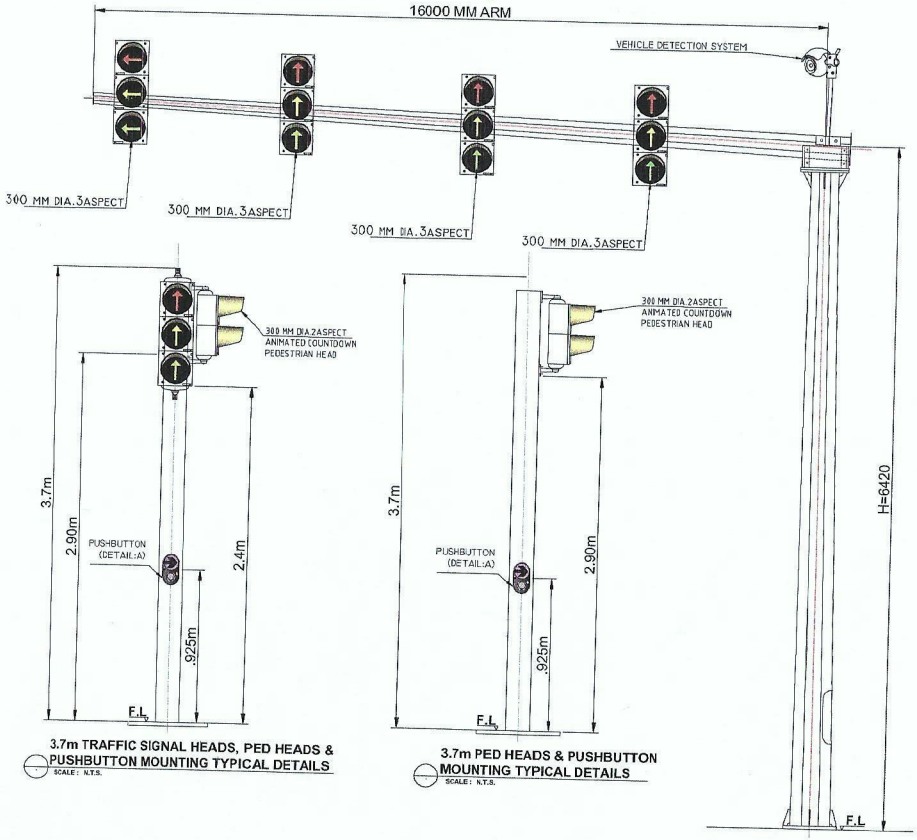

TYPICAL SIGNAL GANTRY (CANTILEVER) DETAIL GANTRY NO - 09




TYPICAL VEHICULAR / PEDESTRIAN SIGNAL HEAD DETAILS
SCALE : N.T.S.




DETAIL-A: PUSH BUTTON
SCALE : N.T.S.

3.7m TRAFFIC SIGNAL HEADS, PED HEADS & PUSHBUTTON MOUNTING TYPICAL DETAILS
SCALE : N.T.S.

3.7m PED HEADS & PUSHBUTTON MOUNTING TYPICAL DETAILS
SCALE : N.T.S.



TYPICAL SIGNAL GANTRY (CANTILEVER) DETAIL GANTRY NO - 20



Notes:
1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3. THIS DRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.


REFERENCE I.F.C DESIGN DRAWING NO:
1. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-2000003
2. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-5000001
3. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-5000002
4. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-5000005
5. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-5000006
6. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-6000001
7. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-6000002
8. QRXP117115-DAH-VORA2R-DWG-ICT-R3-200000-2000006

LEGEND:

Rev. No.	Date	Description	Appr.
00	31-8-2025	FOR REVIEW AND APPROVAL	C
01	08-11-2025	FOR REVIEW AND APPROVAL	C
02	28-12-2025	FOR REVIEW AND APPROVAL	C
03	04-02-2026	FINAL REVISION	
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--


Consultant
Project:
Contractor
ITS Contractor
Job title: Road Access To Resort Core
Drawing title: SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-3 TYPICAL DETAILS-1
Sheet number: SHEET 5 / 20
Scale: NTS
Drawn: M.Elsayed
Checked: M.Abuzaid
Designed:
Approved:
Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-R05-00037
Revision: 03


12m Gantry installed at Junction 3

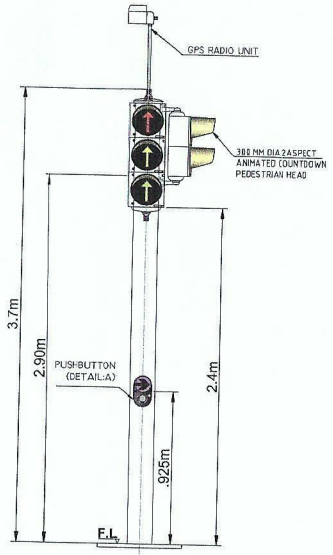


3.7m TYPICAL GPS RADIO UNIT INSTALLATION
SCALE : N.T.S.

For comments refer to the drawing # QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00033

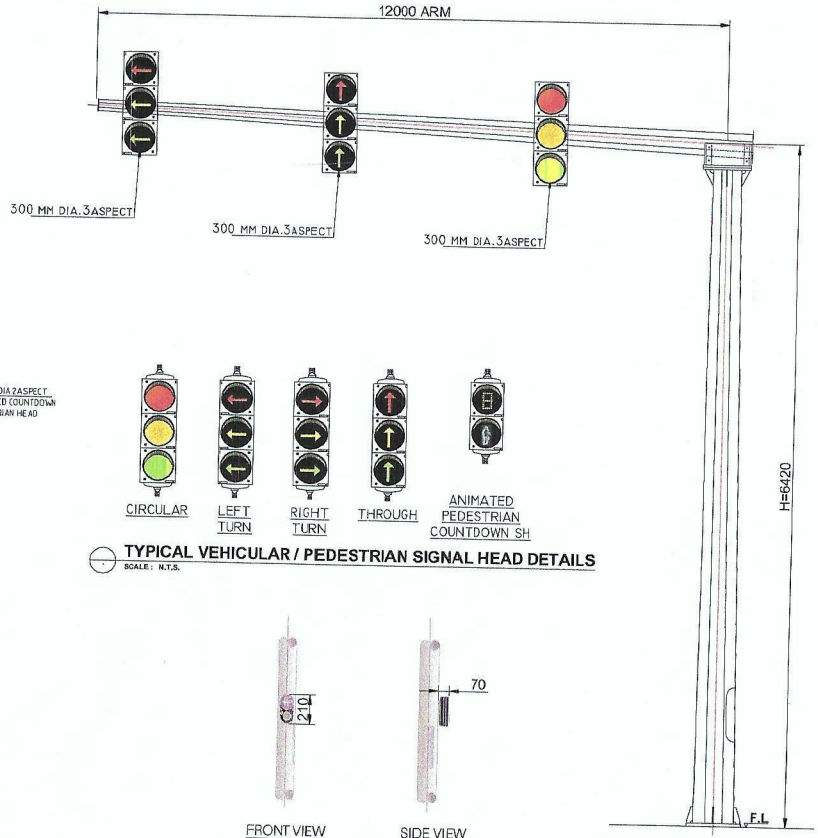

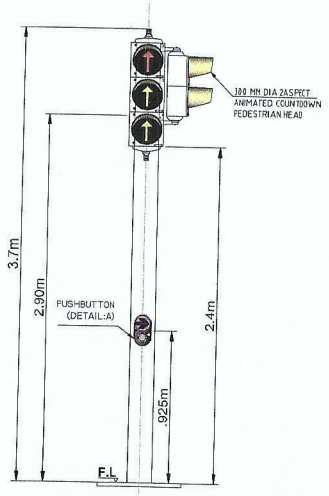

3.7m TRAFFIC SIGNAL HEADS, PED HEADS & PUSHBUTTON MOUNTING TYPICAL DETAILS
SCALE : N.T.S.

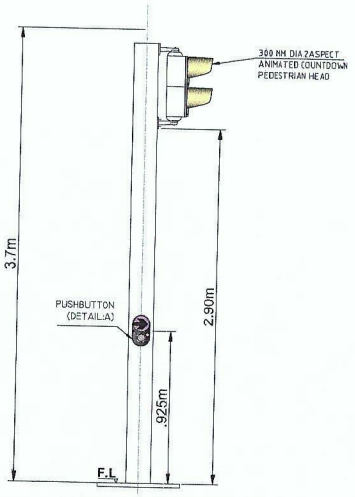


3.7m PED HEADS & PUSHBUTTON MOUNTING TYPICAL DETAILS
SCALE : N.T.S.

TYPICAL VEHICULAR / PEDESTRIAN SIGNAL HEAD DETAILS
SCALE : N.T.S.

DETAIL-A: PUSH BUTTON
SCALE : N.T.S.

TYPICAL SIGNAL GANTRY (CANTILEVER) DETAIL GANTRY NO - 10



Notes:
1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3. THIS DRAWING IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.

REFERENCE T.F.C DESIGN DRAWING NO:
1. QRXP117115-DAH-VOIA2R-DWG-ITS-R3-Z00000-2000001
2. QRXP117115-DAH-VOIA2R-DWG-ITS-R3-Z00000-5000001
3. QRXP117115-DAH-VOIA2R-DWG-ITS-R3-Z00000-5000002
4. QRXP117115-DAH-VOIA2R-DWG-ITS-R3-Z00000-5000005
5. QRXP117115-DAH-VOIA2R-DWG-ITS-R3-Z00000-5000006
6. QRXP117115-DAH-VOIA2R-DWG-ITS-R3-Z00000-6000001
7. QRXP117115-DAH-VOIA2R-DWG-ITS-R3-Z00000-6000002
8. QRXP117115-DAH-VOIA2R-DWG-ICT-R3-Z00000-2000000

LEGEND:

Rev. No.	Date	Description	Appr.
00	31-8-2025	FOR REVIEW AND APPROVAL	C
01	09-11-2025	FOR REVIEW AND APPROVAL	C
02	28-12-2025	FOR REVIEW AND APPROVAL	C
03	04-2-2026	FINAL REVIEW	
--	--	--	--
--	--	--	--
--	--	--	--

Consultant's information
HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com

Consultant
Contractor
ITS Contractor
Project:

Job title: Road Access To Resort Core


Drawing title:
SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-3
TYPICAL DETAILS-2+GPS RADIO UNIT ON 3.7m TRAFFIC SIGNAL POLE

Sheet number:
SHEET 6 / 20

Scale:NTS

Drawn:M.Elsayed | Checked: M.Abuzaid
Designed: | Approved:

Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00038
Revision 03

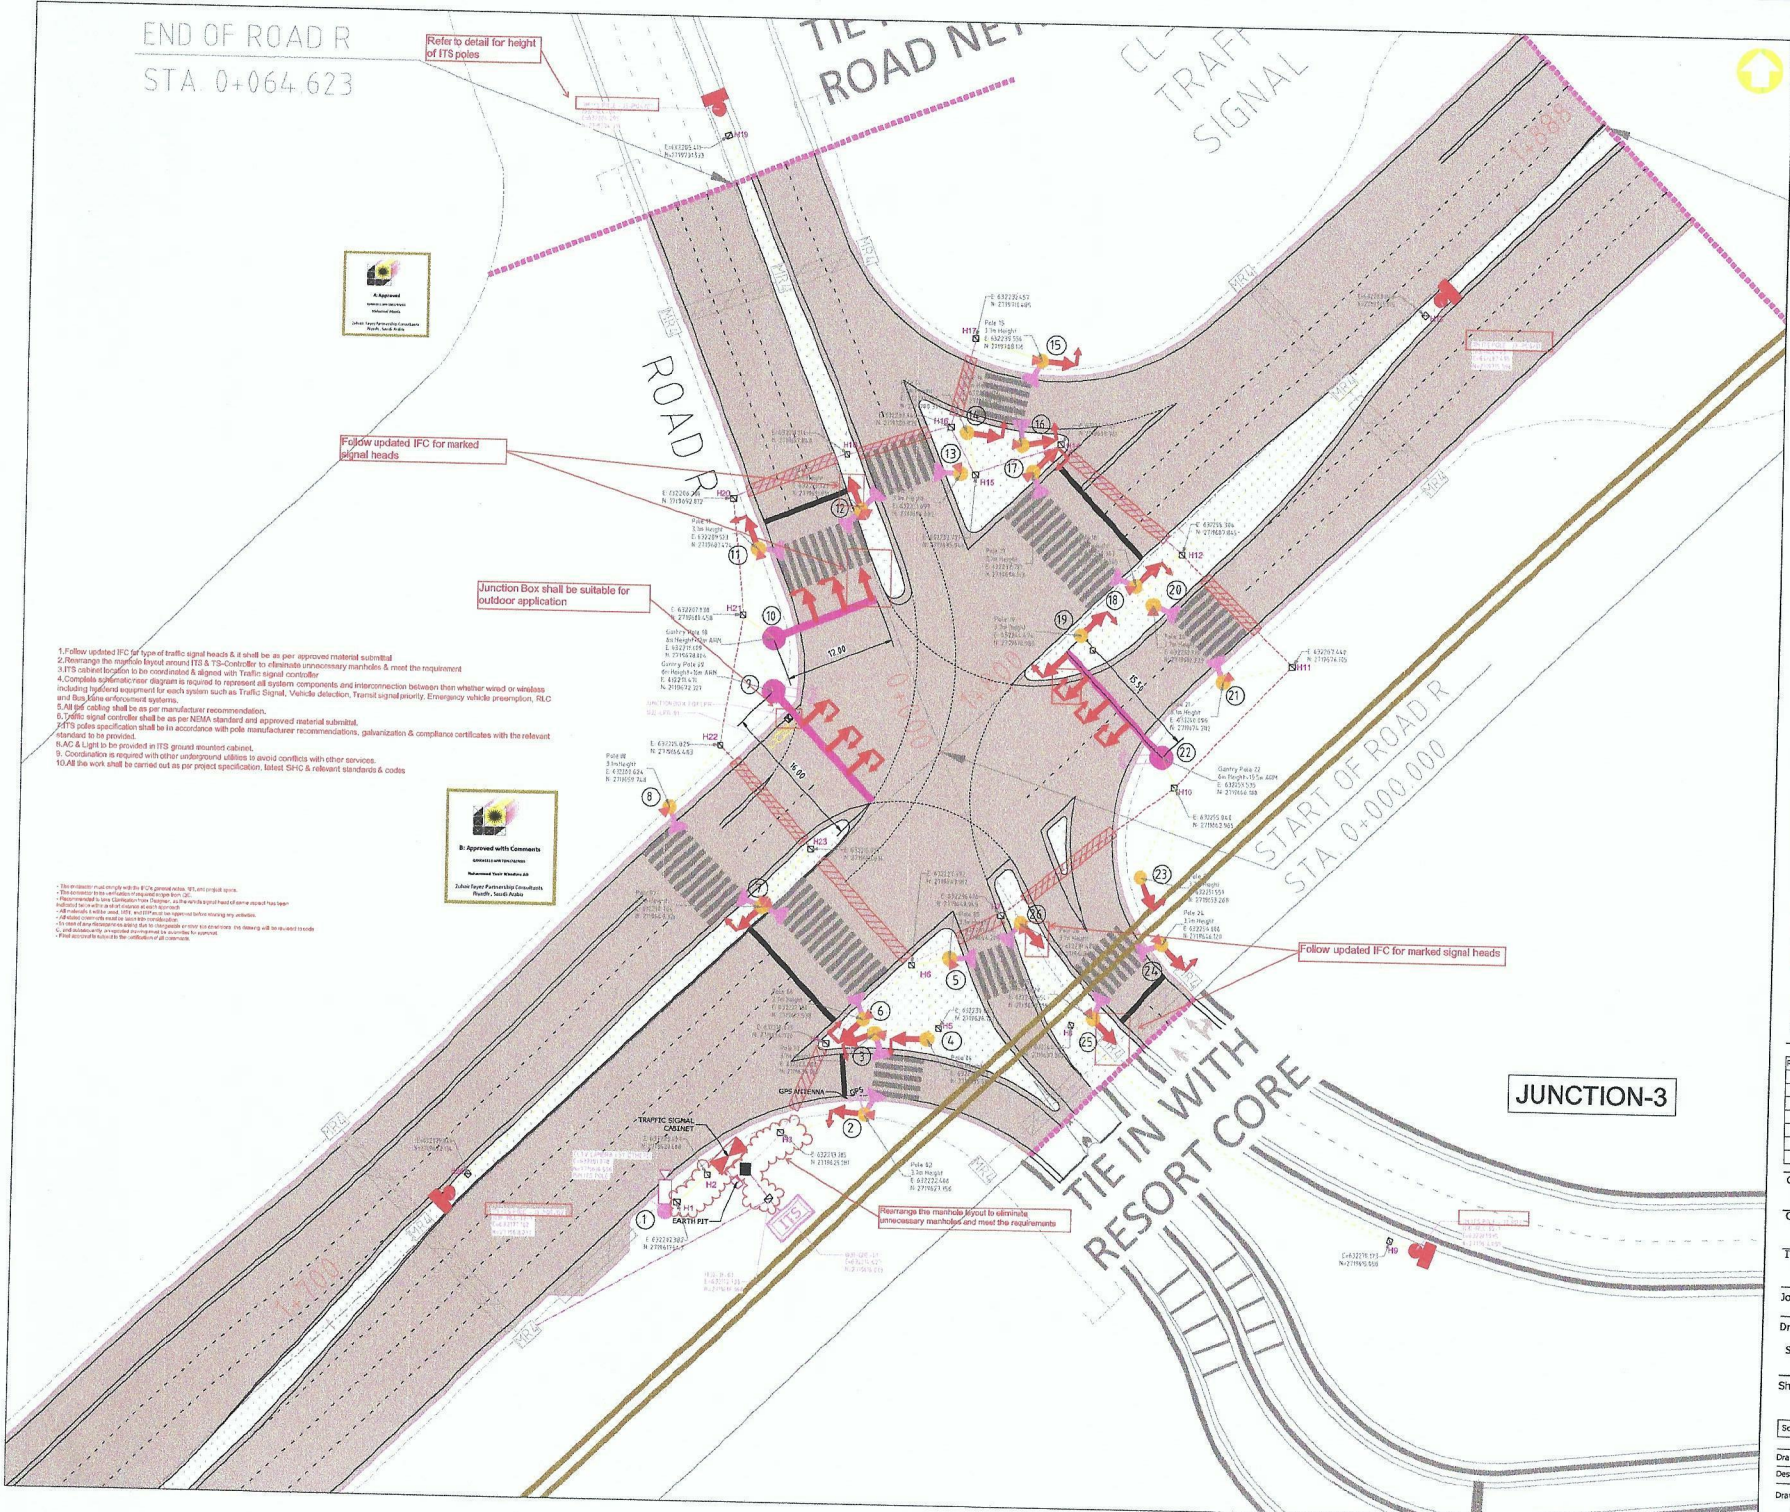

القديـة
Qiddiya

Consultant's information
HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com
Zuhair Fayez Partnership


Notes:
1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3. THIS DRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.

REFERENCE I.F.C DESIGN DRAWING NO:
1. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000003
2. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000001
3. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000002
4. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000005
5. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000006
6. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000001
7. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000002
8. QRXP117115-DAH-VORA2R-DWG-ICT-R3-Z00000-2000000

LEGEND:

Rev. No.	Date	Description	Appr.
00	31-8-2025	FOR REVIEW AND APPROVAL	c
01	08-11-2025	FOR REVIEW AND APPROVAL	--
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--

Consultant
Project:
Contractor
Hail Company
ITS Contractor
TRAFFIC TECH
Job title: Road Access To Resort Core
Drawing title: SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-3
Sheet number: SHEET 1 / 20
Scale: 1:1000 @ A0
Drawn: M.Sayed | Checked: M.Sayed
Designed: | Approved:
Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-R05-00033
Revision 01

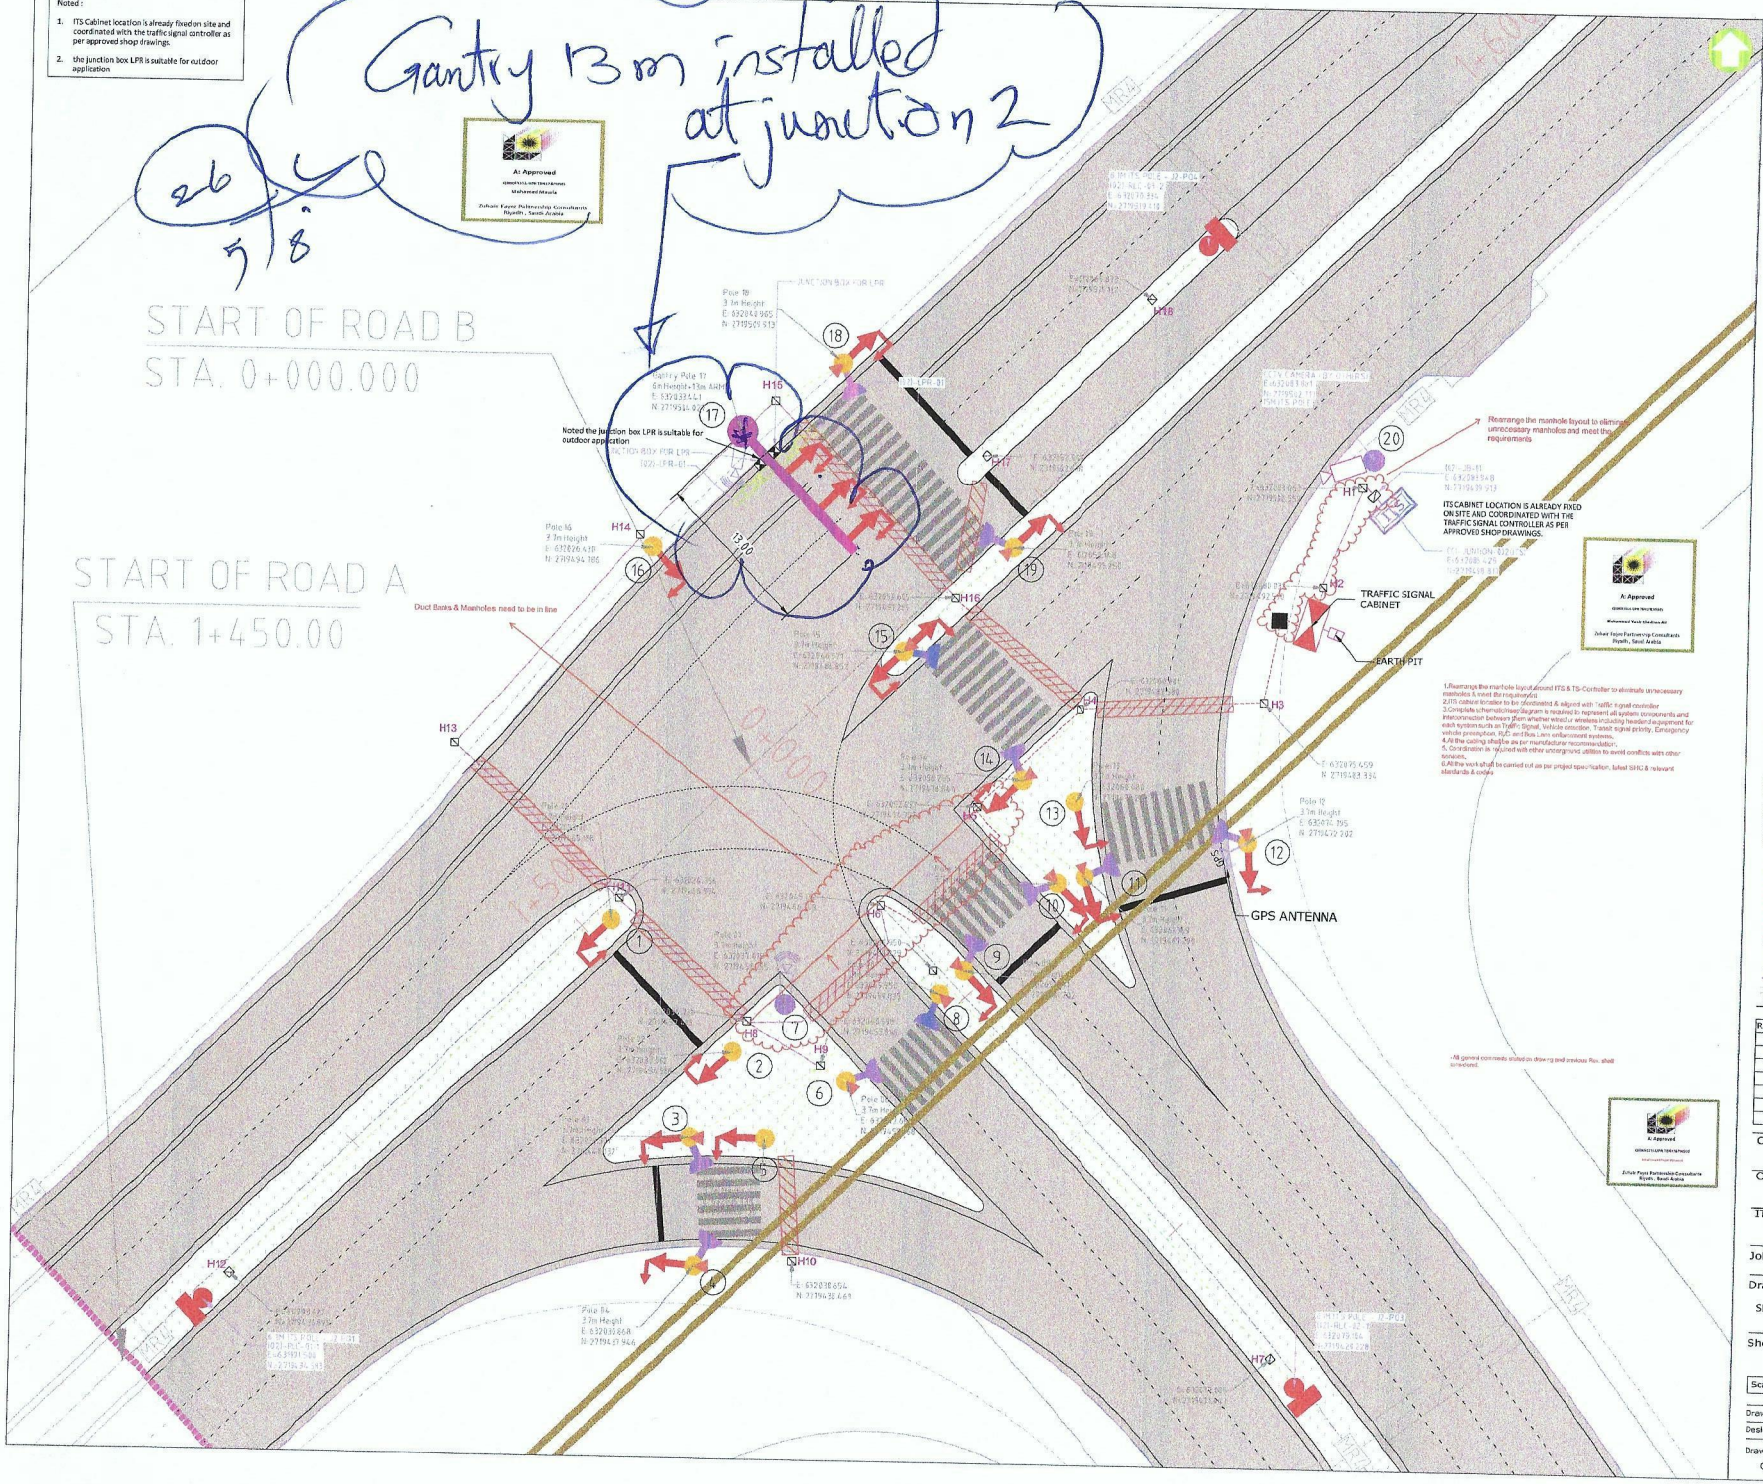

القدية
Qiddiya

Consultant's information

HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com

Zuhair Fayez Partnership

Notes:
1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3. THIS DRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.

REFERENCE I.F.C DESIGN DRAWING NO:
1. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002
2. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000001
3. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000002
4. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000005
5. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000006
6. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000001
7. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000002
8. QRXP117115-DAH-VORA2R-DWG-ICT-R3-Z00000-2000000

LEGEND:

Rev. No.	Date	Description	Appr.
00	30-8-2025	FOR REVIEW AND APPROVAL	C
01	04-11-2025	FOR REVIEW AND APPROVAL	B
02	04-02-2026	FINAL REVISION	
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--

Consultant
Contractor
Half Company
ITS Contractor
TRAFFIC TECH
Project:
القدية Qiddiya

Job title: Road Access To Resort Core

Drawing title: SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-2

Sheet number: SHEET 1 / 19


Scale:1:1000 @ A0


Drawn: M.Elsayed | Checked: M.Abuzaid
Designed: | Approved:

Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-R05-D0024

Revision 02


1-ALL DIMENSIONS ARE IN METER UNLESS OTHERWISE STATED.
2-THIS DRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ITS, ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.
3-ALL DIMENSIONS ARE CONFIRMED FROM THE MANUFACTURE.
3-BUSHINGS OR BELL ENDS TO BE INSTALLED AT ALL CONDUIT TERMINATIONS.
6-THE TOP OF THE COVERS TO BE PLACED 0.1M ABOVE FINAL LEVEL. GREEN AREAS AND SHALL SUITE THE SURROUNDING PURPOSE.
7-ALL FOUNDATIONS SHALL BE PRECAST AND SHALL BE WATER PROOF.
8-The Concrete Compressive Strength as per the specs for Reinforced Concrete to be 35 MPa.
9-The Concrete Compressive Strength as per the specs for Plain Concrete under foundations to be 25 MPa.
10-The Steel bar tensile strength as per the specs. to be 420 MPa.
11-Concrete cover for all foundations shall be 75mm.
12-All Structural Calculations done coordinated with consultant and manufacture in 16m arm gantry.
13-Foundation of gantry with arm 15.5m & 16m shall be taken OD (2.30*2.30*2)m
14-Foundation of gantry with arm 12m & 13m shall be taken OD(2*2*2)m

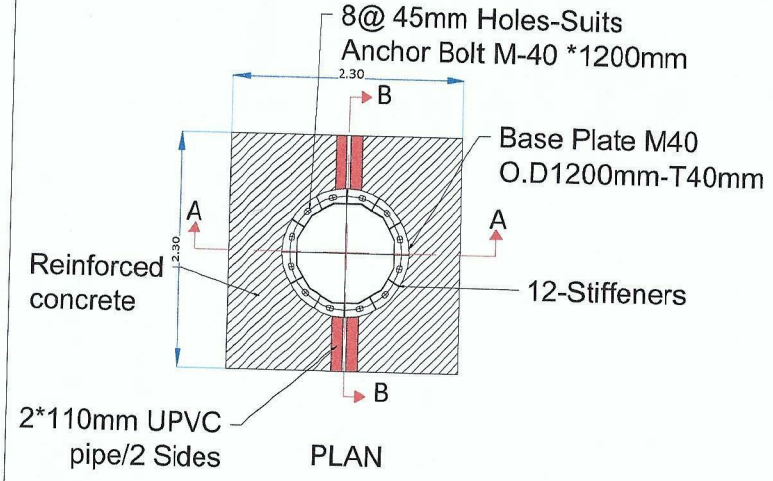


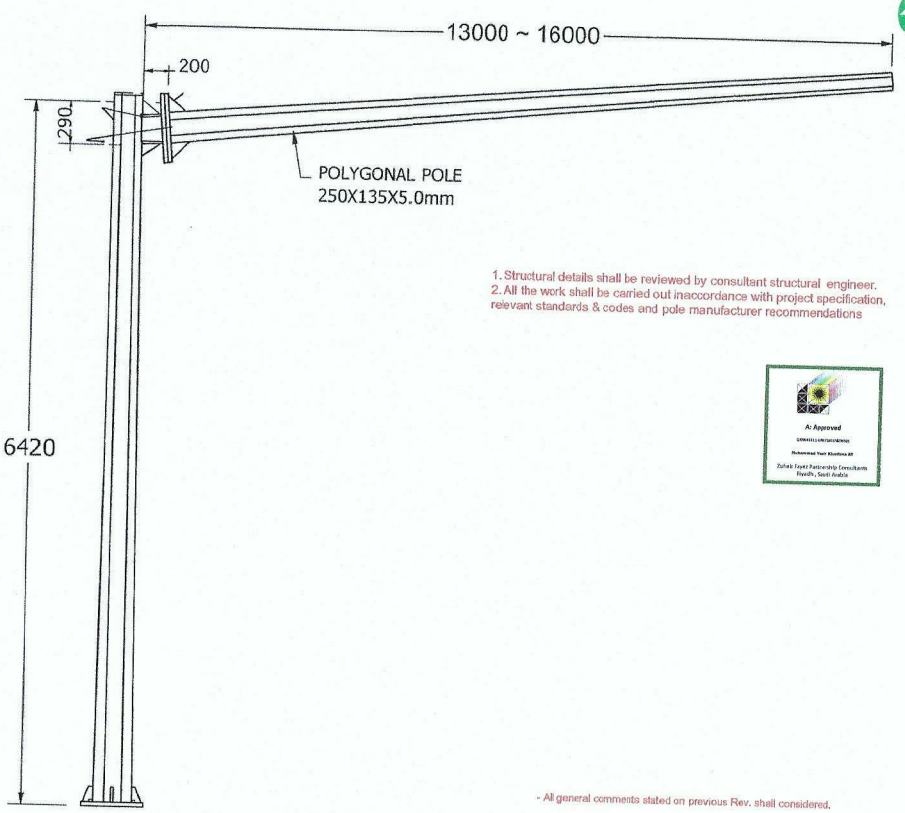

1. Structural details shall be reviewed by consultant structural engineer.
2. All the work shall be carried out inaccordance with project specification, relevant standards & codes and pole manufacturer recommendations

- All general comments stated on previous Rev. shall considered.

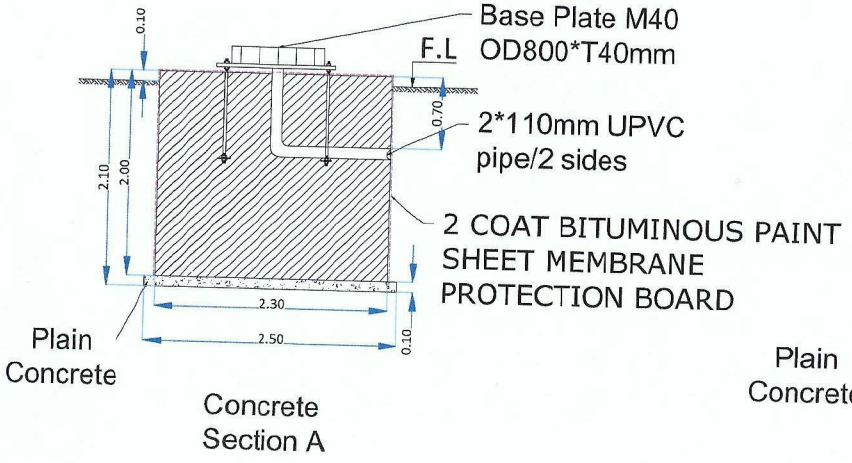

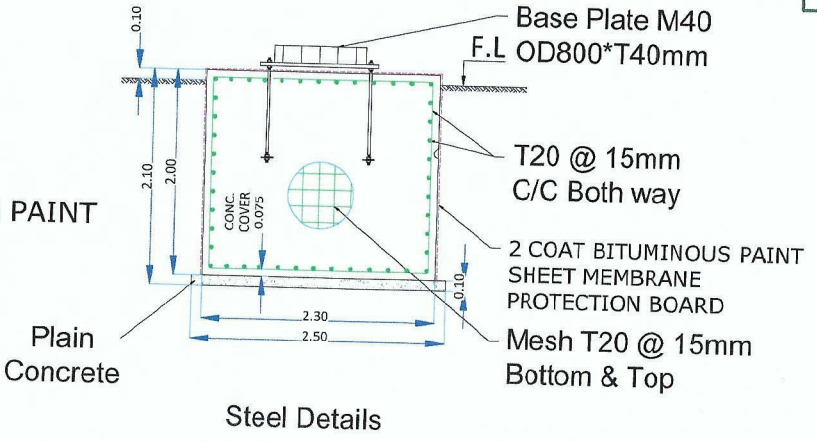


القديـــة
Qiddiya

Consultant's information

HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com

Zuhair Fayez Partnership



Notes:
1. ALL DIMENSIONS ARE IN METER UNLESS OTHERWISE STATED.
2. THIS DRAWINGSIS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.

REFERENCE I.F.C DESIGN DRAWING NO:
1. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002-PDF
2. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000003-PDF
3. QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00024
4. QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00033
5. Calculation Sheet from Approved Manufacture

LEGEND:
- SIGNAL CANTILEVER GANTRY : (6.42m Height+13m Arm)- Junction 2
- SIGNAL CANTILEVER GANTRY : (6.42m Height+12m Arm)- Junction 3
- SIGNAL CANTILEVER GANTRY : (6.42m Height+15.5m Arm)- Junction 3
- SIGNAL CANTILEVER GANTRY : (6.42m Height+16m Arm)- Junction 3

Rev. No.	Date	Description	Appr.
00	16-5-2026	FOR REVIEW AND APPROVAL	
01	20-05-2026	REVIEW AND APPROVAL	
02	02-06-2026	REVIEW AND APPROVAL	
03	13-06-2026	REVIEW AND APPROVAL	
--	--	--	--
--	--	--	--
--	--	--	--

Consultant
Contractor
Half Company
ITS Contractor
TRAFFIC TECH
Project:
القديـــة Qiddiya

Job title: Road Access To Resort Core

Drawing title: Shopdrawing Foundations of Traffic Pole 6.42m with Cantilever Arm at Junction 2 & 3

Sheet number: SHEET 1 / 1

Scale: N.T.S

Drawn: M.Elsayed | Checked: M.Abuzaid
Designed: | Approved:

Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00088 | Revision 03

PO	E	N	Z	Description
1	632212.144	2719679.148	662.232	Cantilver 12m
2	632212.635	2719677.221	662.219	Cantilver 12m
3	632210.685	2719676.766	662.213	Cantilver 12m
4	632210.216	2719678.687	662.202	Cantilver 12m
5	632211.078	2719678.162	662.332	Cantilver 12m
6	632211.58	2719678.337	662.337	Cantilver 12m
7	632211.774	2719677.836	662.34	Cantilver 12m
8	632211.242	2719677.637	662.331	Cantilver 12m
9	632211.424	2719673.994	662.209	Cantilver 16m
10	632213.018	2719672.357	662.198	Cantilver 16m
11	632211.384	2719670.737	662.227	Cantilver 16m
12	632209.777	2719672.401	662.212	Cantilver 16m
13	632210.95	2719672.387	662.34	Cantilver 16m
14	632211.394	2719671.926	662.342	Cantilver 16m
15	632211.853	2719672.349	662.341	Cantilver 16m
16	632211.414	2719672.8	662.344	Cantilver 16m
17	632033.424	2719502.63	660.769	Cantilver 13m
18	632034.838	2719503.975	660.768	Cantilver 13m
19	632033.474	2719505.398	660.794	Cantilver 13m
20	632032.053	2719504.034	660.768	Cantilver 13m
21	632032.756	2719504.043	660.854	Cantilver 13m
22	632033.45	2719503.333	660.854	Cantilver 13m
23	632034.17	2719504.012	660.856	Cantilver 13m
24	632033.466	2719504.716	660.847	Cantilver 13m

PO	E	N	Z	Description
1	632212.144	2719679.148	662.232	Cantilver 12m
2	632212.635	2719677.221	662.219	Cantilver 12m
3	632210.685	2719676.766	662.213	Cantilver 12m
4	632210.216	2719678.687	662.202	Cantilver 12m
5	632211.078	2719678.162	662.332	Cantilver 12m
6	632211.58	2719678.337	662.337	Cantilver 12m
7	632211.774	2719677.836	662.34	Cantilver 12m
8	632211.242	2719677.637	662.331	Cantilver 12m
9	632211.424	2719673.994	662.209	Cantilver 16m
10	632213.018	2719672.357	662.198	Cantilver 16m
11	632211.384	2719670.737	662.227	Cantilver 16m
12	632209.777	2719672.401	662.212	Cantilver 16m
13	632210.95	2719672.387	662.34	Cantilver 16m
14	632211.394	2719671.926	662.342	Cantilver 16m
15	632211.853	2719672.349	662.341	Cantilver 16m
16	632211.414	2719672.8	662.344	Cantilver 16m
17	632033.424	2719502.63	660.769	Cantilver 13m
18	632034.838	2719503.975	660.768	Cantilver 13m
19	632033.474	2719505.398	660.794	Cantilver 13m
20	632032.053	2719504.034	660.768	Cantilver 13m
21	632032.756	2719504.043	660.854	Cantilver 13m
22	632033.45	2719503.333	660.854	Cantilver 13m
23	632034.17	2719504.012	660.856	Cantilver 13m
24	632033.466	2719504.716	660.847	Cantilver 13m
