QIDDIYA DEVELOPMENT COMPANY

DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00004	REVISION NUMBER:	OD	ISSUED BY:	PMO
DOCUMENT TITLE	WIR FORM	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022

Qiddiya

WORK INSPECTION REQUEST (WIR) FORM

Contractor:	HAIF-FREYSSINET JV
Project:	RA2RC
Contract No.:	QPMO-410-CT-00618
Work Inspection Request Number:	QRXM114000-HFC-TEC-WIR-ITS-02-RO5-00093

Haif Company — Freyssinet — HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☑	Quality	☐	Project Controls	☐
Civil / Structural	☐	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

WORK DESCRIPTION

Inspection / Test Location:	INTERIM ROAD Sta. (Traffic signal Gantry (Cantilever)		
GIS/GPS GeoTag Coordinates (If applicable)			
Inspection Date:	17-Sep-2026	**Inspection Start Time:**	11:30 am
ITP:	QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00006	**Checklist:**	HFC-CKL-9003
Spec's / Dwg. Ref.:	QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00033 ,37	**Approved Method Statement Number:**	QRXM114000-HFC-TEC-MST-ITS-02-RO5-00002
Attachments:	☑ Drawings ☐ Data Sheets ☐ TQs/RFI ☐ OTHER		

DESCRITPTION OF WORK

Inspection request for Installation of Traffic signal Gantry (Cantilever), Junction-3 (15.5 mtr),at Access to Resort core interim Road. As per attached drawing.

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Complies with Approved ITPs/Checklists?	◉ YES ○ NO ○ NA	REMARKS	
All Strucutral Embedded Items Cleared?	○ YES ○ NO ○ NA	WIR Number	
Embedded Electrical items Cleared by Electrical QC?	○ YES ○ NO ○ NA	WIR Number	
Embedded Mechanical Items Cleared by Mechanical QC?	○ YES ○ NO ○ NA	WIR Number	

Accepted:	
Accepted with Comments (See Remarks):	◉
Rejected (See Remarks):	○

REMARKS:					
Name:	Naseem Ahmed	**Signature:**	Naseem	**Date:**	17/9/26

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Project spec requirements?	○ YES ○ NO	Okay to Proceed with next activity?	○ YES ○ NO ○ NA

Accepted:	
Accepted with Comments (See Remarks):	○
Rejected (See Remarks):	◉

REMARKS:	* final approval Subject to Signal heads instellation * Cmply to all Comments on the MAR Submission				
Name:	Mahmoud	**Signature:**		**Date**	4/10/26

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

Revise the Submission date

Client:	Consultant:	Contractor:
Qiddiya		شركة هيف Haif Company

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
**Location: RA2RC ** Qiddiya INTERM ROAD	**Date:** 13-June-2026
Document Title: Method of Statement for Traffic Signal System Installation and Commissioning	Ref No: QRXM114000-HFC-TEC-MST-ITS-02-RO5-00002
	Rev No: 00

Department: ☐ Architectural ☐ Civil/Structural Electrical ☐ Mechanical ☐ Authority ☒ Others

Type: ☐ Pre-Qualification ☒ Method Statement ☐ Material Submittal ☐ Sample ☐ Other

Document Description: Method of Statement for Traffic Signal System Installation and Commissioning

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-MST-ITS-02-RO5-00002	**Method of Statement for Traffic Signal System Installation and Commissioning**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz Signature: Date: 13- June-2026	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments: All the work shall be carried out in accordance with approved shop drawings, project specifications & relevant standards & codes

Refer to the supplementary file "Traffic_Signal_MS_HSE_Comments_Sheet-16-06-2026.xlsx"









Below portion for Client use only

Comments:

Signed by: Signature: Date:

QIDDIYA DEVELOPMENT COMPANY

DOCUMENT NUMBER	QDC-XXX-YYY-QHS-XXXX	REVISION NUMBER	01	ISSUED BY	PMO
DOCUMENT TITLE	MIR FORM	DOCUMENT TYPE	FORM	DATE ISSUED	MM-DD-2022

MATERIAL INSPECTION REQUEST (MIR) FORM

Contractor:	HAIF COMPANY
Project:	QPMO-410-CT-00618- ROAD ACCESS TO RESORT CORE
Contract No.:	QI09043311-WO-0004
Material Inspection Request Number:	QRXM114000-HFC-TEC-MIR-ITS-02-RO5-00018

HAIF-PRESTIGE(1) JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☐	Quality	☐	Project Controls	☐
Civil/Structural	☑	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

MATERIAL DESCRIPTION

Inspection / Test Location:	INTERIM ROAD MAIN LINE-02		
Material Name:	ITS SYSTEMS TRAFFIC SIGNALS POLES	Quantity:	04 No.
P.O Number		Delivery Note Number:	TTSDN-HAIF-290726-026
Approved Material Transmittal Number: (Quality document Approval)	QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00015	Approval Date:	
Inspection Date:	30-Jul-2026	Inspection Start Time:	10:00 AM
ITP:	QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00006	Checklist:	HFC-CKL-9001
Spec's / Dwg. Ref.:	TRAFFIC TECH SECURITY W.L.L	Approved Method Statement Number:	
Attachments:	Test Certificate: ◉ Yes ○ No IFC / Shop Drawings: ○ Yes ◉ No		

DESCRIPTION OF MATERIAL

6.42 Octagonal Traffic Signal Pole W Nos 1.0 Cantilever Arm 15.5 Mtrs & Base Plate Only (1 Nos.) 6.42M Octagonal Traffic Signal Pole W Nos 1.0 Cantilever Arm 16 Mtrs & Base Plate Only (1 Nos.) 6.42 M Octagonal Traffic Signal Pole W Nos 1.0 Cantilever Arm 12 Mtrs & Base Plate Only (1 Nos.) 6.42 Octagonal Traffic Signal Pole W Nos 1.0 Cantilever Arm 13 Mtrs & Base Plate Only (1 Nos.) for Interim Road Main Line-02

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Are Complete Details Mentioned in P.O and Delivery Note?	◉ YES ○ NO	REMARKS	
Complies with Approved ITPs/Checklists?	◉ YES ○ NO	REMARKS	
Signs of Physical Damage?	○ YES ◉ NO	REMARKS	
Conforms to Approved Material Submittal?	○ YES ○ NO	REMARKS	

Accepted:	◉
Accepted with Comments:	○
Rejected (See Remarks):	○

REMARKS:					
Name:	Moataz Elkhateeb	Signature:		Date:	30-07-2026

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Material requirements?	○ YES ○ NO	Materials Are Stored correctly?	○ YES ○ NO ○ NA

Accepted:	○
Accepted with Comments:	◉
Rejected (See Remarks):	○

REMARKS:	Inspection done for aforementioned material at the site stores open and found as per delivery note and material approval. Found approved subjected to provide quality test from TPI Company, the specification.				
Name:	Abdulrahman Hassan	Signature:		Date	30/7/2026

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

Client:	Consultant:	Contractor:
Qiddiya		Hail Company HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - **Interim Road Access to Resort Core**	**Project Code:** QRXM114000
Location: 00	**Date:** 21-September-2025
Document Title: **Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (Traffic Signal Controller)**	**Ref No:** QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00007 **Rev No:** 00

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☑ ITS ☐ Civil

Type: ☐ Pre-Qualification ☐ Method Statement ☒ Material Submittal ☐ Sample ☐ Other

Document Description: Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (Traffic Signal Controller)

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00007	**Material Approval Request FOR ITS SYSTEM SUPPLYING & INSTALLING BY TRAFFIC TECH SECURITY W.L.L (Traffic Signal Controller)**

Enclosure:

Submitted By:	**Received By:**
Name: **Eng. Moataz** Signature: Date:21-September-2025	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments:

Refer to letter No. QRXM114000-ZFP-COR-LTR-ADM-00036; the proposed Traffic Signal Controller based on Australian standard SCATS is rejected and shall be installed only on a temporary basis for the opening of the Resort Core. The permanent Traffic Signal Controller shall comply with NEMA standards and shall be submitted for approval, with no additional cost to the Client. The Contractor/Supplier is hereby instructed to strictly adhere to the referenced letter and ensure full compliance with the following comments for the permanent Traffic Signal Controller.

1.Provide technical comparison sheet against project specification.
2.Clarify the system type (isolated or interconnected) and specify the controller type (Type-1, Type-2, Type-3)
3.SASO/SABER certificate to be provided
4.Provide Rister Diagram of Traffic signal system
5.ITP to be submitted separately
6.SAT test procedure to be provided.
7.Provide reference that the subject material has Category C1 as mentioned in the submittal.

Below portion for Client use only

Comments:

Signed by: Signature: Date:

QIDDIYA DEVELOPMENT COMPANY					
DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00004	REVISION NUMBER:	00	ISSUED BY:	PMO
DOCUMENT TITLE	WIR FORM	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022

WORK INSPECTION REQUEST (WIR) FORM

Contractor:	HAIF-FREYSSINET JV
Project:	RA2RC
Contract No.:	QPMO-410-CT-00618
Work Inspection Request Number:	QRXM114000-HFC-TEC-WIR-ITS-02-RO5-00092

HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☑	Quality	☐	Project Controls	☐
Civil / Structural	☑	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

WORK DESCRIPTION

Inspection / Test Location:	INTERIM ROAD Sta. (Concrete of ITS TRAFFIC SIGNAL POLE Foundation) Main Line -02		
GIS/GPS GeoTag Coordinates (If applicable)			
Inspection Date:	13-Aug-2026	Inspection Start Time:	3:30 pm
ITP:	QRXM114000-HFC-TEC-ITP-CIV-02-RO5-00002	Checklist:	HFC-CKL-405
Spec's / Dwg. Ref.:	QRXM114000-HFC-DRW-SDW-CIV-02-RO5-00033-88	Approved Method Statement Number:	QRXM114000-HFC-TEC-MST-CIV-02-RO5-00008
Attachments:	☑ Drawings ☑ Data Sheets ☐ TQs/RFI ☐ OTHER		

DESCRITPTION OF WORK

Inspection request, for Pouring of Foundation concrete for ITS TRAFFIC SIGNAL POLE 6m with CANTILEVER ARM 15.5m, at Junction-03, AS SHOWN ON ATTACHED DRAWING,at Access to Resort core interim Road.As per attached drawing.

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Complies with Approved ITPs/Checklists?	◉ YES ○ NO ○ NA	REMARKS	
All Strucutral Embedded Items Cleared?	○ YES ○ NO ○ NA	WIR Number	
Embedded Electrical Items Cleared by Electrical QC?	○ YES ○ NO ○ NA	WIR Number	
Embedded Mechanical Items Cleared by Mechanical QC?	○ YES ○ NO ○ NA	WIR Number	

Accepted:	◉
Accepted with Comments (See Remarks):	○
Rejected (See Remarks):	○

REMARKS:					
Name:	Naseem Ahmed	Signature:	(N)	Date:	13/8/26

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Project spec requirements?	○ YES ○ NO	Okay to Proceed with next activity?	○ YES ○ NO ○ NA

Accepted:	○
Accepted with Comments (See Remarks):	◉
Rejected (See Remarks):	○

REMARKS:	Provide 28 day Concrete test report.				
Name:	Abdelmonem Sayfan	Signature:		Date	18-08-26

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Haif Company / Freyssinet — HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
Location: 00	**Date:** 4 -June-2026
Document Title: **Inspection & Test Plan for Inteligent Transportation System Works for TRAFFIC SIGNAL SYSTEM**	**Ref No:** QRXM114000-HFC-TEC-ITP-ITS-00006
	Rev No: 00

Department: ☐ Architectural ☐ Structural ☒ Electrical ☐ Mechanical ☐ Authority ☐ Civil

Type: ☐ Pre-Qualification ☐ Method Statement ☐ Material Submittal ☐ Sample ☒ ITP

Document Description: This is Inspection&Test Plan for Inspection&Test Plan for Inteligent Transportation system Works for TRAFFIC SIGNAL SYSTEM

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-ITP-ITS-00006	**Inspection&Test Plan for Inteligent Transportation system Works for TRAFFIC SIGNAL SYSTEM**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz Signature: Date: 4 -June-2026	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments: All the work shall be carried out inaccordance with project specification, relevant standards & codes and manufacturer recommendations.

A: Approved
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

A: Approved
Saud Nawab
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

A: Approved
Zuhair Fayez Partnership Consultants
Riyadh , Saudi Arabia

Below portion for Client use only

Comments:

Signed by: Signature: Date:

HAIF-FSA JV Inspection & Test Plan					I &TP		APPROVED DATE	DISCIPLINE ITS
Inteligent Transportation System Works for TRAFFIC SIGNAL SYSTEM					**HFC-ITP-090**			
PROJECT TITLE:WBS Access Road To Resort Core (RA2RC)					CONTRACTOR/SUBCONTRACTOR			
WIR No.					CONSTRUCTION- Intelligent Transportation System Works for TRAFFIC SIGNAL SYSTEM		HAIF	

ITEM NO.	PROJECT PHASE	TASK / ACTIVITY	Quality Requirements /references/ specifications	Quality Record	INSPECTION RESPONSIBILITY ASSIGNMENTS			REMARKS
					Contractor	Third Party	Consultant	
1.0 DOCUMENT REVIEW								
1.7		Material Approval & Shop Drawing - Vehicle Video Detection System	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0B Section 137714 VEHICLE DETECTION SYSTEM IFC Drawing QRXP117115-DAH-VORA2R-DWG-GEN-R3-Z00000-5000006	QRXM114000-HFC-TEC-MAT-ITS-02-R05-00010 Material Approval Request for VEHICLE VIDEO DETECTION SYSTEM Approved SHOP DRAWINGS: QRXM114000-HFC-DRW-SDW-ITS-02-R05-00019-R02 QRXM114000-HFC-DRW-SDW-ITS-02-R05-00031-R01 QRXM114000-HFC-DRW-SDW-ITS-02-R05-00044-R01	R		H	
2.0 MATERIAL RECEIVING INSPECTION								
2		Material receiving inspection, protection & storage	QD0002-ADM-TEM-QMS00007[0A] MaterialReceiving Inspection in site HFC-CKL-9001	QD0002-ADM-TEM-QMS00007[0A] MaterialReceivingInspection in site HFC-CKL-9001	H		H	MIR to be submitted
3.0 WORK INSTALLATION								
3.1		PRE - INSTALLATION	HFC-CKL-9002	HFC-CKL-9002	H		H	
3.2		INSTALLATION	HFC-CKL-9003	HFC-CKL-9003	H		H	
3.3		TESTING	HFC-CKL-9004	HFC-CKL-9004	H		H	

	GENERAL NOTES
1	Surveillance: QA/QC organization to monitor work in progress without notice from Construction Organization
2	Witness: QA/QC organization shall be notified of the timing of Inspection or test in advance. However, the inspection or test shall be performed as scheduled if the QA/QC organization representative is not present
3	Hold: QA/QC organization shall be notified of the timing of inspection or test in advance. Inspection or test shall not be carried out without the QA/QC organization representative in attendance.
4	If the Main Contractor delegates the assigned responsibility to the Subcontractor, then the Main Contractor will have the same degree of responsibility as assigned to Consultant.

LEGEND			
H	Hold Point for QC Inspection/ Test	R	Review of Documents
W	Witness Inspection/T	RH	Review & approval of Documents
S	Surveillance		

HFC-ITP-090		

Checklist : HFC-CKL-9003

INSTALLATION OF TRAFFIC SIGNAL SYSTEM	Checklist	APPROVED DATE	**DISCIPLINE**
PROJECT TITLE: Road Access To Resort Core (RA2RC)	**HFC-CKL-9003**		**ITS**
WIR No.	WBS	CONTRACTOR/SUBCONTRACTOR	
	CONSTRUCTION- Intelligent Transportation System Works for INSTALLATION AND OPERATION of TRAFFIC SIGNAL SYSTEM	HAIF	


ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
1.0	**INSTALLATION OF TRAFFIC SIGNAL SYSTEM - EMERGENCY VEHICLE PRE-EMPTION SYSTEM (EVPS)**					
ITEM NO.	**Check Points & Acceptance Criteria**	**Reference**	**Pass**	**Fail**	**Not Applicable**	**Re-Inspection**
2.0	**INSTALLATION OF TRAFFIC SIGNAL SYSTEM - TRAFFIC SIGNAL HEADS**					
2.1	Are all Shop Drawings, Method Statement and Material Submittals were approved ?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
2.2	Are all TRAFFIC SIGNAL HEADS (LED) and components installed as per approved Material Submittals?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
2.3	Are all TRAFFIC SIGNAL HEADS (LED) material quantity as per approved Material Submittals and Shop Drawings?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
2.4	Are all TRAFFIC SIGNAL HEADS (LED) installed on poles firmly secured, fixed and tightened?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
2.5	Is installation performed in accordance with the applicable standards, requirements, manufacturers' guidelines and any authorities having jurisdiction	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
2.6	Are all TRAFFIC SIGNAL HEADS (LED) components labeled and marked?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
2.7	Are all TRAFFIC SIGNAL HEADS (LED) fittings and accessories,have been installed as per requirements for proper,safe, and reliable operation of the system?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
2.8	Ensure safe ingress and egress from all work areas are maintained during movement and installation of equipment/materials	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
2.9	Is the facing and orientation of LED Signals properly done as per Approved shop drawings	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
2.10	Adjustment shall permit 360° rotation about a vertical axis, all vehicle signal faces shall contain 3 sections arranged vertically: red-top, yellow-center, green-bottome.	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
2.11	Are the signal cables properly and safely conntect through the cable entry?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
2.12	Did the Technical Manual received for installed materials?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			


Remarks

PM/Contractor			QDC		
Contractor Construction			**Third Party (if applicable)**		
The work is ready for inspection			**Document Reviewed**	**Work Inspected**	**Test Records Verified**
Name	Signature	Date	Name	Signature	
Naseem		19/6/26	Mehmet		
Contractor QC Inspector			QDC Supervision Consultant		


Form Ref. No. QD0002-ADM-TEM-QTY-00003– Rev.0A

A-Approved
For comments refer to the drawing # QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00033

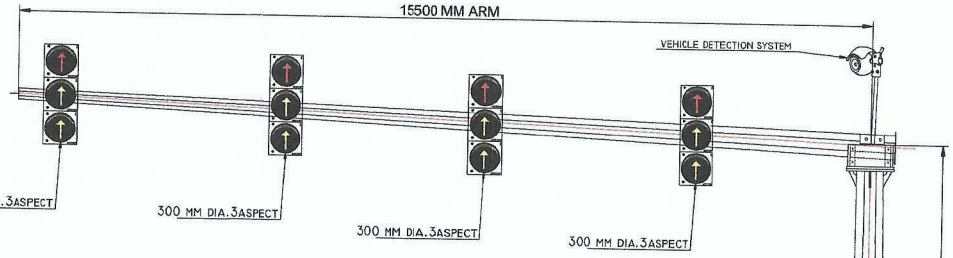

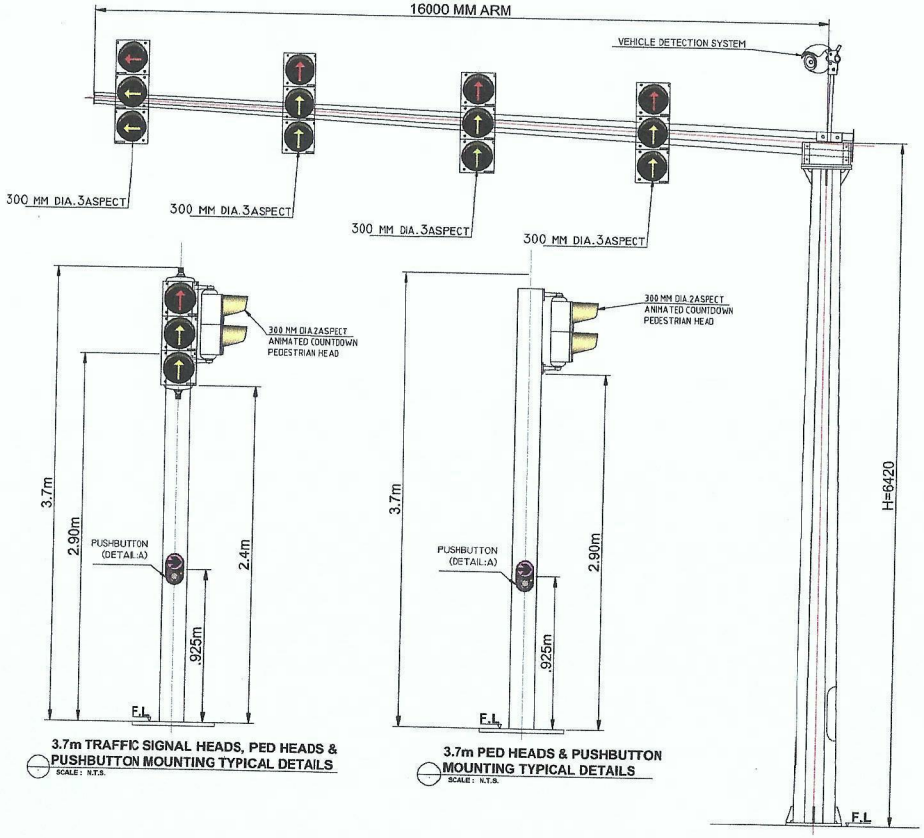


TYPICAL SIGNAL GANTRY (CANTILEVER) DETAIL GANTRY NO - 09




TYPICAL VEHICULAR / PEDESTRIAN SIGNAL HEAD DETAILS
SCALE : N.T.S.

3.7m TRAFFIC SIGNAL HEADS, PED HEADS & PUSHBUTTON MOUNTING TYPICAL DETAILS
SCALE : N.T.S.

3.7m PED HEADS & PUSHBUTTON MOUNTING TYPICAL DETAILS
SCALE : N.T.S.



DETAIL-A: PUSH BUTTON
SCALE : N.T.S.



TYPICAL SIGNAL GANTRY (CANTILEVER) DETAIL GANTRY NO - 20

All general comments notes or drawing and previous Rev. shall be maintained
A-Approved
Zuhair Fayez Partnership Consultants
Riyadh - Saudi Arabia

القديـــة
Qiddiya

Consultant's information
HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com
Zuhair Fayez Partnership



Notes:
1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3. THISDRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.

REFERENCE I.F.C DESIGN DRAWING NO:
1. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000003
2. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000001
3. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5900002
4. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5300005
5. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000006
6. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000001
7. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000002
8. QRXP117115-DAH-VORA2R-DWG-ICT-R3-Z00000-2000000

LEGEND:

Rev. No.	Date	Description	Appr.
00	31-8-2025	FOR REVIEW AND APPROVAL	C
01	08-11-2025	FOR REVIEW AND APPROVAL	C
02	28-12-2025	FOR REVIEW AND APPROVAL	C
03	04-02-2026	FINAL REVISION	C
--	--	--	--
--	--	--	--
--	--	--	--

Consultant
Contractor
Hail Company
ITS Contractor
TRAFFIC TECH
Project:
القديـــة Qiddiya

Job title: Road Access To Resort Core


Drawing title:
SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-3
TYPICAL DETAILS-1

Sheet number:
SHEET 5 / 20

Scale:NTS

Drawn: M.Elsayed | Checked:M.Abuzaid
Designed: | Approved:

Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00037
Revision 03

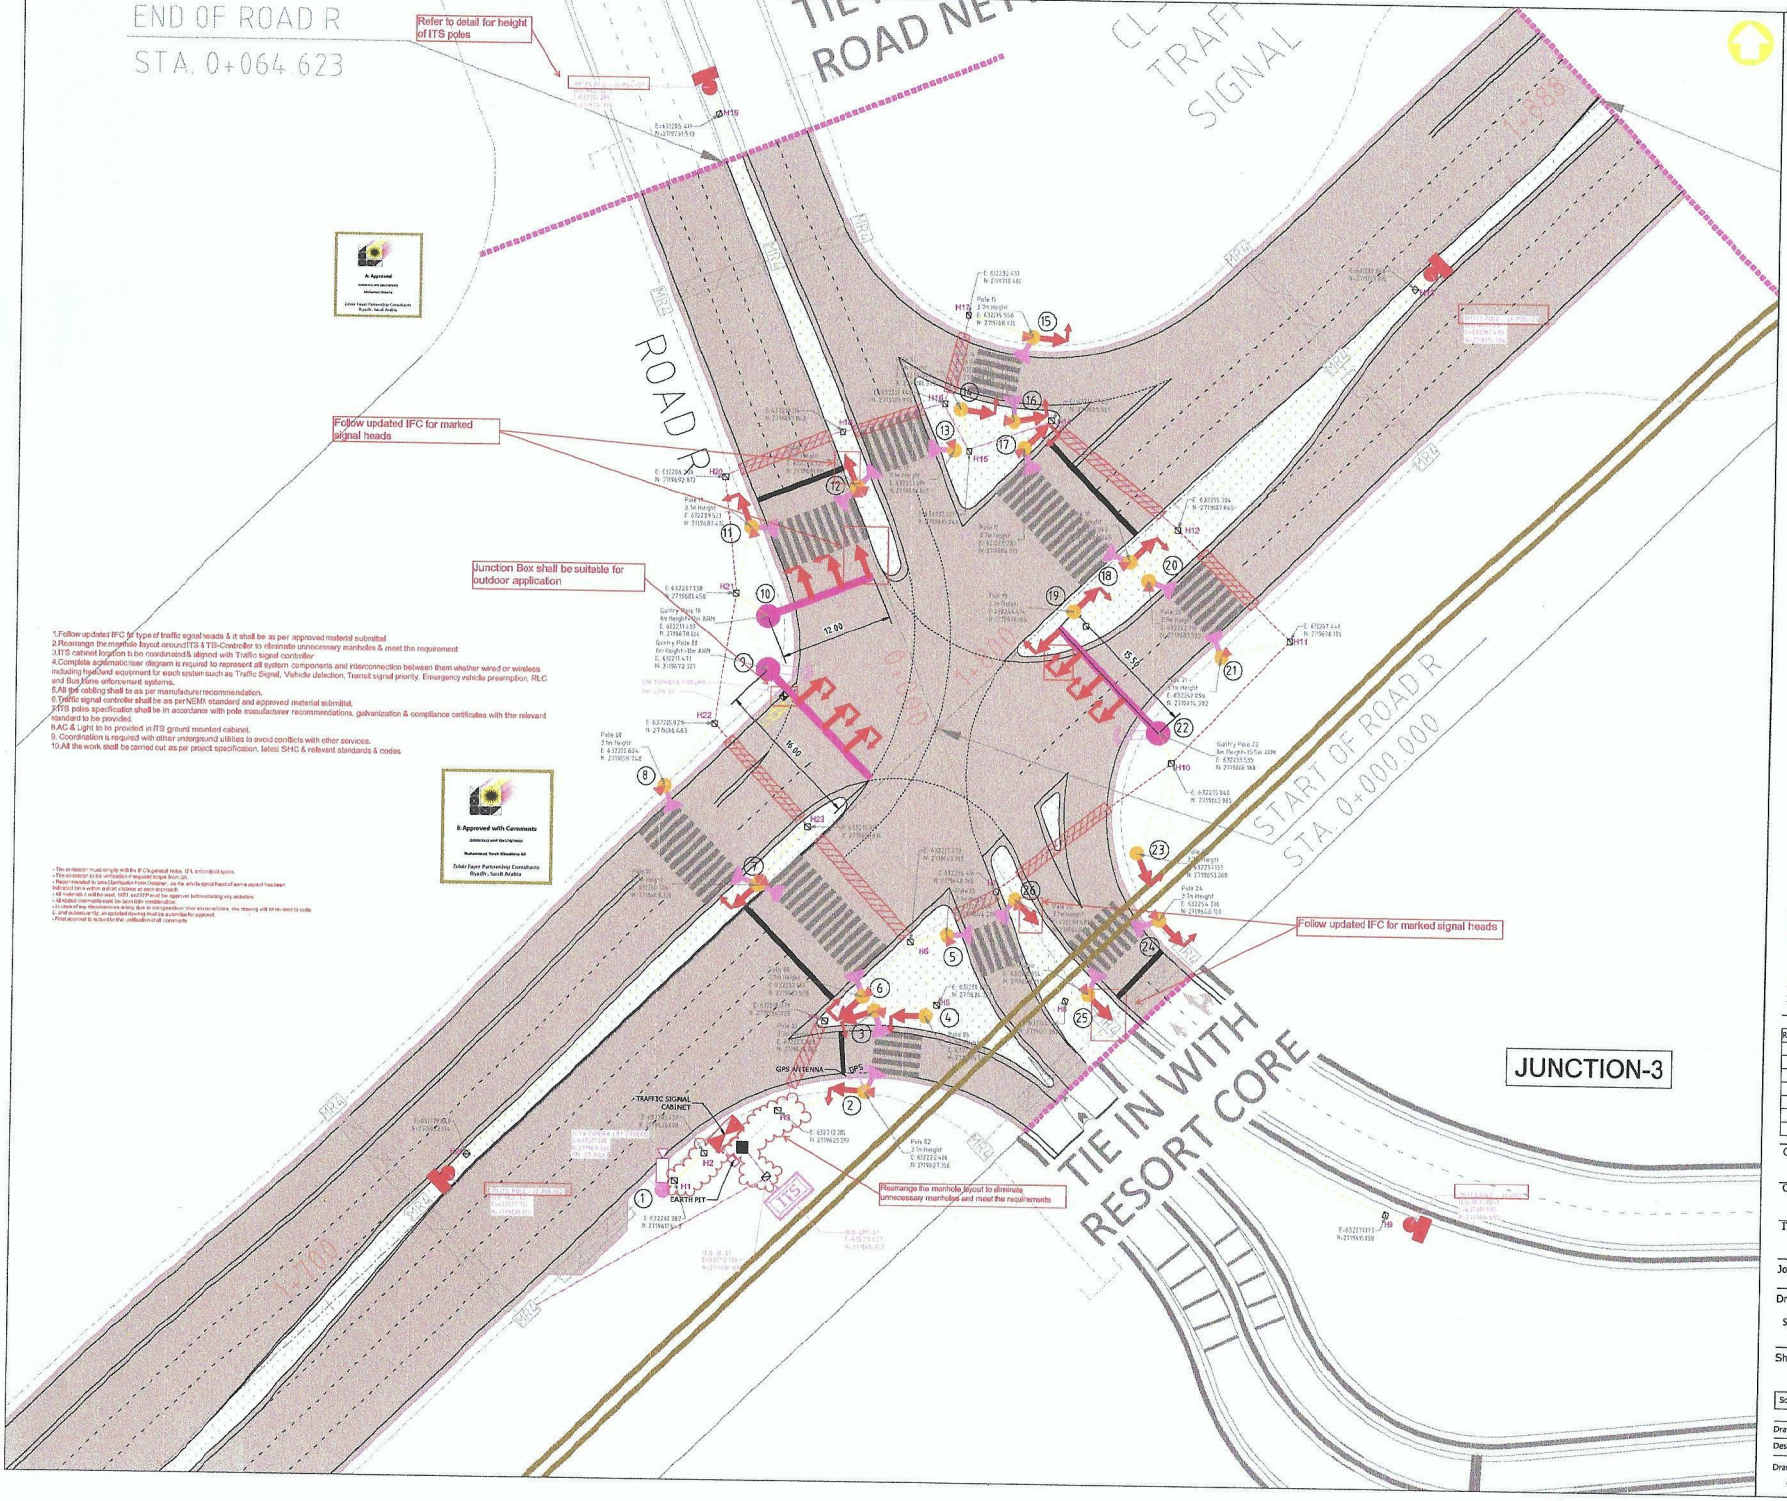


القديـــة
Qiddiya

Consultant's information

HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com

Zuhair Fayez Partnership



Notes:
1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3. THIS DRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS.

REFERENCE I.F.C DESIGN DRAWING NO:
1. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-2000003
2. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-5000001
3. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-5000002
4. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-5000005
5. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-5000006
6. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-6000001
7. QRXP117115-DAH-VORA2R-DWG-ITS-R3-200000-6000002
8. QRXP117115-DAH-VORA2R-DWG-ICT-R3-200000-2000000

LEGEND:

Rev. No.	Date	Description	Appr.
00	31-8-2025	FOR REVIEW AND APPROVAL	c
01	08-11-2025	FOR REVIEW AND APPROVAL	--
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--

Consultant
Contractor
Hail Company
ITS Contractor
TRAFFIC TECH
Project:
القديـــة Qiddiya

Job title: Road Access To Resort Core

Drawing title: SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-3

Sheet number: SHEET 1 / 20

Scale: 1:1000 @ A0

Drawn: M.Sayed | Checked: M.Sayed
Designed: | Approved:

Drawing number: QRXH114000-HFC-DRW-SDW-ITS-02-RO5-00033 | Revision 01

PO	N	E	Z	Description
25	632253.657	2719664.284	662.495	Cantilever 15.5m
26	632251.879	2719665.997	662.515	Cantilever 15.5m
27	632253.585	2719667.801	662.527	Cantilever 15.5m
28	632255.37	2719666.09	662.507	Cantilever 15.5m
29	632254.413	2719666.152	662.592	Cantilever 15.5m
30	632253.727	2719666.852	662.605	Cantilever 15.5m
31	632252.979	2719666.067	662.606	Cantilever 15.5m
32	632253.674	2719665.374	662.58	Cantilever 15.5m

PO	N	E	Z	Description
25	632253.657	2719664.284	662.495	Cantilever 15.5m
26	632251.879	2719665.997	662.515	Cantilever 15.5m
27	632253.585	2719667.801	662.527	Cantilever 15.5m
28	632255.37	2719666.09	662.507	Cantilever 15.5m
29	632254.413	2719666.152	662.592	Cantilever 15.5m
30	632253.727	2719666.852	662.605	Cantilever 15.5m
31	632252.979	2719666.067	662.606	Cantilever 15.5m
32	632253.674	2719665.374	662.58	Cantilever 15.5m
