Inspection on site.

QIDDIYA DEVELOPMENT COMPANY					
DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00004	REVISION NUMBER:	00	ISSUED BY:	PMO
DOCUMENT TITLE	WIR FORM	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022

WORK INSPECTION REQUEST (WIR) FORM

Contractor:	HAIF-FREYSSINET JV
Project:	RA2RC
Contract No.:	QPMO-410-CT-00618
Work Inspection Request Number:	QRXM114000-HFC-TEC-WIR-ITS-02-RO5-00100

HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☑	Quality	☐	Project Controls	☐
Civil / Structural	☐	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

WORK DESCRIPTION

Inspection / Test Location:	INTERIM ROAD Sta. (Opticom Radio Preemption)		
GIS/GPS GeoTag Coordinates (If applicable)			
Inspection Date:	17-Oct-2026	Inspection Start Time:	9:30 am
ITP:	QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00006	Checklist:	HFC-CKL-9003
Spec's / Dwg. Ref.:	QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00052	Approved Method Statement Number:	QRXM114000-HFC-TEC-MST-ITS-02-RO5-00001
Attachments:	☑ Drawings ☐ Data Sheets ☐ TQs/RFI ☐ OTHER		

DESCRITPTION OF WORK

Inspection request for Installation of Opticom Radio Preemption Vehicle kit (02 Nos) Opticom Model 764 Multimode Phase (2 No) & Infrared Detector (08Nos) & Opticom Model 3052 Card rack & Opticom Infrared 794 LED Emitter (02Nos) & Opticom Model Auxiliary Interface (02Nos) & Radio antenna (02Nos) at (Junction-1,2,3),
at Access to Resort core interim Road. As per attached drawing.

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Complies with Approved ITPs/Checklists?	◉ YES ○ NO ○ NA	REMARKS	
All Strucutral Embedded Items Cleared?	○ YES ○ NO ○ NA	WIR Number	
Embedded Electrical items Cleared by Electrical QC?	○ YES ○ NO ○ NA	WIR Number	
Embedded Mechanical Items Cleared by Mechanical QC?	○ YES ○ NO ○ NA	WIR Number	

Accepted:	◉
Accepted with Comments (See Remarks):	○
Rejected (See Remarks):	○

REMARKS:					
Name:	Naseem Ahmed	Signature:	Naseem	Date:	17/10/26

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Project spec requirements?	○ YES ○ NO	Okay to Proceed with next activity?	○ YES ○ NO ○ NA

Accepted:	○
Accepted with Comments (See Remarks):	◉
Rejected (See Remarks):	○

REMARKS:	final approval upon T&C				
Name:	Mahmoud	Signature:		Date	5/11/26

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Hail Company / Freyssinet — HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
Location: 00	**Date:** 4 -June-2026
Document Title: **Inspection & Test Plan for Inteligent Transportation System Works for TRAFFIC SIGNAL SYSTEM**	**Ref No:** QRXM114000-HFC-TEC-ITP-ITS-00006
	Rev No: 00

Department: ☐ Architectural ☐ Structural ☒ Electrical ☐ Mechanical ☐ Authority ☐ Civil

Type: ☐ Pre-Qualification ☐ Method Statement ☐ Material Submittal ☐ Sample ☒ ITP

Document Description: This is Inspection&Test Plan for Inspection&Test Plan for Inteligent Transportation system Works for TRAFFIC SIGNAL SYSTEM

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-ITP-ITS-00005	**Inspection&Test Plan for Inteligent Transportation system Works for TRAFFIC SIGNAL SYSTEM**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz Signature: Date: 4 -June-2026	Name: Signature: Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments:







Below portion for Client use only

Comments:

Signed by: Signature: Date:

HAIF-FSA JV Inspection & Test Plan			
Inteligent Transportation System Works for TRAFFIC SIGNAL SYSTEM	I &TP **HFC-ITP-090**	APPROVED DATE	**DISCIPLINE** **ITS**
PROJECT TITLE:WBS	CONTRACTOR/SUBCONTRACTOR		
WIR No.	CONSTRUCTION- Intelligent Transportation System Works for TRAFFIC SIGNAL SYSTEM HAIF		

ITEM NO.	PROJECT PHASE	TASK / ACTIVITY	Quality Requirements /references/ specifications	Quality Record	INSPECTION RESPONSIBILITY ASSIGNMENTS			REMARKS
					Contractor	Third Party	Consultant	
1.0 DOCUMENT REVIEW								
1.7		Material Approval & Shop Drawing - Vehicle Video Detection System	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0B Section 137714 VEHICLE DETECTION SYSTEM IFC Drawing QRXP117115-DAH-VORA2R-DWG-GEN-R3-Z00000-5000006	QRXM114000-HFC-TEC-MAT-ITS-02-R05-00010 Material Approval Request for VEHICLE VIDEO DETECTION SYSTEM Approved SHOP DRAWINGS: QRXM114000-HFC-DRW-SDW-ITS-02-R05-00019-R02 QRXM114000-HFC-DRW-SDW-ITS-02-R05-00031-R01 QRXM114000-HFC-DRW-SDW-ITS-02-R05-00044-R01	R		H	
2.0 MATERIAL RECEIVING INSPECTION								
2		Material receiving inspection, protection & storage	QD0002-ADM-TEM-QMS00007[0A] MaterialReceiving Inspection in site HFC-CKL-9001	QD0002-ADM-TEM-QMS00007[0A] MaterialReceivingInspection in site HFC-CKL-9001	H		H	MIR to be submitted
3.0 WORK INSTALLATION								
3.1		PRE - INSTALLATION	HFC-CKL-9002	HFC-CKL-9002	H		H	
3.2		INSTALLATION	HFC-CKL-9003	HFC-CKL-9003	H		H	
3.3		TESTING	HFC-CKL-9004	HFC-CKL-9004	H		H	

GENERAL NOTES

1	Surveillance: QA/QC organization to monitor work in progress without notice from Construction Organization
2	Witness: QA/QC organization shall be notified of the timing of Inspection or test in advance. However, the inspection or test shall be performed as scheduled if the QA/QC organization representative is not present
3	Hold: QA/QC organization shall be notified of the timing of inspection or test in advance. Inspection or test shall not be carried out without the QA/QC organization representative in attendance.
4	If the Main Contractor delegates the assigned responsibility to the Subcontractor, then the Main Contractor will have the same degree of responsibility as assigned to Consultant.

LEGEND

H	Hold Point for QC Inspection/ Test	R	Review of Documents
W	Witness Inspection/T	RH	Review & approval of Documents
S	Surveillance		

Checklist : HFC-CKL-9003

INSTALLATION OF TRAFFIC SIGNAL SYSTEM

PROJECT TITLE: Road Access To Resort Core (RA2RC)

WIR No.

Checklist	APPROVED DATE	DISCIPLINE
HFC-CKL-9003		ITS
WBS	CONTRACTOR/SUBCONTRACTOR	

CONSTRUCTION-
Intelligent Transportation System Works for INSTALLATION AND OPERATION of TRAFFIC SIGNAL SYSTEM

HAIF

ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
1.0	**INSTALLATION OF TRAFFIC SIGNAL SYSTEM - EMERGENCY VEHICLE PRE-EMPTION SYSTEM (EVPS)**					
1.1	Are all Shop Drawings, Method Statement and Material Submittals were approved ?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
1.2	Are all EVPS equipment firmly secured?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.3	Is installation performed in accordance with the applicable standards, requirements, manufacturers' guidelines and any authorities having jurisdiction	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.4	Are all EVPS components labeled and marked?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION				
1.5	Are all EVPS fittings and accessories,have been installed as per requirements for proper,safe, and reliable operation of the system?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.6	Ensure safe ingress and egress from all work areas are maintained during movement and installation of equipment/materials	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.7	Are the EVPS structural details installed as per approved Shop drawings?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.8	Are the EVPS cameras installed on the support structure as per manufacturer's instructions?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.9	Are conductors, control and signal cables installed as per manufacturer's instructon?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.10	Are patch cords, cables have been properly labeled as per specifications and approved shop drawings?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.11	Are the connections completed on numbered terminal strips in junction, pull, and outlet boxes; terminal cabinets, and equipment enclosures?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			

Remarks

PM/Contractor			QDC		
Contractor Construction			**Third Party (if applicable)**		
The work is ready for inspection			**Document Reviewed**	**Work Inspected**	**Test Records Verified**
Name	Signature	Date	Name	Signature	
Mukhavis		17/4/26			
Contractor QC Inspector			QDC Supervision Consultant		

Form Ref. No. QD0002-ADM-FEM-QTY-00003– Rev.0A

Checklist : HFC-CKL-9003

INSTALLATION OF TRAFFIC SIGNAL SYSTEM

PROJECT TITLE: Road Access To Resort Core (RA2RC)

WIR No

Checklist	APPROVED DATE	DISCIPLINE
HFC-CKL-9003		ITS
WBS	CONTRACTOR/SUBCONTRACTOR	

CONSTRUCTION-
Intelligent Transportation System Works for INSTALLATION AND OPERATION of TRAFFIC SIGNAL SYSTEM

HAIF

ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
1.0	**INSTALLATION OF TRAFFIC SIGNAL SYSTEM - EMERGENCY VEHICLE PRE-EMPTION SYSTEM (EVPS)**					
1.1	Are all Shop Drawings, Method Statement and Material Submittals were approved ?	SHC 306 SECTION 12 TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
1.2	Are all EVPS equipment firmly secured?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.3	Is installation performed in accordance with the applicable standards, requirements, manufacturers' guidelines and any authorities having jurisdiction	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.4	Are all EVPS components labeled and marked?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.5	Are all EVPS fittings and accessories,have been installed as per requirements for proper,safe, and reliable operation of the system?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.6	Ensure safe ingress and egress from all work areas are maintained during movement and installation of equipment/materials	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.7	Are the EVPS structural details installed as per approved Shop drawings?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.8	Are the EVPS cameras installed on the support structure as per manufacturer's instructions?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.9	Are conductors, control and signal cables installed as per manufacturer's instruction?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.10	Are patch cords, cables have been properly labeled as per specifications and approved shop drawings?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.11	Are the connections completed on numbered terminal strips in junction, pull, and outlet boxes; terminal cabinets; and equipment enclosures?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			

Remarks

PM/Contractor			QDC		
Contractor Construction			**Third Party (if applicable)**		
The work is ready for inspection			**Document Reviewed**	**Work Inspected**	**Test Records Verified**
Name	Signature	Date	Name	Signature	
Muhamad		17/10/26			
Contractor QC Inspector			QDC Supervision Consultant		

Form Ref. No. QD0002-ADM-TEM-QTY-00003– Rev.0A

Checklist : HFC-CKL-9003

INSTALLATION OF TRAFFIC SIGNAL SYSTEM

PROJECT TITLE: Road Access To Resort Core (RA2RC)

WIR No.:

Checklist	APPROVED DATE	DISCIPLINE
HFC-CKL-9003		ITS
WBS	CONTRACTOR/SUBCONTRACTOR	

CONSTRUCTION-
Intelligent Transportation System Works for INSTALLATION AND OPERATION of TRAFFIC SIGNAL SYSTEM

HAIF


ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
1.0	**INSTALLATION OF TRAFFIC SIGNAL SYSTEM - EMERGENCY VEHICLE PRE-EMPTION SYSTEM (EVPS)**					
1.1	Are all Shop Drawings, Method Statement and Material Submittals were approved ?	SHC 306 SECTION 12.TRAFFIC SIGNALS, 12.2 SPEFICIFICATIONS	✓			
1.2	Are all EVPS equipment firmly secured?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.3	Is installation performed in accordance with the applicable standards, requirements, manufacturers' guidelines and any authorities having jurisdiction	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.4	Are all EVPS components labeled and marked?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION				
1.5	Are all EVPS fittings and accessories,have been installed as per requirements for proper,safe, and reliable operation of the system?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.6	Ensure safe ingress and egress from all work areas are maintained during movement and installation of equipment/materials	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.7	Are the EVPS structural details installed as per approved Shop drawings?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.8	Are the EVPS cameras installed on the support structure as per manufacturer's instructions?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.9	Are conductors, control and signal cables installed as per manufacturer's instruction?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.10	Are patch cords, cables have been properly labeled as per specifications and approved shop drawings?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			
1.11	Are the connections completed on numbered terminal strips in junction, pull, and outlet boxes; terminal cabinets; and equipment enclosures?	QRXP117115-DAH-VORA2R-SPE-INF-R1-Z00000-000001-0H SECTION 137780 EMERGENCY VEHICLE PREEMPTION (EVP) SYETEM PART 3 EXECUTION 3.1 INSTALLATION	✓			

Remarks

PM/Contractor			QDC		
Contractor Construction			Third Party (if applicable)		
The work is ready for Inspection			Document Reviewed	Work Inspected	Test Records Verified
Name	Signature	Date	Name	Signature	
Muhammad		17/10/26			
Contractor QC Inspector			QDC Supervision Consultant		

Form Ref. No. QD0002-ADMTEM-QTY-00003– Rev.0A

CENTER MANAGEMENT SOFWARE (CMS)
to Update System Configuration, Collect Data and Generate Reports



NOTE:
1. Opticom GPS vehicle equipment transmits vehicle speep, direction and turn signal status to GPS intersection equipment.


2. as vehicle enters radio rage, Opticom GPS intersection equipment relays the request to the Opticom GPS phase selector

3. Opticom GPS phase selector validates request from GPS receiver, and alerts the traffic control system which requests a green traffic signal



Opticom 764 Multimode Phase Selector

PHASE SELECTOR



Wireless Connection

Fiber Optic Connection

Power Cable


Wireless Connection

Radio / GPS Cable Installation


5 Pair Radio/GPS Cable		
Pin	Wire Color	Function
1	Yellow	Radio transmit (+)
2	Yellow Black	Radio transmit (-)
3	Blue	Radio receive (+)
4	Blue White	Radio receive (-)
5	Orange	Radio clock (+)
6	Orange Green	Radio clock (-)
7	Brown	GPS power
8	Brown White	Common
9	Violet	Radio power
10	Violet White	Common
11	Bare	Shield drain wire

5 - Pin Harness Wire		
Pin	Wire Color	Function
1	Gray White	Output A
2	Blue White	Output B
3	Violet White	Output C
4	Brown White	Output D
5	Gray Black	Logic Common

SATELITE



Wireless Connection



Opticom 3100
GPS Radio Unit

Wireless Connection


CLOUD NETWORK INFORMATION PROCESSOR




Wireless Connection

Wireless Connection

OPTICOM RADIO CONTROL UNIT (LOW PRIORITY) MODEL 2101 / OPTICOM INFRARED 794L LED EMITTER LOW PRIORITY



TRANSIT VEHICLE

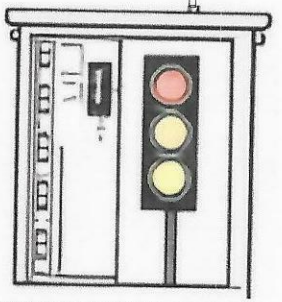

TRAFFIC SIGNAL CABINET

MATERIAL SUBMITTAL REF NO :
QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00016



TRANSIT SIGNAL PRIORTY (TSP) / EMERGENCY VEHICLE PREEMPTION SYSTEM (EVP) - SCHEMATIC / RISER DIAGRAM

القديـــة
Qiddiya

Consultant's information
HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel.: +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email.: zfpr@zfp.com

Zuhair Fayez Partnership



Notes:
1 ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED.
2 ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE.
3 THIS DRAWINGS IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL STRUCTURAL AND SERVICES DRAWINGS.

REFERENCE I.F.C DESIGN DRAWING NO:
1 QRXP117115-DAH-VORA28-DWG-ITS-R3-Z00000-2000001
2 QRXP117115-DAH-VORA28-DWG-ITS-R3-Z00000-5000001
3 QRXP117115-DAH-VORA28-DWG-ITS-R3-Z00000-5000005
4 QRXP117115-DAH-VORA28-DWG-ITS-R3-Z00000-5000006
5 QRXP117115-DAH-VORA28-DWG-ITS-R3-Z00000-6000001
6 QRXP117115-DAH-VORA28-DWG-ICT-R3-Z00000-2000000

LEGEND:

Rev. No.	Date	Description	Appr.
00	06-10-2025	FOR REVIEW AND APPROVAL	B
01	04-11-2025	FOR REVIEW AND APPROVAL	C
02	28-12-2025	FOR REVIEW AND APPROVAL	C
03	04-02-2026	FINAL REVISION	--
--	--	--	--
--	--	--	--
--	--	--	--

Consultant
Contractor
ITS Contractor
Project:

Job title: Road Access To Resort Core

Drawing title:
SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-1
TYPICAL RISER DIAGRAM FOR EMERGENCY VEHICLE PREEMPTION SYSTEM

Sheet number:
SHEET 14 / 18


Scale: NTS

Drawn: M.Elsayed | Checked: M.Abuzaid
Designed: | Approved:

Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00052
Revision: 03

Opticom Radio Preemption Accessories

Vehicle Kit

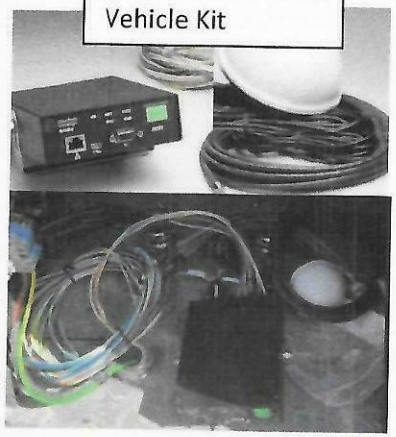




Infrared Detector Camera

Card Rack- Multi Mode
Phase Selector



LED Emitter

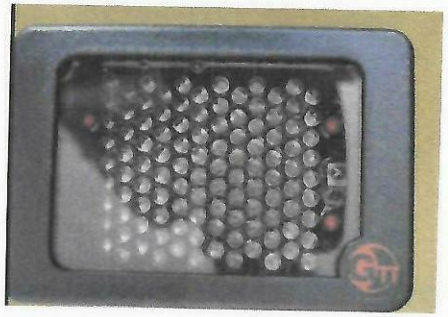

TSP- Auxiliary



RADIO ANTENNA

