QIDDIYA DEVELOPMENT COMPANY					
DOCUMENT NUMBER:	QDC-ADM-TEM-QMS-00004	REVISION NUMBER:	OD	ISSUED BY:	PMO
DOCUMENT TITLE	WIR FORM	DOCUMENT TYPE:	FORM	DATE ISSUED:	MAY-08-2022

WORK INSPECTION REQUEST (WIR) FORM

Contractor:	HAIF-FREYSSINET JV
Project:	RA2RC & JUCTTION
Contract No.:	QPMO-410-CT-00618
Work Inspection Request Number:	QRXM114000-HFC-TEC-WIR-ITS-02-RO5-00113

HAIF-FREYSSINET JV

Discipline

Architecture	☐	Mechanical	☐	Information Technology	☑	Quality	☐	Project Controls	☐
Civil / Structural	☐	Electrical	☐	Landscape	☐	Safety	☐	Construction Management	☐
Other	☐								

WORK DESCRIPTION

Inspection / Test Location:	Interim Road (Traffic Surveillance (CCTV) System), Main Line-02		
GIS/GPS GeoTag Coordinates (If applicable)			
Inspection Date:	17-Oct-2026	Inspection Start Time:	11:30 am
ITP:	QRXM114000-HFC-TEC-ITP-ITS-02-RO5-00007	Checklist:	HFC-CKL-1003
Spec's / Dwg. Ref.:	QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00053 -63-73	Approved Method Statement Number:	QRXM114000-HFC-TEC-MST-ITS-02-RO5-00001
Attachments:	☑ Drawings ☐ Data Sheets ☐ TQs/RFI ☐ OTHER		

DESCRIPTION OF WORK

Inspection request for installation of The (Traffic Surveillance (CCTV) System) include furnishing and installing cameras, ITS Cabinet and assemblies, all cabling necessary for communications and power, connectors, all mounting brackets, all mounting accessories, Camera Lowering Device System, system software and hardware, configuration and setups, certifications and other required documentation, and testing.,at Upgrade and Junction area at Interim Road Main Line -02

CONTRACTOR - QUALITY INSPECTOR - INITIAL INSPECTION FINDINGS:

Complies with Approved ITPs/Checklists?	◉ YES ○ NO ○ NA	REMARKS	
All Strucutral Embedded Items Cleared?	◉ YES ○ NO ○ NA	WIR Number	
Embedded Electrical items Cleared by Electrical QC?	◉ YES ○ NO ○ NA	WIR Number	
Embedded Mechanical Items Cleared by Mechanical QC?	◉ YES ○ NO ○ NA	WIR Number	

Accepted:	◉
Accepted with Comments (See Remarks):	○
Rejected (See Remarks):	○

REMARKS:					
Name:	Naseem Ahmed	Signature:	Naseem Ahmed	Date:	17/10/26

QIDDIYA / SUPERVISION CONSULTANT QC INSPECTOR - FINAL INSPECTION FINDINGS:

Contractor Has complied with Project spec requirements?	◉ YES ○ NO	Okay to Proceed with next activity?	◉ YES ○ NO ○ NA

Accepted:	◉
Accepted with Comments (See Remarks):	✓
Rejected (See Remarks):	○

REMARKS:	final approval upon TSC completion				
Name:	Mahmoud	Signature:		Date	5/11/26

FOR DETAILED MATERIAL INSPECTION STATUS, PLEASE SEE ATTACHED CHECKLIST.
CHECKLISTS THAT ARE NOT ATTACHED AND SIGNED BY SUPERVISION CONSULTANT WILL VOID THIS INSPECTION REQUEST.

This document is the property of Qiddiya Development Company, 2022

Client:	Consultant:	Contractor:
Qiddiya	Zuhair Fayez Partnership	Hail Company / Freyssinet — HAIF-FREYSSINET JV

TECHNICAL DOCUMENTS

Project Name: Package 3 - Interim Road Access to Resort Core	**Project Code:** QRXM114000
Location: 00	**Date:** 14 -June-2026
Document Title: **Inspection & Test Plan for Intelligent Transportation System Works for ITS CABINET SYSTEM INSTALLATION AND OPERATION**	**Ref No:** QRXM114000-HFC-TEC-ITP-ITS-00007
	Rev No: 00

Department: ☐ Architectural ☐ Structural ☐ Electrical ☐ Mechanical ☐ Authority ☐ Civil ☒ Others

Type: ☐ Pre-Qualification ☐ Method Statement ☐ Material Submittal ☐ Sample ☒ ITP

Document Description: This is Inspection&Test Plan for Intelligent Transportation System Works for ITS CABINET SYSTEM INSTALLATION AND OPERATION

Doc. Ref. No.	Title
QRXM114000-HFC-TEC-ITP-ITS-00007	**Inspection&Test Plan for Intelligent Transportation System Works for ITS CABINET SYSTEM INSTALLATION AND OPERATION**

Enclosure:

Submitted By:	**Received By:**
Name: Eng. Moataz	Name:
Signature:	Signature:
Date: 14-June-2026	Date:

Below portion for Consultant Supervision use only

Status: ☐A- Approved ☐B- Approved as noted ☐C- Revise & Resubmit ☐R- For information only

Comments:







Below portion for Client use only

Comments:

Signed by: Signature: Date:

Checklist : HFC-CKL-1003	Checklist	APPROVED DATE	DISCIPLINE
INSTALLATION OF ITS CABINET	HFC-CKL-1003		ITS
PROJECT TITLE: Road Access To Resort Core (RA4RC)	WBS	CONTRACTOR/SUBCONTRACTOR	
WIR No.	CONSTRUCTION- Intelligent Transportation System Works for INSTALLATION AND OPERATION of ITS CABINET	HAIF	


ITEM NO.	Check Points & Acceptance Criteria	Reference	Pass	Fail	Not Applicable	Re-Inspection
1.0	**INSTALLATION OF TRAFFIC SURVEILLANCE (CCTV) SYSTEM-PTZ CAMERAS**					
1.1	During the design stage System integration tests (SIT) procedures shall be described to ensure the ITS equipment has been completed to the required functionality, safety and quality and meets all the contractual specifications the following points shall be included.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.5. System integration tests (SIT)	✓			
1.4	The SIT shall also incorporate the network-manageable portions of the ITS system. The SIT shall begin after the earlier stages of testing have been successfully completed (i.e. PAT and SAT) and accepted by the Competent Authority and Government Authorities. When possible, the SIT shall be conducted during the harshest environment period deemed for that particular equipment. The duration of the SIT will be agreed with the Competent Authority and Government Authorities prior to starting.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.5. System integration tests (SIT)	✓			
1.3	In the event of a system, subsystem, ITS equipment, or ancillary component failure, with the exception of consumable items such as fuses, the Project shall be shut down for purposes of testing and correcting identified deficiencies (System Shutdown). System Shutdown is defined as any condition which, due to work performed by the Contractor, results in the Project, or any system, subsystem, ITS equipment, or ancillary component thereof to cease operation.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.5. System integration tests (SIT)	✓			
1.4	The SIT shall be re-started after the identified deficiency has been corrected.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.5. System integration tests (SIT)	✓			
1.5	If the total number of System Shutdowns exceeds three (3) due to the same system or subsystem, ITS equipment, or ancillary component;	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.5. System integration tests (SIT)	✓			
1.6	The system, subsystem, ITS equipment, or ancillary component shall be removed and replaced with a new and unused unit.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.5. System integration tests (SIT)	✓			
1.7	All applicable PAT and SAT, as deemed necessary by the Competent Authority and Government Authorities shall be performed, and the SIT shall be restarted upon written approval from the Competent Authority and Government Authorities.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.5. System integration tests (SIT)	✓			
1.8	Time extensions shall not be granted to perform the SIT due to any failures. Failures during the SIT shall be rectified at no additional cost to the Competent Authority and Government Authorities.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.5. System integration tests (SIT)	✓			
1.9	Upon the successful completion of the SIT and all the required submittals, testing, training, and documentation have been successfully submitted to and approved by the Competent Authority and Government Authorities, the Competent Authority and Government Authorities shall provide written notice of Final Acceptance.	SHC 306 specification SECTION 7.5.3. Testing SUBSECTION 7.5.3.5. System integration tests (SIT)	✓			

Remarks

PM/Contractor				QDC			
Contractor Construction				Third Party (if applicable)			
The work is ready for inspection				Document Reviewed	Work Inspected	Test Records Verified	
Name	Signature		Date	Name	Signature		
Contractor QC Inspector			17/10/26	QDC Supervision Consultant			


Form Ref. No. QD0004-ADM-TEM-QTY-00003– Rev.0A

NOTE
MATERIAL SUBMITTAL REFERENCE NUMBER :
QRXM114000-HFC-TEC-MAT-ITS-02-RO5-00012

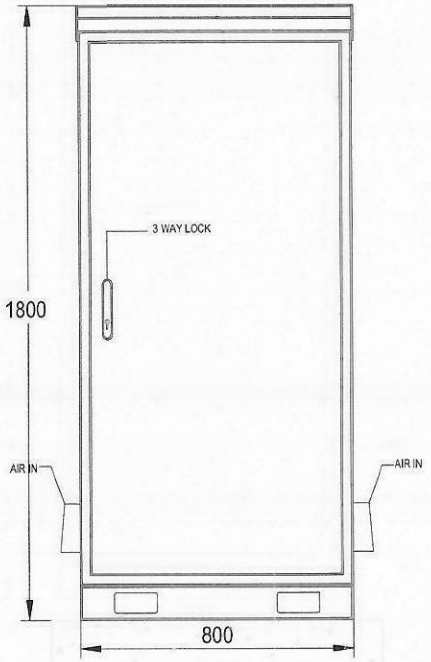


FOUNDATION

FRONT VIEW

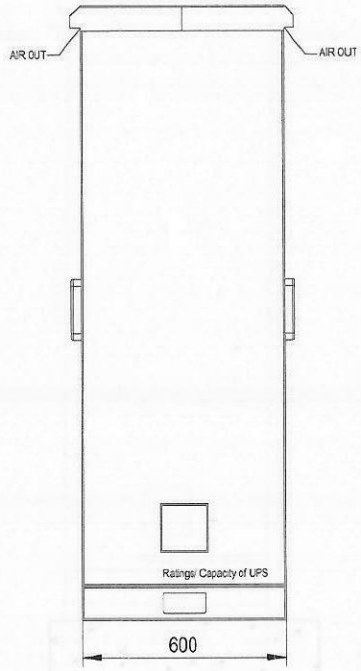


FOUNDATION

SIDE VIEW

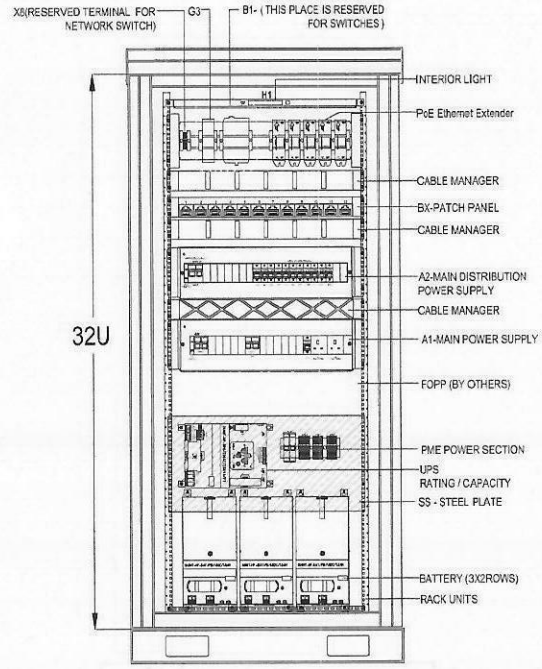

FOUNDATION

FRONT (INTERAL VIEW)

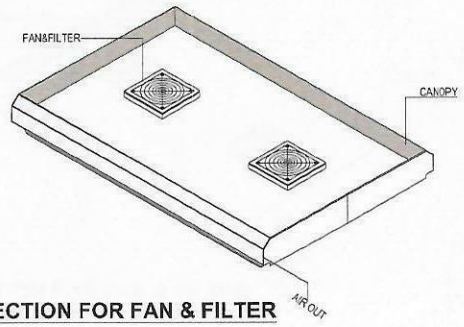

CROSS SECTION FOR FAN & FILTER

UPS & BATTERY CALLCULATIONS	
REQUIRED NO OF UPS	QTY 1 - (TEMP 60 °C) QUINT-HP-UPS/230AC/2.5KVA/PT
REQUIRED NO OF BATTERIES	QTY 6 - (TEMP 40 °C) QUINT-HP-BAT/PB/48DC/7.0AH/PT
BATTERY CAPACITY (AH) = LOAD (VA) X BACKUP TIME (H) X SAFETY FACTOR / (BATTERY VOLTAGE (V) X EFFICIENCY OF UPS) = (2300 x 0.5 x 1.6) / (48 x 0.95) = 40.35AH	

ITS CABINET

H = 1800mm x W = 800mm x D = 600mm

NOTE:
FOUNDATION DESIGN TO BE PROVIDED IN SEPARATE SUBMISSION

القدية
Qiddiya

Consultant's information
HEAD OFFICE - Riyadh
6283 King Abdul Aziz Rd, Ar Rabi
Riyadh 13316 2771, Saudi Arabia
Tel. +966 11 4048484
Fax : +966 11 4048400
Website : www.zfp.com
Email. : zfpr@zfp.com
Zuhair Fayez Partnership



Notes:
1. ALL DIMENSIONS ARE IN MILLIMETER UNLESS OTHERWISE STATED
2. ALL LEVELS ARE IN METERS UNLESS NOTED OTHERWISE
3. THIS DRAWINGS S TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTURAL, STRUCTURAL AND SERVICES DRAWINGS

REFERENCE I.F.C DESIGN DRAWING NO:
1. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-2000002
2. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000001
3. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000002
4. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000005
5. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-5000006
6. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-6000001
7. QRXP117115-DAH-VORA2R-DWG-ITS-R3-Z00000-8000003
8. QRXP117115-DAH-VORA2R-DWG-ICT-R3-Z00000-2000000
9. QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00077

Rev. No.	Date	Description	Appr.
00	04-11-2025	FOR REVIEW AND APPROVAL	C
01	28-12-2025	FOR REVIEW AND APPROVAL	B
02	04-02-2026	FINAL REVISION	
--	--	--	--
--	--	--	--
--	--	--	--
--	--	--	--

Consultant
Project
Contractor
Hail Company
ITS Contractor
TRAFFIC TECH
القدية Qiddiya

Job title: Road Access To Resort Core

Drawing title:
SHOPDRAWING OF TRAFFIC SIGNAL SYSTEM FOR JUNCTION-2
TYPICAL INTERNAL ARRANGEMENT OF ITS CABINET

Sheet number:
SHEET 16 / 19

Scale: NTS

Drawn: M.Elsayed | Checked: M.Abuzaid
Designed | Approved

Drawing number: QRXM114000-HFC-DRW-SDW-ITS-02-RO5-00063
Revision: 02


ITS Cabinet Assemblies for installation of Traffic CCTV Systems



Mounting Brackets




Cable Arrangements

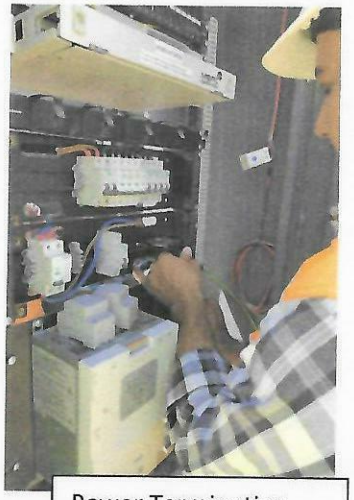


Power Termination



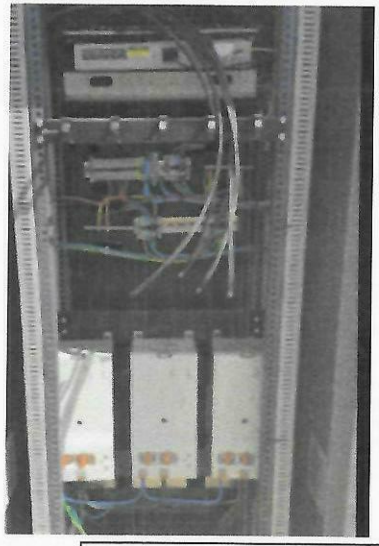

Power - UPS Batter Termination Completed

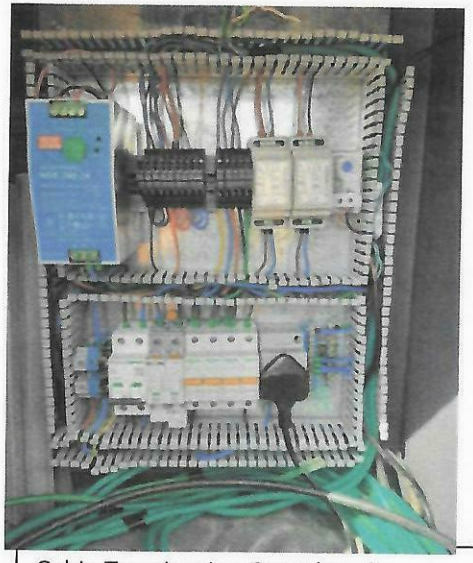

Cabin Termination Completed .

[Cabinet Assemblies Power ,Connectors ,Cabling, Connections]
